



Government of India
Ministry of Statistics and
Programme Implementation



OCMS

Ministry of Statistics & Programme Implementation



466th

Flash Report on Central Sector Infrastructure Projects

(Rs. 150 crore
& above)

(Part - I)*

Synopsis

August 2024

*Refer Part-II for tables comprising detailed project listing.



www.mospi.gov.in



[@GoIStats](https://www.mospi.gov.in)

[/GoIStats](https://www.mospi.gov.in)

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects
(1783, Rs. 27,38,539.25 crore)

Mega*
(620 projects,
Rs. 22,21,461.55
crore)

Major*
(1163 projects,
Rs. 5,17,077.70
crore)

Completed@
projects during
August 2024
(16 projects,
Rs. 12772.92
crore)








**Newly Added/
elevated\$**
Projects during
August 2024
(16 projects,
Rs. 15663.95
crore)

Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
other Indicated legends are in format (Project count, Original Cost)


* Mega Project if having original cost $\geq$ Rs. 1000 crore

* Major Project if original cost < Rs. 1000 crore

\$ reported Anticipated cost more than Rs. 150 crore

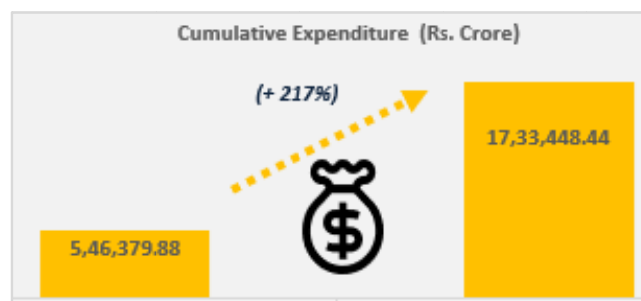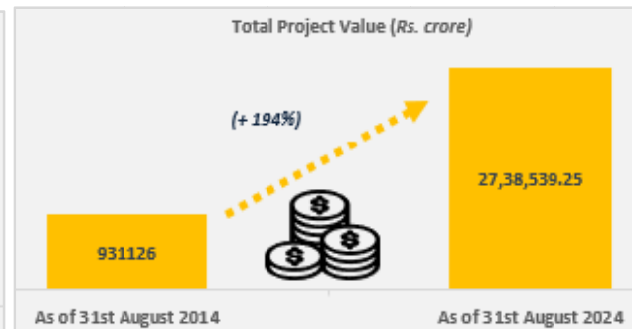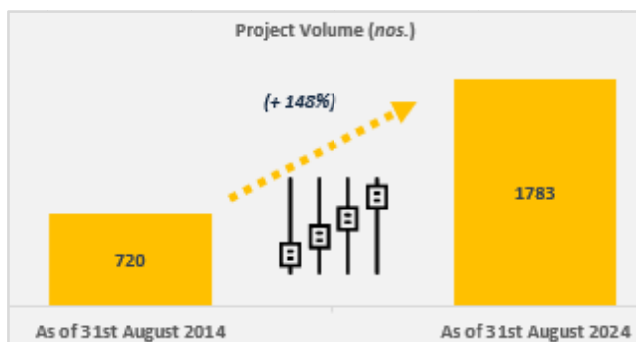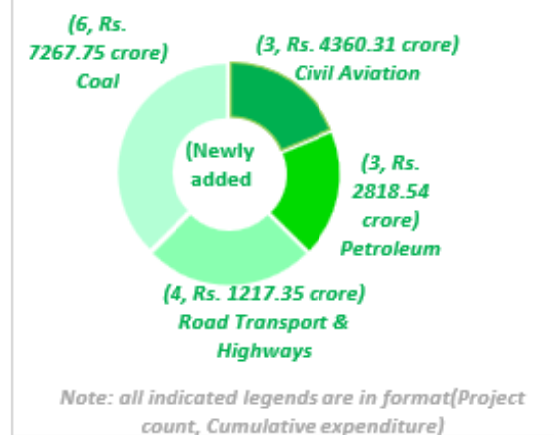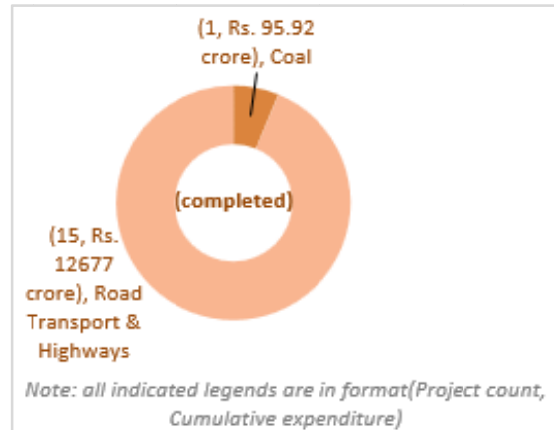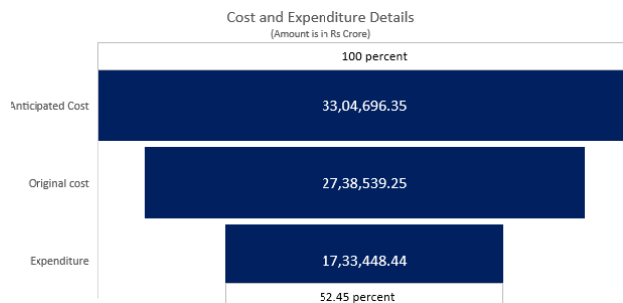


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

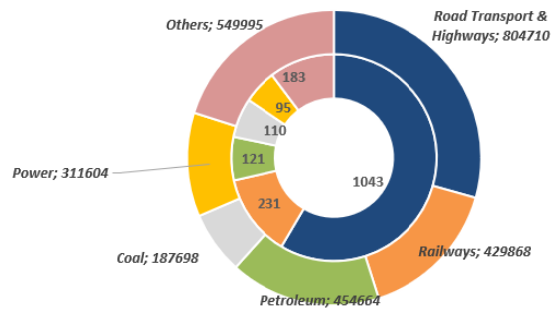


*Others include Water Resources, Civil Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

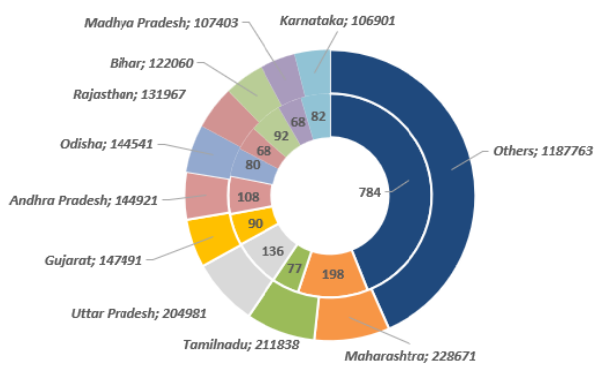

*Others include Jharkhand, Delhi, Chhattisgarh, Haryana, Jammu & Kashmir, West Bengal, Kerala, Assam, Arunachal Pradesh, Punjab, Telangana, Uttarakhand, Himachal Pradesh, Manipur, Sikkim, Nagaland, Mizoram, Meghalaya, Tripura, Goa, A&N

Sectoral Distribution of total 641 projects with reported Physical Progress between 80-100%

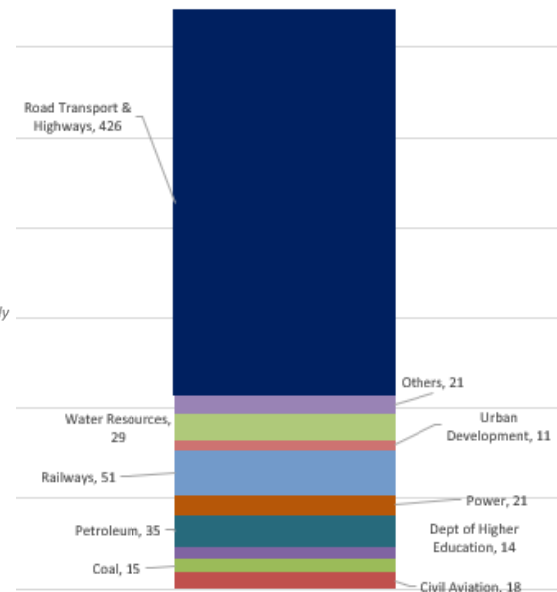

Note: This report is as of August 2024, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/ implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th September 2024



Government of India
Ministry of Statistics and
Programme Implementation



OCMS

Ministry of Statistics & Programme Implementation



466th

Flash Report on Central Sector Infrastructure Projects

(Rs. 150 crore
& above)

(Part - II)*

List of Tables

August 2024

CONTENTS

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	1-2
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	3-5
Table:-3. Project List: Completed during August 2024.....	6-8
Table:-4. Project List: Added during August 2024.....	9-10
Table:-5. Project List: Frozen/Deleted during August 2024.....	11-12
Table:-6. Project List: Ongoing Projects of North-East Region.....	13-36
Table:-7. Project List: Ongoing Projects as of 31 st August 2024.....	37-238

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ATOMIC ENERGY	5	116,741.00 (167,447.00) {171,625.00}	109,458.72
2	CIVIL AVIATION	40	26,490.58 (27,450.90) {30,517.47}	15,445.76
3	COAL	110	187,698.23 (189,867.45) {192,440.13}	70,950.19
4	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,380.58) {10,338.99}	7,144.86
5	DONER	1	151.33 (151.33) {151.33}	148.33
6	DPIIT	2	24,857.00 (24,857.00) {25,485.00}	14,507.26
7	FINANCE	2	577.27 (577.27) {569.04}	399.67
8	HEALTH AND FAMILY WELFARE	9	7,561.27 (7,730.18) {7,727.97}	4,369.45
9	HOME AFFAIRS	5	2,025.73 (2,946.02) {2,946.00}	2,330.04
10	MINES	8	7,559.78 (9,175.81) {9,833.57}	5,164.97
11	PETROLEUM	121	454,664.33 (509,473.18) {524,427.44}	241,963.77
12	POWER	95	311,603.56 (330,572.03) {374,603.92}	195,066.63
13	RAILWAYS	231	429,868.26 (544,743.99) {673,705.21}	414,029.87
14	ROAD TRANSPORT AND HIGHWAYS	1043	804,710.14 (838,463.05) {853,774.04}	404,761.18
15	SHIPPING AND PORTS	1	5,369.18 (4,633.81) {5,061.15}	3,059.64

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80
17	STEEL	12	11,337.99 (11,963.86) {11,963.86}	5,560.17
18	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	3,916.61
19	URBAN DEVELOPMENT	30	287,043.72 (294,057.08) {312,556.91}	205,671.45
20	WATER RESOURCES	41	23,466.28 (23,420.50) {69,848.44}	29,426.07
	Total	1783	2,738,539.25 (3,025,031.92) {3,304,696.35}	1,733,448.44

*Either Revised or Original Cost

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	9	2,847.18 (3,137.68) {3,118.54}	1,999.74
2	ANDHRA PRADESH	108	144,921.32 (150,665.61) {208,419.75}	115,864.22
3	ARUNACHAL PRADESH	24	47,923.74 (47,987.27) {63,009.42}	30,062.53
4	ASSAM	64	64,614.34 (64,805.81) {74,346.77}	40,480.27
5	BIHAR	92	122,059.55 (142,870.31) {150,868.24}	95,110.22
6	CHHATTISGARH	56	83,089.13 (85,307.08) {85,844.92}	35,657.65
7	DELHI	27	92,995.74 (98,711.59) {97,290.55}	73,509.87
8	GOA	6	3,824.63 (3,911.13) {3,911.13}	3,096.66
9	GUJARAT	90	147,491.26 (162,914.21) {168,958.42}	87,226.82
10	HARYANA	33	74,759.15 (84,837.00) {85,586.95}	35,581.57
11	HIMACHAL PRADESH	29	27,418.92 (28,706.60) {43,060.58}	28,233.38
12	JAMMU AND KASHMIR	51	74,532.19 (110,182.74) {114,800.04}	70,809.38
13	JHARKHAND	65	104,141.01 (108,165.43) {111,846.85}	55,804.56
14	KARNATAKA	82	106,901.32 (110,223.78) {112,461.91}	51,715.20
15	KERALA	34	70,127.95 (77,205.09) {77,564.85}	37,181.30

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	944.34
17	MADHYA PRADESH	68	107,403.05 (112,213.37) {121,838.95}	42,587.17
18	MAHARASHTRA	198	228,670.96 (233,816.06) {255,595.75}	129,761.41
19	MANIPUR	33	15,536.95 (23,393.01) {30,600.48}	18,728.90
20	MEGHALAYA	14	5,372.73 (5,659.62) {12,735.93}	3,061.41
21	MIZORAM	21	11,852.41 (16,957.12) {20,444.86}	16,632.77
22	MULTI STATE	58	286,178.20 (330,168.94) {352,132.26}	219,772.80
23	NAGALAND	34	12,315.74 (18,004.99) {17,703.96}	7,933.15
24	ODISHA	80	144,541.42 (148,315.63) {155,562.16}	61,182.76
25	PUNJAB	43	41,821.35 (41,909.94) {41,998.18}	15,944.03
26	RAJASTHAN	68	131,967.33 (172,222.01) {172,429.95}	98,846.55
27	SIKKIM	22	14,500.36 (14,896.52) {22,320.65}	12,146.80
28	TAMIL NADU	77	211,838.43 (247,767.35) {267,494.94}	124,435.94
29	TELANGANA	53	38,381.66 (38,840.81) {41,226.16}	23,378.07
30	TRIPURA	10	5,071.09 (5,193.46) {5,332.56}	1,390.69

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
31	UTTAR PRADESH	136	204,981.45 (211,135.81) {225,790.21}	101,454.32
32	UTTARAKHAND	31	36,349.58 (41,573.69) {58,559.70}	42,464.80
33	WEST BENGAL	61	71,634.14 (80,857.29) {99,206.09}	50,449.16
	Total	1783	2,738,539.25 (3,025,031.92) {3,304,696.35}	1,733,448.44

*Either Revised or Original Cost

Table:-3. Project List: Completed during August 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
<u>COAL</u>					
	1	KARMA OCP (1.0MTY) (CCL) (N06000088) (JHARKHAND)	162.46	03/2014	95.92
<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	2	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR (NHAI) (N24000549) (UTTAR PRADESH)	1,396.74	10/2019	3,986.50
	3	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN (NHAI) (N24000662) (PUNJAB)	754.54	03/2020	800.29
	4	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV (NHAI) (N24000691) (RAJASTHAN)	894.00	04/2020	1,082.77
	5	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH- 112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO (NHAI) (N24000711) (RAJASTHAN)	1,308.73	12/2020	1,308.73
	6	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI- ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. (NHIDCL) (N24000944) (ARUNACHAL PRADESH)	200.44	01/2020	161.25
	7	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 (NHAI) (N24001300) (ANDHRA PRADESH)	1,226.88	02/2021	1,438.66

Table:-3. Project List: Completed during August 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	8	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 (NHIDCL) (N24001333) (ASSAM)	761.54	05/2023	430.31
	9	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. (MoRTH) (N24001409) (RAJASTHAN)	319.09	03/2024	138.67
	10	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. (MoRTH) (N24001412) (RAJASTHAN)	339.65	10/2023	207.23
	11	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDA-SAGWARA) SECTION OF NH-927A. PKG- (MoRTH) (N24001413) (RAJASTHAN)	240.99	01/2024	233.39
	12	CONSTRUCTION OF 4 LANE ELEVATED VIADUCT AT KM. 7.500 MUNSHI PULIA OF NH-24A (MoRTH) (N24001460) (UTTAR PRADESH)	170.60	09/2024	153.26
	13	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF BARMER GHAGARIYA SECTION FROM KM 0 (MoRTH) (N24001531) (RAJASTHAN)	304.87	08/2024	289.31
	14	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-2) (NHAI) (N24001560) (RAJASTHAN)	755.16	10/2023	755.16

Table:-3. Project List: Completed during August 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	15	SANGARIYA (NEAR CHAUTALA)-RASISAR (NEAR BIKANER) (PHASE-I) (AJ/SR-PACKAGE-1) (NHAI) (N24001562) (RAJASTHAN)	738.90	10/2023	738.90
	16	DELHI-VADODARA GREENFIELD ALIGNMENT (NH- 148N) (PKG-16) (CH. 427.300 TO CH.452.420) [MAJOR BRIDGE OVE (NHAI) (N24001572) (RAJASTHAN)	952.57	01/2023	952.57
		Total	10,527.16		12,772.92

Table:-4. Project List: Added during August 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
CIVIL AVIATION	1	DARBHANGA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH-CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112) (BIHAR)	7/2024	911.66 (N.A.) {911.66}	7/2026 (N.A.) {7/2026}
	2	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113) (UTTAR PRADESH)	6/2024	579.00 (N.A.) {579.00}	7/2026 (N.A.) {7/2026}
	3	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114) (UTTAR PRADESH)	7/2024	2,869.65 (N.A.) {2,869.65}	7/2027 (N.A.) {7/2027}
COAL	4	ITAPARA OC (ECL) (N06000272) (WEST BENGAL)	12/2023	929.10 (N.A.) {929.10}	3/2030 (N.A.) {3/2030}
	5	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273) (JHARKHAND)	1/2023	4,011.85 (N.A.) {4,011.85}	3/2030 (N.A.) {3/2030}
	6	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274) (CHHATTISGARH)	1/2023	329.22 (N.A.) {329.22}	3/2029 (N.A.) {3/2029}
	7	HURA C OC (ECL) (N06000275) (JHARKHAND)	8/2022	859.41 (N.A.) {859.41}	3/2029 (N.A.) {3/2029}
	8	UCE OF TILABONI UG (ECL) (N06000276) (WEST BENGAL)	1/2023	749.07 (N.A.) {749.07}	3/2029 (N.A.) {3/2029}
	9	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277) (WEST BENGAL)	1/2023	389.10 (N.A.) {389.10}	3/2029 (N.A.) {3/2029}
	10	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532) (ASSAM)	9/2023	198.70 (N.A.) {198.70}	5/2026 (N.A.) {5/2026}

Table:-4. Project List: Added during August 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>PETROLEUM</u>	11	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533) (MAHARASHTRA)	6/2024	2,379.84 (N.A.) {2,379.84}	5/2026 (N.A.) {5/2026}
	12	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534) (MAHARASHTRA)	6/2024	240.00 (N.A.) {240.00}	4/2026 (N.A.) {4/2026}
<u>ROAD TRANSPORT AND HIGHWAYS</u>	13	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150) (UTTAR PRADESH)	12/2022	515.69 (N.A.) {515.69}	2/2026 (N.A.) {2/2026}
	14	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151) (TAMIL NADU)	3/2022	257.14 (295.00) {295.00}	1/2024 (N.A.) {7/2025}
	15	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152) (TAMIL NADU)	3/2023	274.84 (N.A.) {274.84}	11/2023 (N.A.) {11/2025}
	16	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153) (TAMIL NADU)	3/2023	169.68 (N.A.) {169.68}	2/2024 (N.A.) {8/2025}
<u>Grand Total</u>				15,663.95 (-) {15,701.81}	

**Table:-5. Project List: Frozen / Deleted during August
2024**

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
COAL						
	1	AMRITDHARA OC PROJECT (SECL) (N06000122) (MADHYA PRADESH)	481.60	03/2023	0.00	15
	2	RAJNAGAR OCP RPR (1.70 MTY) (SECL) (N06000124) (MADHYA PRADESH)	357.80	03/2021	81.25	41
	3	BATURA HIGHWALL PROJECT (SECL) (N06000134) (MADHYA PRADESH)	231.92	03/2022	2.75	23
	4	DURGAPUR OPENCAST PROJECT (SECL) (N06000136) (CHHATTISGARH)	916.24	03/2023	19.54	18
	5	VIJAY WEST OPENCAST PROJECT (SECL) (N06000158) (CHHATTISGARH)	976.95	03/2026	0.00	4
	6	TILABONI UG MINE (ECL) (N06000172) (WEST BENGAL)	916.62	03/2027	12.79	10.1
	7	PARASEA- BELBAID REORGANISATION UG MINE (ECL) (N06000185) (WEST BENGAL)	826.42	03/2027	4.47	14
	8	BATURA WEST OC PROJECT (0.80 MTY) (SECL) (N06000207) (MADHYA PRADESH)	496.28	03/2028	0.00	2
	9	KARTALI (EAST) OCP (2.50 MTY) (SECL) (N06000076) (CHHATTISGARH)	178.44	03/2014	15.92	18
	10	MADANNAGAR OPENCAST PROJECT (SECL) (N06000140) (CHHATTISGARH)	1,875.32	03/2024	0.00	5

Table:-5. Project List: Frozen / Deleted during August 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore	Progress (%)
	11	HURA - C OC (3 MTY) (ECL) (N06000143) (JHARKHAND)	359.69	03/2022	330.22	52
TELECOMMUNICATIONS						
	12	NETWORK FOR SPECTRUM (DOT) (N26000101) (MULTI STATE)	13,334.00	07/2015	22,626.69	0
		Total	20,951.28		23,093.63	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2/2019	8/2022 (Dec-24) {12/2024}	645.63 (N.A.) {712.15}	663.45	98.01
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (180100221)	9/2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {21,247.54}	21,833.13	93.72
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2/2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,499.11	12.56
	ROAD TRANSPORT AND HIGHWAYS	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2/2017	11/2023 (Mar-24) {11/2024}	180.57 (244.10) {180.57}	154.17	90.01
		5	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2/2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	144.91	100
		6	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3/2017	3/2022 (Dec-23) {7/2025}	1,718.59 (1,718.59) {1,718.59}	674.32	68.62
		7	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9/2016	12/2019 (Mar-23) {9/2024}	568.92 (568.92) {568.92}	508.65	99.79
		8	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1/2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		9	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA- KHUPA-HAYULIANG SECTION OF NH- 113 FROM CH.68. (NHIDCL) (N24001244)	8/2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	136.35	58.77

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		10	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE- BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9/2020	5/2022 (Oct-22) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3/2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3/2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	568.30	98.99
		13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3/2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	474.23	97.71
		14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3/2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	371.45	91.27
		15	TADADEGE - HENKAR (NHIDCL) (N24001315)	2/2021	3/2023 (Jun-24) {9/2024}	550.45 (N.A.) {550.45}	113.92	44.05
		16	LADDA - BASAI (NHIDCL) (N24001316)	2/2021	4/2023 (Jan-25) {3/2025}	445.96 (N.A.) {445.96}	113.54	47.79
		17	DOGINALA - GAU (NHIDCL) (N24001320)	12/2020	9/2022 (N.A.) {12/2024}	242.30 (N.A.) {242.30}	21.47	17.81
		18	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH- 215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2/2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	449.73	89.08
		19	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6/2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	355.51	96.7

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		20	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6/2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	132.31	34.2
		21	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8/2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	97.23	97.03
		22	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8/2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	144.61	98.29
		23	JORAM ? KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) (NHIDCL) (N24001392)	8/2020	4/2022 (Jul-23) {7/2023}	199.03 (N.A.) {199.03}	102.85	100
		24	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8/2020	4/2022 (Feb-24) {11/2024}	184.88 (N.A.) {184.88}	95.64	93.83
ASSAM	CIVIL AVIATION	25	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12/2016	3/2021 (N.A.) {3/2025}	1,142.00 (N.A.) {2,333.00}	1,290.94	63.48
	HEALTH AND FAMILY WELFARE	26	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5/2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	757.66	98.87
	PETROLEUM	27	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9/2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	0.00	
		28	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3/2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	18.59	68
		29	DCU REVAMP PROJECT (NRL) (N16000511)	8/2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	140.35	33.4
		30	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1/2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	108.35	31

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		31	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1/2018	2/2020 (Dec-23) {12/2024}	543.91 (N.A.) {670.90}	491.56	93.7
		32	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1/2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	12,027.15	62.27
		33	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1/2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,037.54	76.2
		34	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5/2021	10/2023 (Feb-25) {2/2025}	412.00 (509.84) {509.84}	350.40	76.8
		35	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON (ONGC) (N16000433)	8/2021	2/2023 (Jun-24) {8/2024}	218.38 (N.A.) {218.38}	172.05	82.8
		36	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3/2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	156.03	48.8
		37	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6/2021	12/2024 (N.A.) {12/2024}	860.00 (N.A.) {860.00}	300.10	84.4
		38	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12/2020	7/2024 (Mar-24) {12/2024}	430.76 (N.A.) {430.76}	244.08	71.37
		39	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6/2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	57.60	18.5

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		40	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3/2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	1.08	11
		41	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3/2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	30.05	2.7
	RAILWAYS	42	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4/2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,424.50	91
	ROAD TRANSPORT AND HIGHWAYS	43	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3/2020	6/2022 (N.A.) {5/2025}	261.13 (N.A.) {261.13}	64.96	54.59
		44	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3/2020	6/2022 (May-24) {4/2025}	217.50 (N.A.) {217.50}	84.36	64.15
		45	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11/2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	1,998.70	50.74
		46	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3/2021	1/2023 (N.A.) {9/2024}	288.85 (N.A.) {288.85}	221.38	91.24
		47	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3/2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	78.65	27.93
		48	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3/2020	12/2022 (N.A.) {8/2024}	220.20 (N.A.) {220.20}	215.69	97.76
		49	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8/2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	186.61	100
		50	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6/2015	8/2023 (N.A.) {12/2024}	437.39 (N.A.) {437.39}	307.45	20.58

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		51	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6/2015	3/2024 (N.A.) {7/2024}	463.49 (N.A.) {463.49}	368.12	31.56
		52	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1/1991	6/2019 (Jun-19) {10/2024}	520.01 (N.A.) {520.01}	297.99	90.01
		53	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12/2015	12/2018 (Jul-21) {10/2024}	289.99 (N.A.) {289.99}	232.56	87.62
		54	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1/2016	1/2016 (N.A.) {12/2024}	294.17 (N.A.) {294.17}	295.84	38.88
		55	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1/2016	12/2021 (N.A.) {12/2021}	252.00 (N.A.) {330.30}	146.28	
		56	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3/2020	3/2022 (Dec-23) {12/2024}	216.49 (241.52) {216.49}	104.36	79.48
		57	FOUR LANING OF BALACHERA- HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE (NHIDCL) (N24000902)	10/2017	6/2020 (Dec-23) {4/2024}	818.00 (887.68) {887.68}	873.61	100
		58	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3/2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	266.61	32.97

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		59	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3/2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	267.62	30.96
		60	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3/2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	326.53	28.21
		61	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3/2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	172.88	49.02
		62	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3/2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	154.32	46.99
		63	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3/2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	329.25	20.83
		64	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3/2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	198.83	9.09
		65	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3/2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	254.13	9.86
		66	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1/2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	133.24	37.69
		67	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1/2023	12/2025 (N.A.) {12/2025}	356.65 (N.A.) {356.65}	113.59	3.88

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		68	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3/2023	12/2025 (N.A.) {12/2025}	643.42 (N.A.) {643.42}	64.67	8.25
		69	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2/2020	3/2022 (N.A.) {10/2024}	592.06 (N.A.) {592.06}	291.85	93.87
		70	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2/2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	306.95	11.04
		71	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3/2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	703.59	25.1
		72	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2/2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	172.77	18.3
		73	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12/2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	268.54	27.77
		74	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2/2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	321.15	30.59
		75	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12/2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100
		76	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8/2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	291.19	57.1
		77	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9/2021	7/2024 (N.A.) {12/2024}	625.64 (N.A.) {625.64}	455.08	77.77

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		78	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3/2022	7/2024 (N.A.) {8/2024}	215.27 (N.A.) {215.27}	144.52	95.8
		79	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 (NHIDCL) (N24001452)	4/2022	7/2024 (N.A.) {8/2024}	170.95 (N.A.) {170.95}	123.89	98.85
		80	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11/2021	7/2024 (N.A.) {10/2024}	204.10 (N.A.) {204.10}	119.11	77.91
		81	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 (NHIDCL) (N24001544)	3/2022	1/2025 (N.A.) {1/2025}	909.02 (N.A.) {909.02}	388.98	74.54
		82	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8/2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	178.56	98.13
		83	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3/2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	394.71	44.49
		84	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3/2022	6/2024 (N.A.) {12/2024}	457.72 (N.A.) {457.72}	235.64	85
		85	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH (NHAI) (N24001549)	7/2017	4/2020 (Jul-24) {7/2024}	442.23 (N.A.) {442.23}	265.19	100
		86	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3/2022	2/2025 (N.A.) {12/2025}	613.89 (N.A.) {613.89}	17.09	9.23
		87	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1/2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	133.51	37.45

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		88	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3/2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	4.07	10.6
MANIPUR	CIVIL AVIATION	89	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11/2021	7/2024 (Dec-25) {12/2025}	499.00 (N.A.) {499.00}	104.76	32.88
	RAILWAYS	90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4/2003	3/2011 (Mar-28) {12/2026}	4,454.17 (12,274.06) {19,517.70}	14,707.39	79.3
	ROAD TRANSPORT AND HIGHWAYS	91	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12/2021	5/2024 (N.A.) {10/2025}	410.68 (N.A.) {410.68}	105.71	50.78
		92	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12/2021	2/2025 (N.A.) {11/2025}	504.76 (N.A.) {504.76}	95.59	43.38
		93	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3/2022	2/2025 (N.A.) {2/2025}	152.11 (N.A.) {152.11}	51.41	70.28
		94	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8/2021	12/2023 (N.A.) {12/2025}	579.63 (N.A.) {579.63}	131.58	52.16
		95	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8/2021	5/2023 (Dec-23) {2/2025}	477.86 (N.A.) {477.86}	235.67	80.3
		96	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9/2021	5/2023 (Oct-23) {4/2025}	311.18 (N.A.) {311.18}	171.57	72.7
		97	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8/2021	5/2023 (N.A.) {10/2024}	467.41 (N.A.) {467.41}	243.19	91.69
		98	IMPHAL ? MOREH (PACKAGE 4) (NHIDCL) (N24001399)	3/2021	1/2023 (N.A.) {4/2024}	277.99 (N.A.) {277.99}	146.35	100
		99	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3/2021	1/2023 (N.A.) {8/2025}	211.70 (N.A.) {211.70}	29.00	31.88
		100	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7/2021	3/2023 (Feb-24) {3/2025}	467.00 (N.A.) {467.00}	181.65	75.23

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		101	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7/2021	3/2023 (Oct-23) {1/2025}	185.80 (N.A.) {185.80}	112.31	92.65
		102	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7/2021	3/2023 (May-24) {2/2025}	483.87 (N.A.) {483.87}	278.89	91.03
		103	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7/2021	3/2023 (Sep-23) {2/2025}	198.77 (N.A.) {198.77}	110.09	85.12
		104	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7/2021	10/2023 (Feb-24) {6/2025}	673.27 (N.A.) {673.27}	348.20	72.4
		105	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3/2023	2/2026 (N.A.) {3/2026}	578.98 (N.A.) {578.98}	48.64	26.1
		106	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9/2021	1/2025 (N.A.) {1/2025}	315.56 (N.A.) {315.56}	60.63	43.9
		107	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1/2023	12/2025 (N.A.) {3/2026}	760.16 (N.A.) {760.16}	63.80	27.18
		108	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9/2021	2/2024 (N.A.) {4/2025}	310.76 (N.A.) {310.76}	116.81	75.99
		109	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3/2020	6/2022 (Dec-23) {12/2024}	292.24 (N.A.) {292.24}	127.86	85.33
		110	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6/2020	8/2022 (N.A.) {12/2024}	365.53 (N.A.) {365.53}	156.31	77.36
		111	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3/2020	6/2022 (N.A.) {12/2024}	167.95 (204.12) {167.95}	88.05	69.89
		112	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7/2020	8/2022 (N.A.) {12/2024}	177.76 (N.A.) {177.76}	89.67	80.53

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		113	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8/2020	4/2022 (N.A.) {8/2025}	379.39 (N.A.) {379.39}	189.78	45.88
		114	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO (NHIDCL) (N24001275)	8/2020	4/2022 (N.A.) {12/2025}	268.98 (N.A.) {268.98}	22.08	
		115	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8/2020	4/2022 (N.A.) {12/2025}	228.97 (N.A.) {228.97}	0.00	
		116	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2/2021	12/2022 (N.A.) {2/2025}	226.32 (N.A.) {226.32}	85.91	63.1
		117	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2/2021	12/2022 (N.A.) {9/2024}	188.36 (N.A.) {188.36}	124.69	94.92
		118	MARIAM - PEREN PKG-2B (NHIDCL) (N24001351)	2/2021	12/2022 (N.A.) {3/2024}	232.26 (N.A.) {232.26}	156.93	100
		119	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3/2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100
		120	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3/2021	12/2022 (Nov-23) {6/2025}	195.14 (N.A.) {195.14}	59.99	50.01
		121	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3/2021	12/2022 (N.A.) {1/2025}	234.08 (N.A.) {234.08}	139.45	90.34
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	122	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9/2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	272.05	72
	DONER	123	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4/2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	98.5

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	124	NEW BG LINE FROM BYRNIHAT TO SHILLONG (NFR) (N22000205)	4/2010	3/2021 (N.A.) {3/2021}	906.46 (1,202.33) {8,324.28}	269.80	2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	125	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3/2021	12/2022 (Jun-24) {11/2024}	260.21 (N.A.) {260.21}	201.39	86.38
		126	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11/2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	191.35	3
		127	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11/2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	45.46	0.3
		128	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM ((NHIDCL) (N24001313)	11/2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	216.11	20
		129	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11/2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	375.55	10.4
		130	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10/2020	4/2022 (Jun-24) {12/2024}	157.86 (146.92) {157.86}	146.19	97.49
		131	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM (NHIDCL) (N24000903)	3/2019	3/2022 (Dec-23) {12/2023}	306.28 (N.A.) {306.28}	233.49	100
		132	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4/2017	9/2021 (Jul-23) {3/2025}	553.51 (610.09) {553.51}	340.07	66.61

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MIZORAM		133	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9/2021	5/2024 (N.A.) {1/2025}	359.86 (N.A.) {359.86}	215.22	78
		134	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8/2020	2/2022 (Oct-24) {10/2024}	302.88 (N.A.) {302.88}	209.63	93
		135	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11/2021	6/2024 (N.A.) {12/2024}	283.50 (N.A.) {283.50}	196.77	70.19
	RAILWAYS	136	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4/2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,466.67	93
	ROAD TRANSPORT AND HIGHWAYS	137	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9/2021	5/2023 (Jun-24) {1/2025}	492.94 (492.94) {492.94}	355.00	84.44
		138	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRAUNG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9/2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	216.98	37
		139	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12/2021	2/2025 (N.A.) {5/2026}	500.88 (N.A.) {500.88}	122.78	31
		140	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4/2017	4/2023 (Mar-24) {11/2024}	519.09 (785.65) {785.65}	649.83	90
		141	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4/2017	7/2023 (May-24) {7/2024}	640.07 (990.88) {1,286.35}	1,198.44	99

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		142	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4/2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.79	99.5
		143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4/2017	4/2023 (Nov-23) {12/2024}	473.18 (688.25) {688.25}	514.74	83.66
		144	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4/2017	4/2023 (Oct-23) {12/2024}	537.82 (789.05) {789.05}	746.15	91.3
		145	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4/2017	6/2023 (Feb-24) {12/2024}	518.53 (906.76) {906.76}	784.80	88.32
		146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4/2017	4/2024 (Jul-24) {12/2024}	404.29 (750.32) {750.32}	584.01	83
		147	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4/2017	9/2023 (May-24) {12/2024}	428.11 (746.39) {746.39}	579.70	87
		148	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3/2020	7/2022 (Mar-24) {11/2024}	292.24 (331.17) {331.17}	287.95	91.42

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		149	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING- DULTE SECTION OF NH-06 (PKG-IV) (NHIDCL) (N24001283)	3/2020	7/2022 (Jan-24) {1/2024}	281.78 (253.41) {253.41}	237.91	100
		150	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9/2020	10/2022 (Apr-24) {6/2024}	275.02 (247.25) {247.25}	231.19	99.73
		151	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING- DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3/2020	7/2022 (Jan-24) {6/2024}	206.88 (219.33) {219.33}	206.55	97.01
		152	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3/2021	12/2022 (Mar-24) {3/2024}	374.39 (374.39) {374.39}	292.27	100
		153	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3/2021	12/2022 (Apr-24) {4/2024}	233.25 (233.25) {233.25}	178.37	100
		154	DULTE- KWALKULH - CHAMPAI PKG.3 (NHIDCL) (N24001357)	3/2021	6/2023 (Jan-24) {1/2024}	674.71 (674.71) {674.71}	589.25	100
		155	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3/2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	383.62	42.2
		156	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3/2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	276.77	41.5
NAGALAND	PETROLEUM	157	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8/2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	0.20	2.1
	RAILWAYS	158	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4/2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	3,690.86	53
	ROAD TRANSPORT AND HIGHWAYS	159	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3/2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		160	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) (NHIDCL) (N24001280)	3/2020	6/2022 (Mar-23) {9/2023}	320.97 (N.A.) {320.97}	182.21	100

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		161	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) (NHIDCL) (N24001284)	3/2020	6/2022 (Jun-23) {6/2024}	361.53 (365.42) {365.42}	197.64	97.12
		162	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3/2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		163	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4/2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	110.22	55.19
		164	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8/2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	39.59	1.34
		165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3/2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	58.37
		166	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3/2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		167	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3/2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
		168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9/2020	10/2022 (Apr-24) {9/2024}	277.44 (N.A.) {277.44}	160.86	62.16
		169	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8/2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	76.69	15.6

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		170	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8/2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	71.92	26.96
		171	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9/2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		172	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3/2016	9/2019 (Nov-22) {12/2024}	373.07 (534.41) {534.41}	382.50	99.81
		173	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3/2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	283.07	82.64
		174	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2/2017	9/2020 (Feb-23) {12/2024}	387.00 (688.12) {688.12}	387.50	99.32
		175	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3/2018	11/2022 (Aug-24) {12/2024}	500.09 (698.81) {698.81}	373.62	94.43
		176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA- ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3/2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	174.28	99.9
		177	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG- TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3/2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	104.37	23.61

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		178	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG- TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3/2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	81.60	16.03
		179	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12/2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	28.75	17.83
		180	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE- II (DESIGN C (NHIDCL) (N24001977)	12/2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	10.57
		181	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE- III (DESIGN (NHIDCL) (N24001978)	12/2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	55.97	25.78
		182	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3/2022	12/2024 (N.A.) {12/2024}	605.36 (N.A.) {605.36}	214.50	78.62
		183	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7/2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	43.05	23.33
		184	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7/2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	62.78	56.14
		185	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2/2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	0.00	
		186	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6/2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		187	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N) (MoRTH) (N24001466)	3/2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	109.40	55.07
		188	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3/2021	2/2024 (Feb-25) {2/2025}	226.44 (N.A.) {226.44}	109.16	76.78
		189	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2/2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	55.72	53.23
		190	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2/2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	12.83	20.02
SIKKIM	CIVIL AVIATION	191	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11/2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	6.01	3
	DEPARTMENT OF HIGHER EDUCATION	192	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8/2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	135.81	45
	POWER	193	TEESTA VI HE PROJECT (NHPC) (N18000325)	3/2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,671.26	63.26
		194	RANGIT IV HE PROJECT (NHPC) (N18000326)	3/2021	5/2024 (N.A.) {5/2025}	938.29 (N.A.) {1,871.23}	1,216.54	78.54
	RAILWAYS	195	SEVOK RANGPO, NEFR (NFR) (N22000102)	4/2008	12/2015 (N.A.) {12/2023}	1,339.48 (N.A.) {7,876.92}	3,290.96	39.8
	ROAD TRANSPORT AND HIGHWAYS	196	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3/2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	0.00	71.74

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		197	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10/2021	5/2024 (Jan-25) {1/2025}	385.15 (N.A.) {385.15}	167.49	75
		198	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3/2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.51	95.26
		199	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11/2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	96.98
		200	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8/2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	240.56	93.88
		201	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7/2020	4/2023 (Oct-23) {8/2024}	345.38 (395.59) {395.59}	355.08	88.69
		202	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3/2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	234.88	72.99
		203	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8/2020	4/2023 (Aug-23) {1/2025}	295.97 (N.A.) {295.97}	243.68	93.13

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		204	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3/2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		205	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1/2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {332.20}	148.62	40.82
		206	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12/2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	186.64	42.11
		207	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8/2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	179.62	49.22
		208	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9/2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.16	46.04
		209	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9/2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17
		210	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8/2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	200.82	77.2
		211	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10/2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	266.57	39.65

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		212	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10/2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	278.06	35.22
TRIPURA	PETROLEUM	213	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6/2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	298.34	62.5
	RAILWAYS	214	AGARTALA-AKHAURA NL (NFR) (N22000195)	4/2012	3/2020 (Jun-22) {9/2022}	569.63 (N.A.) {708.73}	380.92	84
	ROAD TRANSPORT AND HIGHWAYS	215	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6/2020	1/2022 (Jul-24) {9/2024}	201.99 (287.47) {287.47}	144.07	92.3
		216	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 (NHIDCL) (N24001318)	9/2020	4/2022 (Oct-22) {10/2023}	173.17 (N.A.) {173.17}	93.35	100
		217	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11/2020	6/2022 (Oct-23) {9/2024}	159.13 (171.50) {171.50}	79.43	98.05
		218	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3/2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2
		219	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6/2020	1/2022 (Feb-24) {9/2024}	277.50 (302.02) {302.02}	253.50	98.66
		220	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3/2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	0.23
		221	IMPROVEMENT AND WIDENING TO 2- LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5/2023	11/2024 (N.A.) {2/2025}	195.95 (N.A.) {195.95}	11.50	15.89

Table:-6. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		222	2 LANING FROM MANU-SIMLUNG PKG- 2 (NHIDCL) (N24001542)	2/2022	1/2025 (N.A.) {1/2025}	456.88 (N.A.) {456.88}	95.50	39.12
			Total			177,187.36 (-) {246,494.63}	130,436.52	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ANDAMAN AND NICOBAR ISLANDS	CIVIL AVIATION	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10/2013	9/2018 (May-23) {6/2023}	417.23 (707.73) {707.73}	698.80	100
	RAILWAYS	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH-JHL SECTION (NR) (N22000584)	3/2019	3/2025 (N.A.) {3/2025}	235.72 (N.A.) {235.72}	0.00	0
	ROAD TRANSPORT AND HIGHWAYS	3	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 ((NHIDCL) (N24000744)	3/2015	1/2022 (N.A.) {2/2026}	262.97 (N.A.) {262.97}	92.73	41.55
		4	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3/2017	12/2019 (Mar-23) {7/2024}	409.85 (N.A.) {409.85}	214.23	89.07
		5	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM (NHIDCL) (N24000748)	2/2018	9/2020 (Jan-23) {8/2025}	391.00 (N.A.) {391.00}	170.37	57.55
		6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3/2018	9/2020 (Nov-22) {9/2024}	234.27 (N.A.) {234.27}	126.50	76.86
		7	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11/2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	97.46
		8	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11/2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		9	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2/2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97
ANDHRA PRADESH	CIVIL AVIATION	10	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8/2017	2/2020 (Dec-21) {1/2024}	177.10 (N.A.) {177.10}	143.08	100
		11	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4/2020	3/2023 (N.A.) {6/2025}	611.80 (N.A.) {611.80}	308.89	52
		12	RAJAHMUNDRY AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12/2022	8/2025 (N.A.) {8/2025}	347.15 (N.A.) {347.15}	39.83	24
		13	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3/2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	22.06	14
	DEPARTMENT OF HIGHER EDUCATION	14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2/2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95
		15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC (CPWD EDUCATION) (N42000007)	9/2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	666.18	100
	PETROLEUM	16	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235)	7/2016	7/2020 (Jul-22) {10/2024}	20,928.00 (26,264.00) {30,609.00}	25,921.72	98.41
		17	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3/2016	6/2020 (Mar-25) {3/2025}	34,012.00 (N.A.) {34,012.00}	30,136.72	93.3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	18	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4/2018	4/2022 (Mar-25) {3/2025}	355.00 (N.A.) {355.00}	238.15	76.8
	19	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378)	9/2019	7/2020 (N.A.) {3/2025}	196.26 (196.26) {196.26}	147.53	86.8
	20	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9/2021	6/2024 (N.A.) {6/2025}	160.00 (N.A.) {160.00}	11.36	40
	21	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3/2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	105.01	4.8
	22	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9/2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.57	65.8
POWER	23	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9/2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	83.51	10
RAILWAYS	24	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12/2001	3/2009 (N.A.) {3/2027}	1,045.20 (N.A.) {2,500.98}	1,150.74	
	25	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4/2011	3/2021 (N.A.) {5/2027}	2,288.70 (N.A.) {3,122.35}	1,657.11	
	26	GUNTUR-GUNTAKAL (SCR) (N22000368)	4/2016	3/2022 (N.A.) {12/2025}	3,631.00 (N.A.) {3,887.48}	3,110.26	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	27	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4/2015	12/2023 (N.A.) {12/2024}	3,246.26 (N.A.) {6,238.67}	5,614.60	84
	28	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4/2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,679.82	67
	29	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4/2019	3/2026 (N.A.) {2/2025}	294.67 (307.66) {307.66}	110.93	41
	30	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9/2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	39.46	12
	31	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3/2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	
	32	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4/2016	12/2025 (N.A.) {12/2025}	226.72 (N.A.) {226.72}	161.84	55
	33	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4/2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	147.00	50
<u>ROAD TRANSPORT AND HIGHWAYS</u>	34	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9/2021	9/2022 (Sep-24) {3/2025}	517.05 (N.A.) {655.06}	504.99	60.5
	35	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9/2021	9/2022 (Sep-24) {3/2025}	622.00 (N.A.) {817.91}	481.97	52.35
	36	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2/2019	3/2023 (Oct-24) {10/2024}	757.45 (N.A.) {757.45}	471.32	77.56

Table:-7. Project List: Ongoing Projects as of 31st August 2024

37	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2/2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	313.61	15.05
38	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3/2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	753.00	72.3
39	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2/2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,028.32	56.41
40	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11/2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	874.50	80.8
41	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12/2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	753.94	61.67
42	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1/2022	1/2025 (Jan-23) {1/2025}	1,852.12 (N.A.) {1,787.00}	525.31	62
43	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3/2020	1/2024 (Dec-24) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,207.08	90.2
44	6L KANTAKAPALLE ? SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2/2021	10/2024 (N.A.) {10/2024}	824.29 (N.A.) {924.00}	385.35	61
45	6L JAKKUVA ? KORLAM SECTION OF NH-130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2/2021	3/2024 (Jul-24) {9/2024}	663.60 (N.A.) {768.00}	305.55	85

Table:-7. Project List: Ongoing Projects as of 31st August 2024

46	6L ALURU - JAKKUVA SECTION OF NH-130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2/2021	3/2024 (N.A.) {3/2025}	922.50 (N.A.) {1,128.68}	361.43	68.5
47	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVALU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12/2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	119.04	19.07
48	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVALU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12/2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	76.57	16
49	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12/2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	59.87	11.5
50	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12/2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	131.27	10.77
51	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2/2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	70.84	3.5
52	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2/2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.64	1.5
53	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1/2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	57.22	10.21

Table:-7. Project List: Ongoing Projects as of 31st August 2024

54	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTLA 196.000 KM. PACK (NHAI) (N24001848)	2/2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	59.96	4.6
55	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5/2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	310.90	38.06
56	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5/2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	104.87	29.82
57	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3/2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	393.81	92
58	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH-342 (MoRTH) (N24001932)	3/2022	9/2024 (N.A.) {9/2024}	401.72 (N.A.) {401.72}	162.11	65.45
59	MULAKALACHERUVU TO MADANAPALLE SECTION OF NH42 FROM KM 202.050 TO KM 245.640 EXCLUDING RETAINED STRE (MoRTH) (N24001933)	12/2021	12/2024 (N.A.) {12/2024}	480.10 (N.A.) {480.10}	443.87	78
60	NH440 RAYACHOTY TO VEMPALLI 2LPS (MoRTH) (N24001934)	12/2021	5/2024 (N.A.) {5/2024}	439.82 (N.A.) {439.82}	193.63	27
61	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3/2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	321.81	60
62	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3/2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	292.35	44.16

Table:-7. Project List: Ongoing Projects as of 31st August 2024

63	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3/2021	7/2024 (N.A.) {7/2024}	423.67 (N.A.) {423.67}	228.15	58
64	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12/2021	3/2024 (N.A.) {12/2025}	277.30 (N.A.) {277.30}	152.32	73.78
65	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3/2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	236.30	78.38
66	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1/2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	262.08	71
67	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3/2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	98.83	44.46
68	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12/2021	9/2024 (N.A.) {9/2024}	388.71 (N.A.) {388.71}	172.26	63.84
69	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3/2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	287.91	76
70	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3/2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	126.88	40

Table:-7. Project List: Ongoing Projects as of 31st August 2024

71	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8/2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	216.41	79
72	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8/2020	7/2024 (N.A.) {7/2024}	349.29 (N.A.) {349.29}	138.22	49
73	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8/2020	10/2024 (N.A.) {10/2024}	311.22 (N.A.) {311.22}	100.84	40
74	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3/2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	204.69	30.99
75	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8/2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	18.97
76	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10/2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	226.82	42.63
77	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7/2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	5.13
78	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3/2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	242.60	63.01

Table:-7. Project List: Ongoing Projects as of 31st August 2024

79	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA ? (NHAI) (N24001983)	10/2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	181.56	32.69
80	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3/2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	107.91	21.37
81	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3/2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	940.28	36.22
82	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10/2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	240.43	51.7
83	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6/2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	83.28	49.63
84	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2/2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	210.49	34.33
85	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7/2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	11.2
86	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9/2022	1/2025 (N.A.) {1/2025}	166.52 (N.A.) {166.52}	43.74	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

87	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2/2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	11.72	6
88	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARAPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2/2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	27.33	0.95
89	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2/2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	42.83	1.66
90	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2/2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	55.64	10.2
91	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2/2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	54.54	
92	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3/2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	253.37	29.95
93	SOMAYAJULAPALLI ? DHONE SECTION OF NH ? 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4/2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	185.00	37.85
94	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6/2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	87.55	52

Table:-7. Project List: Ongoing Projects as of 31st August 2024

95	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8/2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	11.35	8.26
96	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8/2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	29.08	19.84
97	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8/2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	183.47	13.37
98	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11/2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	32.76	27
99	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH- 167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11/2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	0.00	0
100	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE- 2) (MoRTH) (N24002147)	12/2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	34.83	14.35
101	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3/2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	0.00	0
102	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1/2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	41.66	0
103	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T (MoRTH) (N24000282)	1/2014	11/2014 (N.A.) {5/2024}	195.45 (N.A.) {385.97}	294.95	97

Table:-7. Project List: Ongoing Projects as of 31st August 2024

104	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3/2015	10/2015 (May-21) {5/2021}	271.45 (N.A.) {271.45}	238.23	100
105	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 (MoRTH) (N24000422)	3/2015	9/2015 (Aug-17) {5/2018}	309.01 (N.A.) {309.01}	0.00	100
106	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3/2018	12/2020 (Dec-22) {12/2024}	314.43 (N.A.) {348.72}	85.61	63.36
107	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 (MoRTH) (N24000928)	10/2015	12/2015 (Dec-19) {1/2021}	333.21 (N.A.) {353.43}	342.71	100
108	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU (MoRTH) (N24000929)	9/2016	2/2017 (Jan-22) {2/2022}	372.68 (N.A.) {309.37}	274.76	100
109	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11/2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90
110	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD (MoRTH) (N24000932)	1/2017	8/2017 (Jul-22) {7/2022}	319.28 (N.A.) {319.28}	241.94	100
111	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3/2018	8/2018 (N.A.) {8/2024}	289.67 (290.00) {285.29}	254.19	97

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		112	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P (MoRTH) (N24000963)	1/2018	8/2018 (Dec-21) {12/2021}	418.03 (386.99) {386.99}	365.55	100
		113	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD (MoRTH) (N24000964)	8/2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	457.55	98
		114	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1/2017	9/2017 (N.A.) {3/2025}	263.45 (N.A.) {263.45}	241.95	83.5
		115	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11/2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,163.91	75.27
		116	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT (MoRTH) (N24001386)	8/2020	3/2021 (N.A.) {8/2024}	222.61 (N.A.) {222.61}	143.53	76
	<u>WATER RESOURCES</u>	117	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2/2009	3/2020 (N.A.) {3/2024}	10,151.04 (N.A.) {55,548.87}	21,644.53	76.88
<u>ARUNACHAL PRADESH</u>	<u>CIVIL AVIATION</u>	118	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2/2019	8/2022 (Dec-24) {12/2024}	645.63 (N.A.) {712.15}	663.45	98.01
	<u>POWER</u>	119	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9/2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {21,247.54}	21,833.13	93.72

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	120	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2/2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,499.11	12.56
ROAD TRANSPORT AND HIGHWAYS	121	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2/2017	11/2023 (Mar-24) {11/2024}	180.57 (244.10) {180.57}	154.17	90.01
	122	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2/2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	144.91	100
	123	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3/2017	3/2022 (Dec-23) {7/2025}	1,718.59 (1,718.59) {1,718.59}	674.32	68.62
	124	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9/2016	12/2019 (Mar-23) {9/2024}	568.92 (568.92) {568.92}	508.65	99.79
	125	TWO-LANING OF HAYULIANG? HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1/2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
	126	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA- KHUPA-HAYULIANG SECTION OF NH- 113 FROM CH.68. (NHIDCL) (N24001244)	8/2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	136.35	58.77
	127	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE- BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9/2020	5/2022 (Oct-22) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38

Table:-7. Project List: Ongoing Projects as of 31st August 2024

128	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3/2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
129	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3/2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	568.30	98.99
130	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3/2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	474.23	97.71
131	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3/2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	371.45	91.27
132	TADADEGE - HENKAR (NHIDCL) (N24001315)	2/2021	3/2023 (Jun-24) {9/2024}	550.45 (N.A.) {550.45}	113.92	44.05
133	LADDA - BASAI (NHIDCL) (N24001316)	2/2021	4/2023 (Jan-25) {3/2025}	445.96 (N.A.) {445.96}	113.54	47.79
134	DOGINALA - GAU (NHIDCL) (N24001320)	12/2020	9/2022 (N.A.) {12/2024}	242.30 (N.A.) {242.30}	21.47	17.81
135	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2/2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	449.73	89.08
136	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6/2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	355.51	96.7

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		137	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (<i>MoRTH</i>) (<i>N24001375</i>)	6/2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	132.31	34.2
		138	JORAM ? KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (<i>NHIDCL</i>) (<i>N24001390</i>)	8/2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	97.23	97.03
		139	JORAM ? KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (<i>NHIDCL</i>) (<i>N24001391</i>)	8/2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	144.61	98.29
		140	JORAM ? KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) (<i>NHIDCL</i>) (<i>N24001392</i>)	8/2020	4/2022 (Jul-23) {7/2023}	199.03 (N.A.) {199.03}	102.85	100
		141	JORAM ? KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (<i>NHIDCL</i>) (<i>N24001393</i>)	8/2020	4/2022 (Feb-24) {11/2024}	184.88 (N.A.) {184.88}	95.64	93.83
ASSAM	CIVIL AVIATION	142	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (<i>AAI</i>) (<i>N04000083</i>)	12/2016	3/2021 (N.A.) {3/2025}	1,142.00 (N.A.) {2,333.00}	1,290.94	63.48
	HEALTH AND FAMILY WELFARE	143	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (<i>HITES</i>) (<i>N21000027</i>)	5/2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	757.66	98.87
	PETROLEUM	144	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (<i>OIL</i>) (<i>N16000331</i>)	1/2018	2/2020 (Dec-23) {12/2024}	543.91 (N.A.) {670.90}	491.56	93.7
		145	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (<i>NRL</i>) (<i>N16000379</i>)	1/2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	12,027.15	62.27

Table:-7. Project List: Ongoing Projects as of 31st August 2024

146	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1/2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,037.54	76.2
147	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5/2021	10/2023 (Feb-25) {2/2025}	412.00 (509.84) {509.84}	350.40	76.8
148	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON (ONGC) (N16000433)	8/2021	2/2023 (Jun-24) {8/2024}	218.38 (N.A.) {218.38}	172.05	82.8
149	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3/2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	156.03	48.8
150	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6/2021	12/2024 (N.A.) {12/2024}	860.00 (N.A.) {860.00}	300.10	84.4
151	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12/2020	7/2024 (Mar-24) {12/2024}	430.76 (N.A.) {430.76}	244.08	71.37
152	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6/2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	57.60	18.5
153	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3/2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	1.08	11
154	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3/2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	30.05	2.7

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	155	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3/2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	18.59	68
	156	DCU REVAMP PROJECT (NRL) (N16000511)	8/2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	140.35	33.4
	157	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1/2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	108.35	31
	158	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9/2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	0.00	
<u>RAILWAYS</u>	159	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4/2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,424.50	91
<u>ROAD TRANSPORT AND HIGHWAYS</u>	160	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2/2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	321.15	30.59
	161	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12/2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100
	162	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8/2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	291.19	57.1
	163	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9/2021	7/2024 (N.A.) {12/2024}	625.64 (N.A.) {625.64}	455.08	77.77

Table:-7. Project List: Ongoing Projects as of 31st August 2024

164	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3/2022	7/2024 (N.A.) {8/2024}	215.27 (N.A.) {215.27}	144.52	95.8
165	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 (NHIDCL) (N24001452)	4/2022	7/2024 (N.A.) {8/2024}	170.95 (N.A.) {170.95}	123.89	98.85
166	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11/2021	7/2024 (N.A.) {10/2024}	204.10 (N.A.) {204.10}	119.11	77.91
167	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3/2022	1/2025 (N.A.) {1/2025}	909.02 (N.A.) {909.02}	388.98	74.54
168	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8/2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	178.56	98.13
169	BALANCE WORK OF 4L OF NARIMBANGLO?JATINGA JUNCTION-HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3/2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	394.71	44.49
170	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3/2022	6/2024 (N.A.) {12/2024}	457.72 (N.A.) {457.72}	235.64	85
171	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH (NHAI) (N24001549)	7/2017	4/2020 (Jul-24) {7/2024}	442.23 (N.A.) {442.23}	265.19	100
172	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3/2022	2/2025 (N.A.) {12/2025}	613.89 (N.A.) {613.89}	17.09	9.23

Table:-7. Project List: Ongoing Projects as of 31st August 2024

173	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1/2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	133.51	37.45
174	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3/2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	4.07	10.6
175	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3/2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	266.61	32.97
176	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3/2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	267.62	30.96
177	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3/2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	326.53	28.21
178	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3/2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	172.88	49.02
179	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3/2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	154.32	46.99
180	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3/2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	329.25	20.83

Table:-7. Project List: Ongoing Projects as of 31st August 2024

181	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3/2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	198.83	9.09
182	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3/2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	254.13	9.86
183	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1/2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	133.24	37.69
184	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1/2023	12/2025 (N.A.) {12/2025}	356.65 (N.A.) {356.65}	113.59	3.88
185	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3/2023	12/2025 (N.A.) {12/2025}	643.42 (N.A.) {643.42}	64.67	8.25
186	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2/2020	3/2022 (N.A.) {10/2024}	592.06 (N.A.) {592.06}	291.85	93.87
187	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2/2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	306.95	11.04
188	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3/2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	703.59	25.1
189	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2/2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	172.77	18.3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

190	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12/2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	268.54	27.77
191	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6/2015	8/2023 (N.A.) {12/2024}	437.39 (N.A.) {437.39}	307.45	20.58
192	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6/2015	3/2024 (N.A.) {7/2024}	463.49 (N.A.) {463.49}	368.12	31.56
193	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1/1991	6/2019 (Jun-19) {10/2024}	520.01 (N.A.) {520.01}	297.99	90.01
194	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12/2015	12/2018 (Jul-21) {10/2024}	289.99 (N.A.) {289.99}	232.56	87.62
195	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1/2016	1/2016 (N.A.) {12/2024}	294.17 (N.A.) {294.17}	295.84	38.88
196	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1/2016	12/2021 (N.A.) {12/2021}	252.00 (N.A.) {330.30}	146.28	
197	FOUR LANING OF BALACHERA- HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE (NHIDCL) (N24000902)	10/2017	6/2020 (Dec-23) {4/2024}	818.00 (887.68) {887.68}	873.61	100
198	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3/2020	12/2022 (N.A.) {8/2024}	220.20 (N.A.) {220.20}	215.69	97.76

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		199	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8/2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	186.61	100
		200	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3/2020	3/2022 (Dec-23) {12/2024}	216.49 (241.52) {216.49}	104.36	79.48
		201	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11/2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	1,998.70	50.74
		202	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3/2020	6/2022 (N.A.) {5/2025}	261.13 (N.A.) {261.13}	64.96	54.59
		203	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3/2020	6/2022 (May-24) {4/2025}	217.50 (N.A.) {217.50}	84.36	64.15
		204	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3/2021	1/2023 (N.A.) {9/2024}	288.85 (N.A.) {288.85}	221.38	91.24
		205	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3/2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	78.65	27.93
BIHAR	CIVIL AVIATION	206	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5/2018	10/2022 (Dec-24) {12/2024}	1,216.90 (N.A.) {1,216.90}	778.89	81.39
		207	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7/2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	0.00	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>DEPARTMENT OF HIGHER EDUCATION</u>	208	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE- II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2/2016	6/2017 (Jan-24) {1/2024}	496.18 (496.00) {460.00}	390.15	100
	209	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9/2018	9/2020 (N.A.) {9/2020}	375.00 (N.A.) {375.00}	327.75	99
<u>PETROLEUM</u>	210	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1/2020	4/2023 (Dec-24) {12/2025}	14,810.00 (N.A.) {14,810.00}	9,441.70	78.9
	211	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6/2019	12/2029 (Mar-30) {3/2030}	163.00 (N.A.) {163.00}	81.62	23.4
	212	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1/2022	4/2025 (N.A.) {4/2025}	389.00 (N.A.) {389.00}	21.69	15.2
	213	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12/2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	178.78	12.5
	214	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12/2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	205.15	11.5
<u>POWER</u>	215	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2/2005	10/2011 (Jul-23) {11/2024}	8,692.97 (21,312.11) {21,312.11}	22,311.28	90
	216	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3/2019	1/2024 (N.A.) {6/2025}	10,439.09 (N.A.) {10,439.09}	10,004.33	82

Table:-7. Project List: Ongoing Projects as of 31st August 2024

RAILWAYS	217	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR (ECR) (220100240)	4/1997	3/2012 (N.A.) {12/2023}	324.73 (967.29) {1,250.00}	1,235.55	99
	218	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4/1997	(N.A.) {12/2026}	162.87 (614.45) {614.45}	451.75	50
	219	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4/2003	(N.A.) {12/2024}	528.65 (2,087.36) {2,087.36}	1,962.20	48
	220	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9/2006	3/2019 (N.A.) {3/2025}	532.87 (2,132.03) {4,415.08}	2,723.84	78
	221	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4/1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	576.03	78
	222	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4/2008	(N.A.) {1/2025}	1,605.17 (1,605.17) {1,605.17}	1,331.47	26
	223	SAKRI-NIRMALI AND JHANJHARPUR- LAUKAHABAZAR AND SAHARSA- FORBESGANJ (GC) (ECR) (N22000180)	4/2004	(N.A.) {6/2024}	372.14 (1,470.50) {2,350.00}	2,502.46	97
	224	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA- BARDIBAS(NEPAL) GC (ECR) (N22000181)	4/2009	3/2020 (N.A.) {3/2026}	548.00 (548.00) {783.83}	544.31	78
	225	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5/2015	(N.A.) {3/2025}	380.00 (519.33) {519.33}	532.01	62
	226	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12/2015	3/2020 (N.A.) {9/2024}	1,200.20 (1,200.20) {1,771.07}	1,717.88	96

Table:-7. Project List: Ongoing Projects as of 31st August 2024

227	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12/2015	3/2020 (N.A.) {5/2025}	1,491.47 (1,491.47) {1,600.00}	1,569.68	77
228	SAGauli VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4/2016	3/2021 (N.A.) {12/2024}	744.04 (1,215.54) {1,215.54}	1,388.96	85
229	MUZAFFARPUR SAGauli DOUBLING 100.60 KM (ECR) (N22000473)	4/2016	3/2021 (N.A.) {9/2024}	731.64 (1,185.73) {1,300.00}	1,363.41	80
230	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, (ECR) (N22000476)	4/1991	(N.A.) {12/2024}	329.39 (803.09) {2,722.16}	2,549.45	90
231	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6/2019	6/2025 (N.A.) {9/2024}	983.62 (253.23) {415.00}	378.05	80
232	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7/2022	7/2027 (N.A.) {6/2025}	486.00 (N.A.) {486.00}	79.51	30
233	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2/2019	6/2028 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	2.34	
234	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10/2022	10/2027 (N.A.) {6/2025}	234.00 (223.69) {223.69}	15.16	
235	KATI HAR-KUMEDPUR & KATI HAR-MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8/2022	8/2027 (N.A.) {8/2027}	745.00 (N.A.) {745.00}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

ROAD TRANSPORT AND HIGHWAYS	236	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH-119D (PKG-III) (NHAI) (N24001697)	2/2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	146.66	11.5
	237	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8/2022	8/2024 (N.A.) {8/2024}	1,198.02 (N.A.) {1,198.02}	0.00	
	238	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3/2022	12/2024 (N.A.) {3/2025}	312.58 (N.A.) {312.58}	128.79	54.95
	239	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12/2021	3/2024 (Dec-24) {12/2024}	552.55 (553.00) {553.00}	414.79	54.95
	240	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4/2022	4/2024 (N.A.) {4/2024}	1,769.50 (N.A.) {1,769.50}	0.00	
	241	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12/2021	9/2024 (N.A.) {9/2024}	184.90 (185.00) {185.00}	161.94	84.78
	242	6 L OF AURANGABAD TO BIHAR- JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2/2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	
	243	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3/2021	3/2024 (Dec-24) {12/2024}	1,020.84 (N.A.) {1,020.84}	84.78	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

244	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3/2022	3/2024 (Dec-24) {12/2024}	1,485.66 (N.A.) {1,485.66}	0.00	
245	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. (NHAI) (N24001706)	3/2021	1/2024 (Oct-24) {10/2024}	1,097.18 (1,097.00) {1,097.00}	518.04	99.7
246	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E (NHAI) (N24001707)	3/2021	1/2024 (Dec-24) {12/2024}	1,143.46 (1,143.46) {1,143.46}	487.45	97.8
247	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9/2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	96.57
248	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9/2020	4/2023 (Dec-24) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
249	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S (NHAI) (N24001710)	9/2020	3/2023 (Oct-24) {10/2024}	2,334.68 (2,494.20) {2,494.20}	913.70	99.2
250	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9/2020	3/2023 (Dec-24) {12/2024}	939.43 (N.A.) {939.43}	370.62	100
251	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8/2020	7/2023 (Dec-24) {12/2024}	690.00 (N.A.) {690.00}	770.73	98.55
252	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHI?MOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12/2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

253	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2/2022	11/2024 (Mar-25) {3/2025}	624.43 (N.A.) {624.43}	188.90	67
254	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3/2021	1/2025 (Mar-25) {3/2025}	477.54 (N.A.) {477.54}	201.92	56.14
255	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3/2021	3/2024 (Jun-25) {6/2025}	566.15 (N.A.) {566.15}	156.09	35
256	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7/2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	263.84	18.44
257	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2/2022	12/2024 (Mar-25) {3/2025}	427.29 (N.A.) {427.29}	128.25	55.9
258	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3/2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	31.83	25.5
259	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3/2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	0.00	
260	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12/2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	100.28	68.58
261	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12/2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	32.97	16.01

Table:-7. Project List: Ongoing Projects as of 31st August 2024

262	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2/2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	6.6
263	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2/2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
264	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3/2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	52.94	46
265	PATNA-MUZZAFFARPUR (NHAI) (N24000165)	8/2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.15
266	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1/2011	7/2013 (Apr-25) {4/2025}	575.00 (N.A.) {575.00}	544.76	84.87
267	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1/2014	10/2019 (Dec-24) {12/2024}	675.00 (780.77) {780.77}	678.26	87.77
268	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12/2015	4/2019 (Jul-22) {3/2025}	1,041.10 (567.00) {639.58}	553.73	97.09
269	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12/2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	94.25
270	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2/2016	11/2018 (Sep-24) {9/2024}	319.68 (503.28) {503.28}	430.14	98.75

Table:-7. Project List: Ongoing Projects as of 31st August 2024

271	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2/2016	5/2016 (Sep-24) {9/2024}	178.85 (225.06) {278.54}	232.61	98.35
272	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2/2016	5/2016 (Sep-24) {9/2024}	553.30 (706.39) {706.39}	607.49	98
273	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1/2014	10/2016 (Dec-24) {12/2024}	1,408.85 (2,138.16) {2,138.16}	1,695.16	95.89
274	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3/2017	3/2020 (Mar-25) {3/2025}	672.89 (736.01) {830.31}	566.83	74.19
275	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8/2017	2/2022 (Aug-23) {10/2024}	950.64 (1,161.00) {1,168.33}	966.99	83.29
276	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12/2017	10/2024 (Apr-25) {6/2025}	2,598.00 (N.A.) {1,962.50}	1,249.32	68.11
277	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1/2018	12/2021 (Dec-19) {3/2025}	573.70 (644.50) {726.99}	452.20	75.06
278	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3/2018	11/2021 (Dec-24) {12/2024}	496.20 (470.18) {537.17}	366.24	84.99

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	279	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9/2018	6/2024 (Feb-26) {2/2026}	1,478.40 (N.A.) {1,478.40}	806.35	57.45
	280	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2/2019	9/2024 (N.A.) {2/2026}	2,926.42 (N.A.) {2,926.42}	970.95	47
	281	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10/2013	12/2020 (Dec-24) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.3
	282	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10/2013	11/2020 (Dec-24) {12/2024}	446.97 (598.48) {740.50}	638.80	96.3
	283	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10/2013	11/2020 (Dec-24) {12/2024}	464.09 (605.53) {765.12}	698.25	97.3
	284	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10/2019	8/2023 (Dec-24) {12/2024}	1,101.99 (N.A.) {1,101.99}	765.79	63.38
URBAN DEVELOPMENTS	285	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAIL) (N28000148)	2/2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	2,637.57	38.15
WATER RESOURCES	286	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3/2018	7/2021 (Dec-19) {9/2024}	230.06 (N.A.) {230.06}	228.38	95
	287	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10/2017	9/2020 (Nov-20) {10/2024}	254.13 (413.29) {413.29}	120.95	82

Table:-7. Project List: Ongoing Projects as of 31st August 2024

288	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028)	11/2018	12/2020 (N.A.) {2/2024}	236.15 (N.A.) {236.15}	142.08	100
289	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3/2018	8/2021 (Mar-18) {9/2024}	305.19 (N.A.) {305.19}	310.39	90
290	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3/2018	10/2021 (Mar-18) {6/2024}	294.02 (350.79) {294.02}	365.58	100
291	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037)	12/2014	3/2020 (N.A.) {6/2022}	225.77 (N.A.) {398.90}	363.79	100
292	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4/2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	489.65	100
293	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040)	5/2017	4/2021 (May-17) {2/2023}	356.37 (364.00) {356.37}	312.11	100
294	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043)	5/2017	11/2020 (May-17) {5/2022}	191.62 (N.A.) {191.62}	122.98	100
295	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3/2017	5/2021 (Mar-17) {2/2023}	277.42 (253.98) {277.42}	345.95	100
296	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8/2017	6/2022 (N.A.) {9/2024}	578.89 (453.83) {578.89}	150.50	46
297	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8/2017	6/2022 (N.A.) {9/2024}	824.00 (734.09) {824.00}	377.18	48

Table:-7. Project List: Ongoing Projects as of 31st August 2024

CHHATTISGARH	COAL	298	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6/2010	3/2023 (N.A.) {3/2025}	11,816.40 (N.A.) {11,816.40}	6,086.17	77
		299	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY (SECL) (N06000008)	8/2013	3/2023 (N.A.) {3/2025}	7,612.33 (N.A.) {7,612.33}	4,542.11	81
		300	PELMA OCP(15.00MTY) (SECL) (N06000045)	11/2014	3/2023 (N.A.) {3/2030}	1,624.59 (N.A.) {1,624.59}	13.65	16
		301	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12/2013	3/2022 (Mar-25) {3/2025}	610.63 (N.A.) {610.63}	565.04	81
		302	AMERA OC RCE (SECL) (N06000123)	2/2015	3/2018 (Mar-26) {3/2026}	335.97 (N.A.) {335.97}	173.32	42
		303	AMGAON OPENCAS T PROJECT RCE (SECL) (N06000135)	7/2015	3/2020 (Mar-26) {3/2026}	316.10 (N.A.) {316.10}	187.50	56
		304	MAHAMAYA OPENCAS T PROJECT (SECL) (N06000164)	5/2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	178.90	37
		305	JHIRIA WEST OPENCAS T PROJECT (SECL) (N06000166)	11/2018	3/2026 (N.A.) {3/2026}	366.94 (N.A.) {366.94}	29.97	36
		306	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8/2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	843.12	38
		307	JAMPALI OCP RCE (SECL) (N06000198)	5/2020	3/2024 (Mar-25) {3/2025}	278.64 (N.A.) {278.64}	207.60	73

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	308	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12/2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	41.88	10
	309	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12/2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,628.55	26
	310	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7/2016	3/2020 (Mar-05) {3/2025}	459.49 (N.A.) {459.49}	254.75	92
	311	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1/2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	0.00	2
<u>DEPARTMENT OF HIGHER EDUCATION</u>	312	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3/2020	7/2022 (N.A.) {7/2022}	808.62 (N.A.) {808.62}	640.70	99.2
<u>PETROLEUM</u>	313	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3/2021	3/2024 (Mar-25) {3/2025}	456.00 (N.A.) {456.00}	330.02	80.1
<u>POWER</u>	314	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2/2023	11/2023 (N.A.) {9/2024}	385.84 (N.A.) {385.84}	85.61	37
	315	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3/2023	9/2024 (N.A.) {10/2024}	271.69 (N.A.) {271.69}	108.34	50
	316	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX (PGCIL) (N18000355)	3/2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	56.59	60
	317	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (BHEL) (N18000381)	8/2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	709.38	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

RAILWAYS	318	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12/2012	3/2020 (N.A.) {3/2024}	1,160.00 (N.A.) {1,440.00}	1,425.45	88
	319	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4/2015	3/2021 (Dec-23) {12/2024}	1,973.00 (2,135.34) {2,135.34}	2,017.74	80
	320	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4/2013	9/2018 (N.A.) {12/2024}	3,055.00 (3,438.39) {3,438.39}	3,041.21	93
	321	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7/2011	10/2024 (N.A.) {2/2025}	1,171.30 (N.A.) {1,171.30}	460.35	45
	322	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9/2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.10	
	323	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12/2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	0.21	
	324	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9/2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	0.63	
	325	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9/2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	0.22	
	326	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9/2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	0.37	
	327	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9/2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	328	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (<i>SECR</i>) (<i>N22000580</i>)	6/2022	6/2030 (N.A.) {6/2030}	1,376.20 (N.A.) {775.82}	38.91	5
	329	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (<i>RVNL</i>) (<i>N22000602</i>)	3/2008	6/2025 (N.A.) {6/2025}	631.78 (N.A.) {1,627.56}	1,323.64	84
	330	CHIRIMIRI-NAGPUR HALT (<i>SECR</i>) (<i>N22000616</i>)	10/2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	
<u>ROAD TRANSPORT AND HIGHWAYS</u>	331	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (<i>NHAI</i>) (<i>N24001588</i>)	12/2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	504.46	50.76
	332	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (<i>NHAI</i>) (<i>N24001593</i>)	11/2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	782.50	70.65
	333	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH- 130A (<i>NHAI</i>) (<i>N24001611</i>)	4/2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	388.19	69.01
	334	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (<i>MoRTH</i>) (<i>N24001917</i>)	3/2020	5/2024 (N.A.) {11/2024}	278.97 (N.A.) {278.97}	169.62	70
	335	UPGRADATION OF NH 930 JHALMALA TO SHERPAR FROM NH KM 30.600 TO KM 67.800 TO TWOFOUR LANE WITH PAVED (<i>MoRTH</i>) (<i>N24001918</i>)	12/2020	8/2023 (Jul-24) {7/2024}	222.86 (N.A.) {222.86}	168.98	100
	336	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOU (<i>MoRTH</i>) (<i>N24001919</i>)	12/2020	9/2023 (Nov-24) {11/2024}	193.16 (N.A.) {193.16}	73.42	61.3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

337	UPGRADATION OF NH 130A MUNGELI TO PONDII FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3/2021	9/2024 (N.A.) {9/2024}	218.57 (N.A.) {218.57}	91.66	66.27
338	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3/2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	81.25	8.05
339	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6/2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	318.96	9.5
340	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6/2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	585.16	22.1
341	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1/2016	8/2016 (N.A.) {12/2024}	497.14 (572.66) {572.66}	363.29	57.37
342	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION (MoRTH) (N24001218)	11/2015	6/2017 (N.A.) {7/2024}	335.32 (397.32) {335.32}	345.52	100
343	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V (MoRTH) (N24001219)	1/2016	9/2016 (N.A.) {7/2024}	476.20 (610.18) {543.73}	501.42	100
344	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1/2016	10/2016 (N.A.) {9/2024}	624.98 (731.50) {731.50}	604.79	99

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	345	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3/2016	7/2016 (N.A.) {12/2024}	452.94 (N.A.) {435.61}	287.53	61.93
	346	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3/2018	1/2019 (N.A.) {9/2024}	349.03 (N.A.) {349.03}	316.52	97.78
	347	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A (MoRTH) (N24001228)	11/2017	5/2019 (N.A.) {9/2024}	188.80 (N.A.) {188.80}	136.81	97
STEEL	348	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11/2015	6/2023 (Jul-24) {3/2026}	2,907.00 (N.A.) {2,907.00}	2,114.17	62.7
	349	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3/2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,212.31	62.6
	350	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7/2021	11/2024 (N.A.) {1/2026}	282.44 (N.A.) {282.44}	110.78	41.03
	351	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10/2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	36.47	1.3
	352	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11/2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	225.98	39.4
URBAN DEVELOPMEN I	353	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5/2019	9/2020 (Oct-24) {10/2024}	299.97 (299.97) {299.97}	245.83	80

Table:-7. Project List: Ongoing Projects as of 31st August 2024

DELHI	<u>CIVIL AVIATION</u>	354	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11/2016	4/2020 (Apr-24) {4/2024}	303.80 (374.98) {374.98}	327.61	100
	<u>DPIIT</u>	355	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11/2017	12/2019 (N.A.) {9/2024}	4,773.00 (N.A.) {5,401.00}	4,789.04	97.2
	<u>FINANCE</u>	356	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7/2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85
	<u>HOME AFFAIRS</u>	357	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10/2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,869.93	99
		358	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6/2019	7/2022 (N.A.) {5/2025}	277.35 (N.A.) {277.35}	89.77	53
	<u>RAILWAYS</u>	359	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4/2012	(N.A.) {9/2023}	295.68 (N.A.) {419.00}	133.78	30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	360	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6/2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	97
		361	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAIPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5/2020	7/2024 (N.A.) {1/2026}	1,467.44 (N.A.) {1,942.89}	912.69	78.28
		362	DEVELOPMENT OF 6L UER-II (PACKAGE-I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7/2020	10/2023 (N.A.) {9/2024}	2,171.80 (N.A.) {2,171.80}	958.13	98.9

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	363	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778)	7/2020	10/2023 (N.A.) {6/2024}	801.46 (N.A.) {801.46}	382.03	99.33
	364	DWARKA EXPRESSWAY FROM KM - 0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK-RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3/2018	9/2022 (N.A.) {9/2024}	2,507.00 (N.A.) {3,030.73}	1,155.70	84.29
	365	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1/2018	10/2021 (N.A.) {9/2024}	2,067.67 (N.A.) {2,160.00}	1,496.49	94.7
	366	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7/2020	10/2023 (N.A.) {9/2024}	1,894.96 (N.A.) {1,894.96}	741.88	83.56
TELECOMMUNICATIONS	367	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10/2014	3/2018 (N.A.) {12/2024}	248.20 (N.A.) {248.20}	213.22	98
URBAN DEVELOPMENT I	368	DELHI MRTS PHASE-III (DMRC) (N28000056)	9/2011	3/2016 (Aug-21) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,524.65	99.99
	369	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7/2016	(N.A.) {8/2024}	2,694.00 (N.A.) {2,694.00}	2,375.93	98
	370	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10/2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2
	371	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10/2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	529.45	43

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	372	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7/2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	12,650.99	53.5
	373	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND (DMRC) (N28000136)	5/2017	12/2020 (Nov-22) {11/2022}	565.00 (739.49) {565.00}	521.45	100
	374	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1/2022	11/2024 (May-25) {5/2025}	646.52 (N.A.) {646.52}	213.45	58
	375	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10/2016	3/2024 (N.A.) {3/2025}	1,536.72 (N.A.) {1,536.72}	272.02	73
<u>WATER RESOURCES</u>	376	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD ? 10MG/L (DJB) (N30000014)	3/2017	12/2022 (N.A.) {9/2024}	665.78 (N.A.) {665.78}	782.51	96
	377	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015)	5/2016	12/2021 (N.A.) {2/2024}	211.79 (223.70) {211.79}	208.71	100
	378	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016)	5/2016	2/2022 (Sep-23) {7/2023}	239.11 (314.71) {239.11}	268.13	100
	379	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (DJB) (N30000017)	12/2018	1/2021 (N.A.) {3/2022}	515.07 (N.A.) {515.07}	388.08	100
	380	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO (DJB) (N30000018)	5/2017	5/2020 (N.A.) {5/2020}	344.81 (N.A.) {344.81}	0.00	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

GOA	CIVIL AVIATION	381	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11/2017	9/2021 (N.A.) {3/2025}	255.69 (N.A.) {255.69}	68.63	52
	DEPARTMENT OF HIGHER EDUCATION	382	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5/2019	8/2021 (Jun-24) {12/2024}	303.90 (390.40) {390.40}	360.00	99
	PETROLEUM	383	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (ONGC) (N16000502)	3/2023	6/2024 (N.A.) {11/2024}	325.53 (N.A.) {325.53}	286.18	98.9
	ROAD TRANSPORT AND HIGHWAYS	384	MOPA AIRPORT (MoRTH) (N24001458)	12/2021	4/2022 (Sep-24) {9/2024}	1,183.16 (N.A.) {1,183.16}	1,106.30	97
		385	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE (MoRTH) (N24000444)	10/2015	(Sep-23) {9/2023}	936.40 (N.A.) {936.40}	770.90	100
		386	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR (MoRTH) (N24000516)	12/2015	(N.A.) {12/2023}	819.95 (N.A.) {819.95}	504.65	99
GUJARAT	ATOMIC ENERGY	387	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 (NPCIL) (N02000010)	10/2009	12/2015 (N.A.) {3/2024}	11,459.00 (22,517.00) {22,517.00}	21,479.00	100
	CIVIL AVIATION	388	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1/2018	8/2022 (May-24) {9/2024}	1,405.00 (N.A.) {1,405.00}	1,268.49	99.8
		389	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8/2018	2/2021 (N.A.) {10/2024}	353.25 (N.A.) {353.25}	337.30	97.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	390	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6/2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	234.90	30
PETROLEUM	391	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2/2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,093.53	89.4
	392	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11/2019	5/2023 (Mar-24) {12/2024}	5,251.00 (5,894.00) {5,894.00}	4,158.49	98.2
	393	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9/2020	8/2024 (Dec-25) {12/2025}	18,936.00 (N.A.) {18,936.00}	8,641.75	74.5
	394	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10/2020	8/2023 (Nov-24) {11/2024}	1,614.00 (N.A.) {1,614.00}	1,003.59	89.74
	395	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4/2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	270.11	52
	396	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8/2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	390.39	31.7
	397	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1/2022	11/2024 (N.A.) {11/2024}	621.40 (N.A.) {621.40}	101.03	19.8
	398	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1/2022	9/2024 (N.A.) {8/2025}	328.00 (N.A.) {328.00}	23.25	18.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	399	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5/2022	2/2025 (N.A.) {2/2025}	249.43 (N.A.) {249.43}	96.35	75.4
	400	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8/2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	720.56	50
	401	CONSTRUCTION OF TWO PRODUCED WATER TREATMENT PLANTS (PWTP) AT BECHARAJI AND SOBHASAN INSTALLATION OF (ONGC) (N16000482)	7/2021	7/2024 (N.A.) {9/2024}	320.20 (N.A.) {187.61}	151.05	88.3
	402	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7/2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	117.88	73.8
	403	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11/2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	29.20	18.5
POWER	404	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1/2021	7/2022 (N.A.) {7/2022}	842.27 (N.A.) {842.27}	494.80	0
	405	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5/2021	9/2022 (N.A.) {9/2022}	674.92 (N.A.) {674.92}	457.90	0
	406	Bagodara Solar Power Project (SJVN) (N18000297)	5/2021	10/2022 (N.A.) {3/2025}	339.35 (N.A.) {339.35}	330.05	72
	407	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11/2021	5/2023 (N.A.) {6/2024}	937.80 (N.A.) {937.80}	690.34	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

408	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7/2022	3/2025 (N.A.) {3/2025}	1,316.02 (N.A.) {1,316.02}	207.34	0
409	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9/2022	9/2024 (N.A.) {9/2024}	7,179.54 (N.A.) {7,179.54}	916.13	0
410	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11/2022	3/2024 (N.A.) {6/2024}	1,442.60 (N.A.) {1,442.60}	80.60	0
411	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3/2023	12/2024 (N.A.) {2/2025}	922.30 (N.A.) {922.30}	191.77	25
412	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3/2023	3/2025 (N.A.) {3/2025}	815.12 (N.A.) {815.12}	7.89	25
413	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3/2023	12/2024 (N.A.) {2/2025}	966.79 (N.A.) {966.79}	120.72	33
414	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3/2023	3/2025 (N.A.) {3/2025}	1,167.55 (N.A.) {1,167.55}	376.14	20
415	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3/2023	3/2025 (N.A.) {3/2025}	2,820.99 (N.A.) {2,820.99}	152.10	18
416	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6/2023	12/2024 (N.A.) {12/2024}	6,283.81 (N.A.) {6,283.81}	383.77	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	417	DAYAPAR WIND- III (HYBRID TRANCHE-V) (<i>NTPC</i>) (<i>N18000366</i>)	5/2023	1/2025 (N.A.) {5/2025}	1,095.01 (N.A.) {1,095.01}	119.46	0
	418	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (<i>PGCIL</i>) (<i>N18000383</i>)	7/2023	7/2025 (N.A.) {7/2025}	334.00 (N.A.) {334.00}	0.00	
	419	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (<i>PGCIL</i>) (<i>N18000384</i>)	12/2023	12/2025 (N.A.) {12/2025}	3,752.00 (N.A.) {3,752.00}	113.02	1
RAILWAYS	420	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) (<i>WR</i>) (<i>N22000123</i>)	4/2008	3/2012 (Sep-26) {9/2026}	318.24 (1,531.55) {1,531.55}	1,103.50	83
	421	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (<i>WR</i>) (<i>N22000142</i>)	4/2011	(Oct-25) {10/2025}	844.10 (844.10) {844.10}	529.95	41
	422	ANAND GODHRA DOUBLING PROJECT 79 KMS (<i>WR</i>) (<i>N22000504</i>)	4/2017	3/2020 (Dec-24) {12/2024}	692.25 (692.26) {692.26}	529.42	90
	423	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (<i>WR</i>) (<i>N22000505</i>)	4/2018	3/2024 (N.A.) {12/2024}	537.31 (537.31) {537.31}	564.48	96
	424	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (<i>WR</i>) (<i>N22000532</i>)	2/2023	3/2027 (Feb-27) {2/2027}	961.67 (961.67) {961.67}	13.13	1
	425	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (<i>WR</i>) (<i>N22000533</i>)	2/2023	12/2025 (Oct-25) {10/2025}	152.44 (152.44) {152.44}	14.51	3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

426	MEHSANA-PALANPUR (65.1 KM) (WR) (N22000534)	9/2020	9/2026 (Sep-24) {9/2024}	529.30 (N.A.) {537.31}	268.08	94
427	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10/2021	10/2026 (Jun-25) {6/2025}	1,011.72 (1,080.58) {1,080.58}	671.97	56
428	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6/2022	2/2030 (Feb-25) {2/2025}	354.99 (482.42) {482.42}	314.62	47
429	PETLAD-BHADRAN (22.5 KM) (WR) (N22000538)	5/2022	5/2030 (N.A.) {12/2025}	202.50 (307.12) {307.12}	41.68	4
430	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5/2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	45.04	5
431	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2/2023	3/2030 (N.A.) {10/2025}	401.48 (670.17) {670.17}	68.98	7
432	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5/2022	3/2030 (Apr-25) {4/2025}	216.72 (349.93) {349.93}	60.45	12
433	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5/2022	3/2030 (Feb-25) {2/2025}	309.81 (415.38) {415.38}	261.99	65
434	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5/2022	5/2030 (N.A.) {5/2030}	296.54 (N.A.) {296.54}	0.00	0
435	KALOL-KADI-KATOSAN ROAD (37.23 KM) (WR) (N22000549)	6/2022	6/2027 (Sep-24) {9/2024}	279.23 (346.94) {346.94}	293.48	89

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	436	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2/2023	1/2028 (Sep-26) {9/2026}	410.46 (410.46) {410.46}	15.88	2
	437	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD (16.51 KM) (PB#29/NR/202 (WR) (N22000551)	10/2022	10/2027 (N.A.) {10/2027}	437.21 (N.A.) {437.21}	0.00	0
	438	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7/2022	7/2030 (N.A.) {12/2026}	1,695.82 (N.A.) {2,798.16}	642.63	8
	439	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6/2022	12/2026 (N.A.) {12/2026}	492.83 (N.A.) {492.83}	0.00	0
	440	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9/2012	3/2027 (Mar-26) {3/2026}	261.68 (261.68) {261.68}	260.75	35
	441	NATHDWARA-NEW NATHDWARA NEW LINE (MM OF AJMER-CHITTAURGARH-UDAIPUR) (WR) (N22000623)	6/2013	6/2025 (N.A.) {6/2025}	166.33 (N.A.) {166.33}	53.74	5
<u>ROAD TRANSPORT AND HIGHWAYS</u>	442	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6/2020	4/2023 (Sep-24) {9/2024}	166.21 (N.A.) {166.21}	98.65	93
	443	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5/2020	3/2024 (Oct-24) {11/2024}	690.30 (929.95) {929.95}	693.41	77.5
	444	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5/2020	1/2024 (Oct-24) {11/2024}	882.00 (N.A.) {882.00}	737.57	71.63

Table:-7. Project List: Ongoing Projects as of 31st August 2024

445	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5/2020	7/2023 (Aug-24) {11/2024}	691.52 (903.85) {903.85}	713.63	83.5
446	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5/2020	12/2023 (Aug-24) {11/2024}	894.00 (1,210.06) {1,210.06}	873.49	80.4
447	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9/2020	2/2024 (N.A.) {1/2025}	1,542.02 (N.A.) {1,542.02}	778.07	50.51
448	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9/2020	2/2024 (Aug-24) {8/2024}	1,185.69 (N.A.) {1,185.69}	845.32	82.3
449	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11/2019	9/2023 (N.A.) {10/2024}	1,669.56 (N.A.) {1,669.56}	967.79	88.12
450	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9/2020	11/2023 (N.A.) {9/2024}	1,198.55 (N.A.) {1,198.55}	802.45	85.29
451	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11/2019	5/2024 (N.A.) {11/2024}	1,604.06 (N.A.) {1,604.06}	1,219.52	95.73
452	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3/2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	435.91	59.95

Table:-7. Project List: Ongoing Projects as of 31st August 2024

453	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3/2021	3/2024 (N.A.) {3/2025}	1,259.00 (N.A.) {1,910.00}	137.93	15.02
454	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7/2020	12/2023 (N.A.) {6/2024}	2,271.86 (N.A.) {3,916.00}	518.25	74.55
455	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7/2020	8/2023 (N.A.) {6/2024}	1,710.30 (N.A.) {1,927.00}	362.81	68.11
456	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2/2020	8/2023 (Dec-24) {9/2024}	752.30 (N.A.) {766.20}	451.11	98.14
457	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791)	2/2020	6/2023 (Mar-24) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
458	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3/2021	9/2022 (N.A.) {9/2024}	536.03 (N.A.) {536.03}	445.87	98.87
459	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3/2021	9/2022 (N.A.) {9/2024}	485.75 (N.A.) {485.75}	383.09	97.71
460	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2/2020	3/2023 (Dec-24) {9/2024}	778.15 (N.A.) {785.67}	539.42	99.52

Table:-7. Project List: Ongoing Projects as of 31st August 2024

461	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE (NHAI) (N24001827)	3/2022	3/2023 (N.A.) {7/2024}	162.73 (N.A.) {162.73}	131.79	95.3
462	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9/2022	12/2023 (Dec-25) {12/2025}	237.28 (N.A.) {237.28}	0.59	0
463	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12/2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	320.17	47.19
464	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHAI) (N24002035)	9/2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	168.49	11.45
465	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10/2022	2/2024 (Feb-26) {2/2026}	246.60 (291.00) {291.00}	29.33	15
466	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12/2022	2/2024 (Aug-25) {8/2025}	173.06 (N.A.) {219.00}	0.15	0
467	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5/2016	8/2019 (N.A.) {2/2024}	998.18 (N.A.) {998.18}	802.04	100
468	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5/2016	9/2019 (May-24) {10/2024}	723.64 (N.A.) {723.64}	559.55	95.98

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		469	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5/2016	8/2019 (N.A.) {10/2024}	763.08 (N.A.) {763.08}	507.35	95.18
		470	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7/2016	7/2020 (N.A.) {10/2024}	829.97 (N.A.) {829.97}	457.75	92.2
		471	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1/2017	12/2020 (Jun-25) {6/2025}	1,251.11 (1,527.75) {1,527.75}	683.63	83.84
		472	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3/2018	10/2021 (Sep-24) {9/2024}	1,161.39 (1,404.00) {1,404.00}	418.51	39.17
		473	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10/2018	11/2020 (Sep-24) {9/2024}	400.76 (394.44) {394.44}	287.39	87
	URBAN DEVELOPMENT I	474	AHMEDABAD METRO RAIL PROJECT PHASE 1 (MEGA) (N28000122)	11/2014	12/2018 (N.A.) {8/2024}	10,773.00 (N.A.) {12,924.55}	12,277.42	99.76
		475	AHMEDABAD METRO RAIL PROJECT PHASE II (MEGA) (N28000137)	3/2019	3/2024 (N.A.) {12/2024}	5,384.17 (N.A.) {5,384.17}	3,321.18	71.4
		476	SURAT METRO RAIL PROJECT (MEGA) (N28000138)	3/2019	3/2024 (N.A.) {10/2025}	12,020.32 (N.A.) {12,020.32}	5,290.12	51.41
HARYANA	HEALTH AND FAMILY WELFARE	477	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3/2019	3/2023 (Mar-26) {3/2026}	1,294.34 (1,294.34) {1,294.34}	97.69	2.08

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>HOME AFFAIRS</u>	478	C/o separate family accommodation (Phase-I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1/2020	10/2023 (Jan-25) {1/2025}	166.98 (167.00) {166.98}	98.45	87.5
<u>PETROLEUM</u>	479	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6/2019	12/2022 (Jul-25) {7/2025}	2,281.94 (3,219.94) {3,219.94}	1,538.12	60.2
	480	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA (IOCL) (N16000412)	2/2021	9/2024 (Dec-25) {12/2025}	34,627.00 (38,231.00) {38,231.00}	12,865.84	70.4
	481	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3/2022	3/2025 (N.A.) {12/2025}	1,459.00 (2,102.79) {2,102.79}	356.29	36.7
<u>RAILWAYS</u>	482	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2/2023	2/2028 (N.A.) {2/2026}	471.06 (N.A.) {471.06}	35.94	18
	483	DOUBLING BETWEEN REWARI-KATHUWAS (27.73 KM) (NWR) (N22000606)	2/2023	6/2027 (N.A.) {6/2025}	352.41 (N.A.) {352.41}	29.55	12
<u>ROAD TRANSPORT AND HIGHWAYS</u>	484	CONSTRUCTION OF 4-LANE NH-344P-PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11/2021	11/2023 (Jan-24) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100
	485	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11/2020	12/2023 (N.A.) {10/2024}	1,690.23 (N.A.) {2,010.17}	1,305.28	93.01
	486	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12/2020	1/2024 (Apr-24) {9/2024}	1,334.04 (N.A.) {1,334.00}	974.53	93.55

Table:-7. Project List: Ongoing Projects as of 31st August 2024

487	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHAI) (N24001535)	7/2020	7/2022 (May-24) {10/2024}	899.00 (1,882.46) {1,882.46}	1,123.98	91.5
488	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHAI) (N24001536)	7/2020	7/2022 (N.A.) {10/2024}	817.00 (1,605.00) {1,605.00}	1,025.56	96.05
489	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-III) F (NHAI) (N24001633)	12/2020	12/2023 (Feb-24) {9/2024}	1,430.88 (N.A.) {1,430.88}	1,015.55	95.72
490	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-IV) FRO (NHAI) (N24001634)	1/2021	12/2023 (Mar-24) {9/2024}	1,306.95 (N.A.) {1,306.95}	942.41	94.83
491	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHAI) (N24001635)	3/2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	172.00	44
492	SIX LANNING OF MANDI DABWALI (PUNJAB/HARYANA BORDER)-CHAUTALA ROAD SECTION FROM PROPOSED MANDI DABW (NHAI) (N24001672)	1/2021	1/2024 (Apr-24) {4/2024}	864.27 (864.00) {864.27}	533.44	99.96
493	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHAI) (N24001673)	3/2020	3/2023 (Nov-24) {11/2024}	510.97 (N.A.) {510.97}	529.00	87.85
494	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH-352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12/2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,059.96	56.58

Table:-7. Project List: Ongoing Projects as of 31st August 2024

495	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH-11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2/2020	1/2023 (Dec-24) {12/2024}	808.31 (N.A.) {958.00}	804.37	99.42
496	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) (NHAI) (N24001780)	1/2018	11/2020 (Dec-24) {3/2024}	2,228.00 (N.A.) {2,228.00}	1,411.27	100
497	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11/2018	9/2021 (N.A.) {9/2024}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95
498	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA (NHAI) (N24001784)	11/2018	9/2021 (N.A.) {9/2024}	1,935.61 (N.A.) {1,935.61}	856.41	99.9
499	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA-KO (NHAI) (N24002037)	1/2023	12/2025 (N.A.) {12/2025}	609.32 (609.00) {609.00}	53.68	18.5
500	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11/2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	590.64	40
501	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2/2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	316.25	27.23
502	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4/2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	409.06	36.1

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		503	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4/2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	606.10	35.22
		504	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11/2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	116.57	36.02
		505	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH ? 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3/2022	6/2025 (N.A.) {6/2025}	927.22 (N.A.) {927.22}	352.64	50.47
		506	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6/2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	111.00	67
		507	6L ACCESS CONTROLLED HIGHWAY FROM JN WITH JAIPUR PUSHTA ROAD TO JN WITH SECTOR 62/65 DIVIDING ROAD (NHAI) (N24002047)	5/2020	8/2023 (N.A.) {9/2024}	1,328.07 (2,346.00) {2,346.00}	1,078.73	96.22
		508	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7/2022	6/2025 (N.A.) {6/2025}	2,414.67 (2,898.00) {2,898.00}	1,028.35	22.7
		509	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P (NHAI) (N24000835)	3/2018	12/2020 (Dec-24) {3/2024}	1,484.30 (N.A.) {2,182.41}	1,237.02	100
HIMACHAL PRADESH	DEPARTMENT OF HIGHER EDUCATION	510	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9/2018	6/2022 (Dec-24) {4/2024}	392.51 (N.A.) {446.43}	292.90	87.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	511	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3/2021	8/2022 (Nov-24) {11/2024}	512.37 (512.37) {512.37}	100.00	50
<u>HEALTH AND FAMILY WELFARE</u>	512	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH (CPWD FOR HEALTH) (N28000127)	12/2018	6/2021 (Aug-26) {8/2026}	260.00 (371.78) {371.78}	46.24	7
<u>POWER</u>	513	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9/2002	9/2009 (N.A.) {12/2024}	3,919.59 (N.A.) {12,160.00}	11,795.93	97.86
	514	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11/2020	1/2026 (N.A.) {6/2027}	1,810.56 (N.A.) {3,060.71}	1,505.33	50.99
	515	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10/2020	11/2025 (N.A.) {5/2026}	687.97 (N.A.) {687.97}	674.64	59.29
	516	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1/2023	4/2028 (N.A.) {4/2028}	2,614.51 (N.A.) {2,614.51}	707.66	23.95
<u>RAILWAYS</u>	517	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4/2008	12/2026 (N.A.) {3/2025}	2,966.99 (N.A.) {6,753.42}	5,190.99	49
<u>ROAD TRANSPORT AND HIGHWAYS</u>	518	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2/2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	147.63	80
	519	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR-KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8/2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	30.75	13

Table:-7. Project List: Ongoing Projects as of 31st August 2024

520	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8/2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	9.45	0
521	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3/2021	12/2024 (Dec-24) {12/2024}	1,322.95 (1,442.47) {1,442.47}	761.84	77.73
522	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5/2022	3/2024 (Dec-24) {12/2024}	469.95 (N.A.) {280.00}	265.33	94.09
523	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2/2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100
524	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4/2021	6/2024 (N.A.) {9/2024}	583.93 (704.30) {704.30}	170.54	97.99
525	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3/2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.79}	188.76	40.9
526	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7/2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.6
527	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3/2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	0.00	20

Table:-7. Project List: Ongoing Projects as of 31st August 2024

528	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (<i>BRO</i>) (N24001916)	3/2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	0.00	29
529	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (<i>NHAI</i>) (N24002049)	3/2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.5
530	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (<i>NHAI</i>) (N24002050)	2/2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	326.83	35.05
531	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (<i>NHAI</i>) (N24002051)	7/2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	268.70	43.26
532	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (<i>NHAI</i>) (N24002052)	2/2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	866.43	44.07
533	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (<i>NHAI</i>) (N24000613)	9/2016	7/2020 (N.A.) {8/2024}	1,273.71 (N.A.) {1,478.61}	1,383.00	92.14
534	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (<i>NHAI</i>) (N24000852)	3/2018	5/2021 (Dec-24) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83
535	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (<i>MoRTH</i>) (N24001381)	8/2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	132.82	97.43

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		536	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8/2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	81.08	83
		537	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8/2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100
	URBAN DEVELOPMENT I	538	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4/2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	0
JAMMU AND KASHMIR	CIVIL AVIATION	539	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7/2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	47.29	9
	DEPARTMENT OF HIGHER EDUCATION	540	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3/2019	7/2022 (Aug-24) {8/2024}	424.93 (500.91) {500.91}	467.62	98
		541	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1/2018	4/2023 (Sep-24) {9/2024}	676.00 (1,148.68) {1,144.68}	64.75	94
	HEALTH AND FAMILY WELFARE	542	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3/2019	9/2025 (Jan-25) {11/2025}	1,828.00 (1,577.00) {1,577.00}	1,068.37	54
		543	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3/2019	9/2023 (Oct-24) {10/2024}	1,404.00 (1,642.00) {1,642.00}	1,398.50	99.5
	PETROLEUM	544	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4/2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	439.00	43

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	545	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3/2022	3/2032 (Sep-34) {9/2034}	538.00 (N.A.) {538.00}	4.21	0.2
<u>POWER</u>	546	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10/2014	4/2020 (Jul-25) {9/2026}	8,112.12 (N.A.) {8,112.12}	4,790.15	56.88
	547	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3/2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {4,287.59}	1,768.22	40.78
	548	RATLE HE PROJECT (NHPC) (N18000324)	2/2021	2/2026 (N.A.) {12/2026}	5,281.94 (N.A.) {5,281.94}	755.36	15.02
	549	KWAR HE PROJECT (CVPPPL) (N18000363)	5/2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	722.15	11.8
<u>RAILWAYS</u>	550	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (NR) (220100133)	3/1995	11/2002 (Dec-24) {12/2024}	2,500.00 (37,012.26) {41,000.00}	40,599.27	99
<u>ROAD TRANSPORT AND HIGHWAYS</u>	551	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7/2021	8/2023 (Jul-24) {12/2025}	859.67 (N.A.) {859.67}	145.18	33.88
	552	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7/2021	2/2023 (Jul-24) {6/2025}	497.09 (N.A.) {497.09}	142.12	70.29
	553	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2/2021	3/2023 (Mar-24) {11/2024}	431.28 (N.A.) {431.28}	284.34	84.5
	554	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9/2021	12/2023 (Oct-24) {10/2024}	811.19 (N.A.) {811.19}	798.34	38

Table:-7. Project List: Ongoing Projects as of 31st August 2024

555	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3/2021	2/2024 (Aug-24) {6/2025}	2,919.96 (N.A.) {2,919.96}	2,110.25	55.6
556	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7/2022	1/2025 (N.A.) {1/2025}	245.34 (N.A.) {245.34}	46.36	30.45
557	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH-4 (NHAI) (N24001550)	9/2021	9/2024 (Sep-25) {9/2025}	1,821.72 (1,917.32) {1,917.32}	699.75	56.5
558	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5) (NHAI) (N24001551)	10/2021	9/2024 (Jul-25) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,222.55	43.01
559	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHAI) (N24001552)	10/2021	9/2024 (Jul-25) {7/2025}	2,714.95 (2,714.95) {2,714.95}	1,459.77	64.01
560	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHAI) (N24001619)	8/2022	6/2024 (Jun-25) {6/2025}	200.05 (200.05) {208.92}	93.73	37.5
561	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM 130.550 TO KM.130.750; KM. (NHAI) (N24001620)	9/2021	10/2023 (May-25) {5/2025}	442.14 (N.A.) {442.14}	235.17	19.88
562	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHAI) (N24001621)	7/2021	8/2024 (Jun-25) {6/2025}	614.48 (N.A.) {614.48}	140.53	7

Table:-7. Project List: Ongoing Projects as of 31st August 2024

563	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHAI) (N24001622)	7/2021	6/2024 (Jun-25) {6/2025}	1,401.87 (N.A.) {1,401.87}	472.31	
564	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHAI) (N24001623)	1/2020	1/2024 (Dec-24) {12/2024}	336.01 (N.A.) {336.01}	168.91	34
565	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7/2019	10/2020 (Apr-23) {9/2024}	157.05 (N.A.) {157.05}	134.59	100
566	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7/2021	2/2025 (Feb-25) {2/2025}	1,912.17 (N.A.) {1,912.17}	37.21	
567	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7/2022	3/2025 (N.A.) {3/2025}	198.28 (N.A.) {198.28}	58.65	45.18
568	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3/2021	7/2024 (N.A.) {7/2024}	642.24 (N.A.) {642.24}	423.60	82
569	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7/2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	163.15	77
570	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2/2021	7/2024 (N.A.) {7/2024}	395.25 (N.A.) {395.25}	179.60	50

Table:-7. Project List: Ongoing Projects as of 31st August 2024

571	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3/2020	8/2024 (N.A.) {8/2024}	796.97 (N.A.) {796.97}	432.40	73
572	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3/2020	9/2023 (N.A.) {9/2024}	152.93 (N.A.) {152.93}	98.08	75
573	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3/2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	204.55	33.89
574	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6/2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	252.09	17
575	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9/2022	6/2026 (N.A.) {6/2026}	1,183.60 (N.A.) {1,183.60}	119.57	2
576	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3/2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {1,107.00}	77.75	12.15
577	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8/2022	6/2025 (N.A.) {6/2025}	2,474.47 (N.A.) {2,675.93}	715.42	17.5
578	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10/2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	17.26	4

Table:-7. Project List: Ongoing Projects as of 31st August 2024

579	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12/2015	12/2018 (Oct-24) {10/2024}	2,136.97 (2,644.00) {2,644.00}	2,376.13	99.5
580	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12/2017	7/2021 (Sep-24) {9/2024}	1,471.75 (1,471.75) {1,903.98}	1,603.30	96.86
581	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU- AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3/2018	7/2021 (Aug-23) {12/2024}	253.44 (N.A.) {253.44}	178.06	77.54
582	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA (NHIDCL) (N24001253)	12/2019	12/2023 (N.A.) {7/2024}	2,680.42 (N.A.) {2,680.42}	0.00	95.05
583	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG Bi-D (NHIDCL) (N24001256)	8/2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
584	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL (NHIDCL) (N24001264)	7/2020	4/2022 (Mar-24) {12/2024}	228.39 (N.A.) {228.39}	63.12	84.7
585	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7/2020	4/2022 (Nov-23) {12/2024}	210.79 (N.A.) {210.79}	64.28	86.17
586	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3/2021	9/2022 (Aug-23) {10/2024}	486.45 (N.A.) {486.45}	120.08	94.18
587	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3/2021	12/2022 (Jul-24) {10/2024}	398.51 (N.A.) {398.51}	75.26	90.05

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		588	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342)	3/2021	12/2022 (N.A.) {7/2024}	260.40 (N.A.) {260.40}	191.88	93.8
		589	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7/2021	2/2023 (N.A.) {12/2025}	512.43 (N.A.) {512.43}	65.31	48.07
JHARKHAND	COAL	590	CHURI BENTI UG (0.81 MTY) (CCL) (N06000083)	8/2007	3/2011 (N.A.) {10/2024}	163.51 (N.A.) {163.51}	133.35	84.4
		591	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12/2009	3/2016 (N.A.) {3/2025}	510.85 (N.A.) {510.85}	488.31	74.5
		592	MURADIDH UG TURN-KEY PROJECT (BCCL) (N06000096)	2/2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	151.19	70
		593	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8/2011	3/2019 (N.A.) {2/2026}	1,230.27 (N.A.) {1,230.27}	591.37	80
		594	MADHUBAND NLW WASHERY (BCCL) (N06000126)	8/2010	5/2014 (N.A.) {11/2023}	289.45 (N.A.) {302.00}	299.73	100
		595	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8/2018	3/2024 (Mar-26) {3/2026}	513.98 (N.A.) {513.98}	181.32	51
		596	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11/2019	3/2023 (N.A.) {3/2025}	243.52 (N.A.) {243.52}	44.35	46.6
		597	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7/2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	220.23	43

Table:-7. Project List: Ongoing Projects as of 31st August 2024

598	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10/2015	4/2018 (N.A.) {6/2025}	334.27 (N.A.) {334.27}	113.87	40
599	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8/2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,242.16	19
600	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8/2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	683.55	19
601	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7/2021	3/2026 (N.A.) {3/2026}	778.80 (N.A.) {778.80}	683.05	75
602	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8/2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	362.06	38
603	CHANDRAGUPT OCP (CCL) (N06000238)	8/2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	7.95	12.4
604	SIRKA OCP (CCL) (N06000239)	5/2020	3/2025 (N.A.) {3/2025}	222.82 (N.A.) {222.82}	139.31	60
605	JHARKHAND LAIYO OCP (CCL) (N06000240)	8/2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	20
606	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11/2020	3/2025 (N.A.) {3/2025}	230.41 (N.A.) {230.41}	18.14	18.3
607	EPR PUNDI OCP (CCL) (N06000242)	11/2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	39

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	608	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1/2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	82.92	11.7
	609	EXPANSION OF KONAR OCP (CCL) (N06000245)	1/2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	384.03	32
	610	EXPANSION OF KARO OCP (CCL) (N06000246)	1/2022	3/2026 (N.A.) {3/2026}	908.47 (N.A.) {908.47}	145.14	17.2
	611	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5/2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	175.01	12.1
	612	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1/2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	389.65	24
	613	HURA C OC (ECL) (N06000275)	8/2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	32.38	0
DEPARTMENT OF HIGHER EDUCATION	614	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9/2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	175.01	
PETROLEUM	615	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239)	12/2015	3/2023 (Mar-24) {3/2025}	823.27 (1,137.79) {1,137.79}	1,045.36	83.1
	616	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11/2019	1/2024 (Mar-24) {12/2024}	431.00 (N.A.) {431.00}	162.25	56.2
	617	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3/2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	45.05	33.23

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	618	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6/2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	173.21	16.8
POWER	619	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2/2014	6/2019 (Oct-22) {12/2024}	16,242.90 (N.A.) {17,007.00}	15,361.62	85
	620	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11/2017	3/2023 (N.A.) {11/2025}	17,112.00 (N.A.) {17,112.00}	13,151.45	68
	621	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2/2019	10/2024 (N.A.) {10/2024}	501.79 (N.A.) {501.79}	40.35	0
	622	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9/2015	11/2019 (N.A.) {11/2019}	1,553.00 (N.A.) {2,804.00}	0.00	
	623	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4/2002	(N.A.) {3/2025}	459.91 (1,625.87) {1,700.00}	1,746.64	70
RAILWAYS	624	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3/2016	3/2021 (N.A.) {6/2026}	1,724.20 (3,029.04) {3,029.04}	2,135.44	78
	625	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4/2018	6/2022 (N.A.) {6/2026}	428.65 (N.A.) {472.50}	267.53	2
	626	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11/2022	11/2027 (N.A.) {11/2027}	202.00 (349.22) {349.22}	5.26	
	627	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12/2015	3/2025 (N.A.) {3/2025}	1,116.00 (N.A.) {3,270.07}	2,875.04	98

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	628	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11/2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,630.47	90
	629	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3/2017	3/2024 (N.A.) {3/2025}	262.71 (N.A.) {262.71}	192.40	73
	630	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1/2018	12/2025 (N.A.) {12/2025}	487.73 (N.A.) {487.73}	277.28	16
ROAD TRANSPORT AND HIGHWAYS	631	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9/2020	3/2024 (Dec-24) {12/2024}	755.26 (N.A.) {1,039.00}	544.02	82.5
	632	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KHAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9/2020	10/2023 (Dec-24) {12/2024}	748.99 (N.A.) {903.00}	803.50	99.98
	633	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2/2022	1/2025 (N.A.) {1/2025}	534.73 (N.A.) {534.73}	0.00	59.96
	634	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHAI) (N24001595)	8/2020	3/2024 (N.A.) {10/2024}	1,034.00 (1,785.18) {1,785.18}	41.50	79.91
	635	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHAI) (N24001596)	11/2021	7/2023 (Jun-25) {6/2025}	1,302.72 (N.A.) {1,302.72}	798.50	53.91
	636	BALANCE WORK OF RANCHI-MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG- (NHAI) (N24001597)	1/2019	12/2020 (Jul-24) {7/2024}	466.55 (518.00) {466.55}	0.00	99.25

Table:-7. Project List: Ongoing Projects as of 31st August 2024

637	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHAI) (N24001854)	6/2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,324.95}	608.19	40
638	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2/2020	8/2023 (Jun-24) {6/2024}	153.01 (N.A.) {153.01}	83.60	96.3
639	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1/2022	7/2024 (N.A.) {7/2024}	315.21 (N.A.) {315.21}	59.59	50
640	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3/2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	0.00	0
641	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3/2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	0
642	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4/2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	343.02	45.1
643	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH-75 PKG SEC-III (NHAI) (N24002054)	10/2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	196.32	50.04
644	FOUR LANING OF BASUKINATH-DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3/2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	645	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6/2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	362.33	23.47
	646	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12/2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	
	647	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 (NHAI) (N24000725)	1/2018	11/2021 (Aug-24) {8/2024}	273.46 (N.A.) {276.17}	244.92	95
	648	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1/2018	11/2021 (Jun-25) {6/2025}	1,155.16 (N.A.) {950.49}	629.74	69
	649	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K (NHAI) (N24000854)	3/2018	3/2021 (Dec-24) {12/2024}	1,005.08 (1,073.10) {1,073.10}	699.05	81
	650	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12/2016	9/2021 (Jun-24) {6/2024}	196.00 (N.A.) {196.00}	163.97	90
STEEL	651	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3/2015	10/2017 (Dec-21) {8/2026}	1,034.01 (N.A.) {1,034.01}	871.45	51.73
	652	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9/2023	7/2025 (N.A.) {7/2025}	513.82 (N.A.) {513.82}	73.44	32
	653	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11/2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	45.51	15

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		654	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (<i>SAIL</i>) (<i>N12000135</i>)	3/2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	0.00	1
KARNATAKA	CIVIL AVIATION	655	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (<i>AAI</i>) (<i>N04000105</i>)	6/2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	35.11	10.5
		656	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (<i>AAI</i>) (<i>N04000108</i>)	6/2023	2/2026 (N.A.) {1/2026}	320.47 (N.A.) {320.47}	11.04	10
	DEPARTMENT OF HIGHER EDUCATION	657	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (<i>CPWD EDUCATION</i>) (<i>N42000006</i>)	7/2019	3/2022 (Oct-22) {3/2023}	851.00 (851.00) {851.00}	886.26	100
		658	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (<i>CPWD</i>) (<i>N42000010</i>)	8/2021	2/2024 (Nov-24) {11/2024}	316.25 (N.A.) {316.25}	333.42	
	PETROLEUM	659	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (<i>HPCL</i>) (<i>N16000369</i>)	12/2018	12/2022 (Sep-24) {9/2024}	854.00 (854.00) {854.00}	601.58	88
		660	DEVANGONTHI MARKETING TERMINAL (<i>MANGALORE REFIN</i>) (<i>N16000401</i>)	6/2020	6/2023 (Mar-24) {8/2024}	200.00 (304.00) {304.00}	255.87	100
		661	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (<i>IOCL</i>) (<i>N16000437</i>)	1/2022	7/2025 (Dec-25) {12/2025}	463.00 (500.62) {500.62}	165.39	55.4
		662	POWER SYSTEM UPGRADATION PROJECT (<i>MANGALORE REFIN</i>) (<i>N16000509</i>)	10/2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	57.52	27.65

Table:-7. Project List: Ongoing Projects as of 31st August 2024

POWER	663	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A&B) AND GADAG II (PHASE A) IN KARNATAK (PGCIL) (N18000385)	12/2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	0.00	0
	664	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2/2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	0.00	3
RAILWAYS	665	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4/2011	(N.A.) {12/2027}	1,801.01 (N.A.) {1,801.01}	305.09	11
	666	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4/2010	3/2016 (N.A.) {12/2026}	986.30 (1,378.00) {1,378.00}	532.54	34
	667	HOSPET-HUBLI-LONDA-VASCODAGAMA DL (RVNL) (N22000297)	4/2010	3/2023 (N.A.) {12/2026}	2,127.00 (N.A.) {3,692.60}	3,481.82	86
	668	GADAG-WADI NL (SWR) (N22000299)	4/2013	12/2018 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,197.98	28
	669	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4/2012	3/2016 (N.A.) {6/2026}	279.54 (296.72) {296.72}	95.96	14
	670	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) (SWR) (N22000486)	3/1996	3/2017 (N.A.) {12/2025}	644.78 (825.31) {825.31}	575.06	66
	671	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4/2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	0
	672	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (NCRTC) (N22000543)	4/2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	673	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (SWR) (N22000557)	9/2020	3/2026 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.36	
	674	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000558)	6/2019	4/2028 (N.A.) {12/2027}	663.03 (748.85) {748.85}	0.34	1
	675	SHIMOGA-SHIKARIPURA-RANEENNUR (UMBRELLA WORK PB#23/2018-19/NR) (SWR) (N22000559)	9/2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	65.53	5
	676	BANGALORE-WHITEFIELD-BANGALORE CITY-KRISHNARAJAPURAM QUADRUPLING (SWR) (N22000621)	3/2018	3/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	169.03	46
<u>ROAD TRANSPORT AND HIGHWAYS</u>	677	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3/2021	11/2021 (Mar-25) {3/2025}	1,100.88 (1,713.98) {1,713.98}	896.43	63.25
	678	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3/2021	10/2021 (Mar-25) {3/2025}	317.90 (576.32) {576.32}	339.63	94.5
	679	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1/2022	4/2025 (Apr-25) {4/2025}	1,388.70 (1,388.70) {1,388.70}	299.54	47.3
	680	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3/2018	12/2022 (Jun-25) {6/2025}	440.16 (N.A.) {440.16}	301.02	63.75
	681	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2/2023	2/2025 (N.A.) {2/2025}	1,240.60 (N.A.) {1,240.60}	612.56	51.94

Table:-7. Project List: Ongoing Projects as of 31st August 2024

682	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11/2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	540.35	95.44
683	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12/2022	6/2025 (N.A.) {6/2025}	2,718.46 (N.A.) {2,718.46}	274.90	31.2
684	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11/2022	5/2024 (May-24) {5/2024}	226.76 (226.76) {226.76}	70.45	51.51
685	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10/2022	4/2025 (Apr-25) {4/2025}	1,479.30 (1,479.30) {1,479.30}	385.46	57.49
686	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3/2021	10/2024 (Jun-25) {6/2025}	1,409.68 (N.A.) {1,409.68}	789.18	41.9
687	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8/2022	8/2025 (Aug-25) {12/2025}	2,032.15 (2,032.15) {2,032.15}	159.83	42.9
688	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	3/2022	3/2024 (Jan-25) {1/2025}	294.62 (N.A.) {294.62}	31.76	12.8
689	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9/2021	4/2023 (Dec-24) {12/2024}	912.37 (N.A.) {424.16}	326.36	97.2
690	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9/2020	1/2023 (Sep-20) {5/2025}	688.00 (602.09) {688.00}	463.32	75.26

Table:-7. Project List: Ongoing Projects as of 31st August 2024

691	CONSTRUCTION OF 4 LANE BANGALORE -CHENNAI EXPRESSWAY FROM KM 53.500 TO KM 71.000 SECTION OF NE-7 (BA (NHAI) (N24001685)	1/2021	1/2024 (May-24) {9/2024}	1,069.00 (N.A.) {1,067.89}	827.38	99.78
692	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3/2021	3/2023 (Oct-24) {10/2024}	1,065.06 (1,444.50) {1,444.50}	157.31	88.92
693	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10/2021	10/2023 (Oct-24) {3/2025}	1,331.77 (2,082.98) {2,082.98}	318.47	68.1
694	CONSTRUCTION OF 4 LANE BANGALORE-CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE- 7(ALONG WITH 0.700 (NHAI) (N24001688)	10/2020	9/2023 (Mar-24) {9/2024}	3,184.00 (N.A.) {2,867.98}	1,164.41	98.53
695	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M (NHAI) (N24001689)	12/2020	9/2023 (Mar-24) {9/2024}	1,745.00 (N.A.) {1,595.20}	1,251.74	98.44
696	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A (NHAI) (N24001690)	1/2021	1/2023 (Dec-23) {3/2025}	1,167.52 (1,157.00) {1,167.52}	946.27	88.01
697	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10/2019	10/2021 (Oct-24) {10/2024}	1,225.24 (1,505.85) {1,505.85}	77.12	93.55
698	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3/2021	3/2023 (Jul-24) {7/2024}	344.79 (N.A.) {344.79}	10.00	90

Table:-7. Project List: Ongoing Projects as of 31st August 2024

699	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2/2023	2/2024 (Feb-25) {2/2025}	398.48 (N.A.) {398.48}	5.00	50
700	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6/2021	6/2024 (Jun-25) {6/2025}	298.00 (N.A.) {298.00}	10.70	52
701	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1/2023	1/2026 (Sep-25) {9/2025}	166.58 (N.A.) {166.58}	3.54	0
702	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1/2023	1/2025 (Jan-25) {1/2025}	350.69 (N.A.) {350.69}	10.00	56
703	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9/2022	3/2024 (Jan-25) {1/2025}	172.98 (N.A.) {172.98}	6.48	65
704	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANGES KM 112.750 TO (MoRTH) (N24001944)	1/2023	6/2024 (Jul-24) {7/2024}	255.88 (N.A.) {255.88}	60.99	78
705	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8/2022	2/2024 (Dec-24) {12/2024}	170.34 (N.A.) {170.34}	4.25	72
706	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11/2022	11/2024 (Nov-24) {11/2024}	218.93 (N.A.) {218.93}	10.00	95

Table:-7. Project List: Ongoing Projects as of 31st August 2024

707	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2/2023	2/2025 (Feb-25) {2/2025}	177.94 (N.A.) {177.94}	6.66	47
708	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10/2022	10/2024 (Dec-24) {12/2024}	355.72 (N.A.) {355.72}	11.32	60
709	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3/2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	396.52	45.3
710	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12/2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	400.00	42
711	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5/2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	223.03	43.52
712	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12/2021	6/2024 (Dec-24) {12/2024}	516.96 (N.A.) {516.96}	19.93	70
713	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3/2023	3/2025 (Mar-25) {3/2025}	718.52 (N.A.) {718.52}	24.81	23
714	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA- SANKESWAR SE (MoRTH) (N24002013)	3/2021	2/2022 (Oct-24) {10/2024}	766.64 (N.A.) {766.64}	13.55	75

Table:-7. Project List: Ongoing Projects as of 31st August 2024

715	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (MoRTH) (N24000334)	3/2015	11/2015 (Aug-24) {8/2024}	165.67 (N.A.) {165.67}	126.47	99
716	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (NHAI) (N24000462)	5/2014	8/2016 (Dec-24) {12/2024}	1,655.01 (2,639.00) {2,639.00}	1,822.06	97.8
717	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (NHAI) (N24000552)	3/2016	3/2019 (Dec-23) {3/2025}	701.40 (591.86) {701.40}	428.98	77
718	HOSPET-BELLARY-KARNATAKA AP BORDER (NHAI) (N24000603)	8/2016	3/2019 (May-25) {5/2025}	1,167.42 (N.A.) {1,224.01}	790.15	75.6
719	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM (NHAI) (N24000622)	9/2016	8/2019 (Jun-24) {9/2024}	950.69 (1,487.46) {2,525.02}	1,895.61	99.11
720	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS ? PA (MoRTH) (N24001156)	1/2017	9/2017 (May-23) {5/2023}	166.67 (N.A.) {264.34}	192.08	100
721	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8/2016	2/2017 (Jul-24) {7/2024}	175.50 (N.A.) {241.60}	189.72	90
722	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3/2018	6/2019 (Dec-23) {12/2023}	159.97 (N.A.) {242.61}	113.15	100
723	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1/2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

724	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9/2017	10/2018 (Apr-22) {4/2022}	191.60 (N.A.) {191.60}	112.03	100
725	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12/2017	1/2019 (Apr-22) {4/2022}	297.30 (N.A.) {318.28}	280.25	100
726	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3/2018	10/2018 (Nov-22) {11/2022}	325.86 (N.A.) {386.41}	356.78	100
727	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10/2016	3/2017 (Jul-22) {7/2022}	396.96 (N.A.) {396.96}	329.58	100
728	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11/2016	3/2017 (Oct-21) {10/2021}	314.90 (N.A.) {314.90}	233.95	100
729	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3/2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98
730	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5/2018	5/2018 (Dec-23) {12/2023}	171.60 (N.A.) {171.60}	134.81	100
731	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1/2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		732	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI ? JADERCELA SECTION (MoRTH) (N24001173)	2/2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	62.31	60
		733	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1/2017	9/2017 (May-23) {5/2023}	264.34 (N.A.) {264.34}	201.07	100
		734	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3/2019	12/2019 (Nov-24) {11/2024}	423.15 (N.A.) {423.15}	284.58	82
	URBAN DEVELOPMENT I	735	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRL) (N28000058)	2/2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89
		736	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRL) (N28000151)	6/2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30
KERALA	CIVIL AVIATION	737	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6/2023	9/2025 (N.A.) {9/2025}	323.98 (N.A.) {323.98}	0.00	2
	DEPARTMENT OF HIGHER EDUCATION	738	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7/2019	3/2021 (Mar-23) {11/2025}	753.63 (N.A.) {753.63}	412.37	66
	HEALTH AND FAMILY WELFARE	739	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) (CPWD FOR HEALTH) (N28000112)	9/2017	3/2020 (May-24) {9/2024}	150.29 (N.A.) {162.00}	148.60	99.25

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>PETROLEUM</u>	740	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3/2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	74.24	58.7
	741	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12/2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	19.90	3.7
<u>RAILWAYS</u>	742	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2/2015	(Dec-26) {12/2026}	1,431.90 (3,785.45) {3,785.45}	3,097.41	30
	743	TURAVUR-AMBALAPUZHA DOUBLING (SR) (N22000400)	2/2015	(N.A.) {3/2025}	1,000.00 (N.A.) {1,416.49}	1.63	
	744	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12/2010	3/2028 (Jul-26) {7/2026}	600.82 (595.39) {595.39}	270.57	0.5
	745	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12/2011	8/2023 (Sep-26) {9/2026}	812.85 (802.80) {802.80}	258.69	0.5
<u>ROAD TRANSPORT AND HIGHWAYS</u>	746	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8/2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	465.76	32.78
	747	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12/2021	2/2025 (Feb-25) {2/2025}	3,273.61 (N.A.) {3,273.61}	423.59	44.25
	748	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH-66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12/2021	1/2025 (Aug-25) {8/2025}	3,635.64 (N.A.) {3,635.64}	275.13	35.8

Table:-7. Project List: Ongoing Projects as of 31st August 2024

749	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9/2021	9/2024 (Mar-26) {9/2024}	2,878.97 (N.A.) {2,878.97}	328.17	25.7
750	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3/2020	6/2022 (Feb-24) {8/2024}	210.37 (216.94) {216.94}	198.10	99.4
751	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH ?66 (OLD NH-17) FROM DESIGN CHAINAGE 397+750 (O (NHAI) (N24001653)	11/2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,905.52	42.24
752	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6/2021	3/2025 (Feb-25) {2/2025}	2,641.37 (N.A.) {2,641.37}	385.44	49.92
753	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHAI) (N24001655)	6/2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	2,982.18	49.7
754	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH ? 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHAI) (N24001656)	6/2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	2,916.74	42.98
755	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHAI) (N24001657)	6/2021	10/2024 (Dec-25) {12/2025}	2,842.14 (N.A.) {2,842.14}	379.06	54.95
756	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHAI) (N24001658)	1/2021	7/2024 (Mar-25) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,246.86	80.1

Table:-7. Project List: Ongoing Projects as of 31st August 2024

757	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD-SECTION OF NH-66(OLD NH-17) FROM DESIGN CH (NHAI) (N24001659)	2/2021	7/2024 (Mar-25) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,137.79	82
758	SIX LANING OF THALIPARAMBHA-MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHAI) (N24001660)	8/2020	2/2024 (Nov-21) {12/2025}	2,714.60 (3,319.41) {2,714.60}	1,691.38	58.18
759	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHAI) (N24001661)	10/2020	4/2024 (May-25) {12/2025}	3,219.47 (3,713.14) {3,713.14}	2,078.78	44.06
760	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5/2020	5/2024 (Nov-21) {3/2025}	1,981.07 (2,467.68) {1,981.07}	1,368.26	74.65
761	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6/2020	4/2024 (Oct-21) {12/2025}	3,041.65 (3,799.76) {3,041.65}	2,033.02	50.8
762	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6/2020	4/2024 (Oct-21) {11/2025}	1,746.45 (2,377.88) {1,746.45}	1,125.92	58.48
763	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L/@L+PS SECTION IN TH (NHAI) (N24002074)	8/2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	76.29	16.8
764	4-LANNING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704)	9/2017	5/2020 (Nov-23) {2/2024}	1,124.11 (1,568.00) {1,568.00}	1,521.71	100
765	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2/2018	2/2023 (Dec-24) {3/2025}	1,424.77 (1,862.77) {1,862.77}	671.44	74.38

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		766	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (<i>MoRTH</i>) (<i>N24001369</i>)	2/2017	8/2017 (Mar-22) {8/2024}	294.28 (296.53) {296.53}	285.30	98
		767	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (<i>MoRTH</i>) (<i>N24001370</i>)	2/2017	9/2017 (Jan-23) {8/2024}	380.76 (372.87) {372.87}	337.83	100
	URBAN DEVELOPMEN I	768	KOCHI METRO RAIL PROJECT (<i>KMRCL</i>) (<i>N28000081</i>)	7/2012	7/2017 (Sep-20) {9/2020}	5,181.79 (N.A.) {6,218.14}	6,059.17	100
		769	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (<i>KMRCL</i>) (<i>N28000158</i>)	7/2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	2.81	0
		770	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPIUNITHURA (<i>KMRCL</i>) (<i>N28000159</i>)	6/2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	0
	LADAKH	CIVIL AVIATION	771	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (<i>AAI</i>) (<i>N04000078</i>)	7/2018	9/2021 (Oct-24) {3/2025}	480.33 (N.A.) {640.00}	344.56
	ROAD TRANSPORT AND HIGHWAYS	772	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (<i>BRO</i>) (<i>N24001999</i>)	11/2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	27.99	15
		773	KARGIL-ZANSKR PACKAGE-1 (<i>NHIDCL</i>) (<i>N24001343</i>)	3/2021	1/2023 (Dec-24) {10/2025}	384.23 (N.A.) {384.23}	101.55	58.4
		774	KARGIL-ZANSKR PACKAGE-2 (<i>NHIDCL</i>) (<i>N24001344</i>)	3/2021	1/2023 (Nov-23) {10/2025}	404.89 (N.A.) {404.89}	139.50	50.26

Table:-7. Project List: Ongoing Projects as of 31st August 2024

MADHYA PRADESH		775	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8/2020	1/2023 (Jun-24) {11/2024}	381.01 (N.A.) {381.01}	159.11	61.45
		776	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3/2021	1/2023 (Aug-24) {11/2024}	398.37 (N.A.) {398.37}	171.63	72.57
	CIVIL AVIATION	777	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6/2016	6/2021 (N.A.) {7/2024}	412.24 (N.A.) {412.24}	400.31	100
		778	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10/2021	8/2023 (Jun-24) {7/2024}	446.12 (N.A.) {446.12}	429.59	100
	COAL	779	KANCHAN OC EXPANSION (SECL) (N06000125)	12/2014	3/2021 (Mar-26) {3/2026}	371.04 (N.A.) {371.04}	130.43	47
		780	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3/2016	3/2021 (Mar-27) {3/2027}	869.44 (N.A.) {869.44}	250.21	64
		781	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162)	11/2017	3/2022 (N.A.) {3/2025}	1,255.17 (N.A.) {1,255.17}	1,231.12	96.64
		782	GANDHIGRAM UG MINE (WCL) (N06000183)	8/2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	24.98	28
		783	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7/2019	3/2023 (N.A.) {3/2025}	998.71 (N.A.) {998.71}	356.53	26.19
		784	NIGAH EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11/2020	3/2025 (N.A.) {3/2025}	1,729.68 (N.A.) {1,729.68}	636.85	39.92

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	785	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7/2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	465.30	44
	786	TAWA III UG MINE (WCL) (N06000250)	12/2021	3/2027 (N.A.) {3/2027}	324.25 (N.A.) {324.25}	12.32	9
	787	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9/2022	3/2027 (N.A.) {3/2027}	497.01 (N.A.) {497.01}	160.98	42
	788	VISHNUPURI UG TO OC (WCL) (N06000260)	11/2022	3/2029 (N.A.) {3/2029}	227.65 (N.A.) {227.65}	7.02	7
	789	URDHAN OC (WCL) (N06000265)	7/2022	3/2031 (N.A.) {3/2031}	228.42 (N.A.) {228.42}	27.67	9
	790	SHARDA UG (WCL) (N06000266)	7/2022	3/2028 (N.A.) {3/2028}	200.16 (N.A.) {200.16}	34.40	11
<u>PETROLEUM</u>	791	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5/2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	581.20	6
<u>POWER</u>	792	OMKARESHWAR FLOATING SOLAR POWER PROJECT (90 MW) (SJVN) (N18000342)	11/2022	4/2024 (N.A.) {8/2024}	646.17 (N.A.) {646.17}	594.77	100
	793	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6/2022	3/2024 (N.A.) {3/2024}	1,530.49 (N.A.) {1,530.49}	590.76	0
<u>RAILWAYS</u>	794	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4/2001	3/2021 (Dec-25) {12/2025}	424.60 (3,032.46) {5,125.16}	2,947.26	68

Table:-7. Project List: Ongoing Projects as of 31st August 2024

795	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4/2008	3/2022 (Mar-26) {3/2026}	3,503.69 (5,677.80) {6,203.51}	3,886.96	80
796	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12/2015	3/2020 (N.A.) {10/2024}	1,763.93 (N.A.) {2,445.30}	2,666.92	100
797	KATNI-BINA 3RD LINE (263 KM) (WCR) (N22000415)	6/2016	3/2022 (Jun-24) {6/2024}	2,478.23 (N.A.) {2,938.00}	1,279.35	60
798	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8/2016	3/2022 (N.A.) {9/2024}	582.13 (N.A.) {1,247.64}	1,096.23	
799	ANUPPUR-KATNI (SECR) (N22000485)	4/2015	12/2021 (Dec-23) {12/2024}	1,370.00 (1,680.00) {2,311.02}	1,593.08	74
800	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4/2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	152.39	20
801	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10/2021	10/2027 (Mar-25) {3/2025}	910.00 (1,095.88) {1,095.88}	734.55	87
802	POWARKHEDA - JUJHARPUR - SINGLE LINE FLYOVER IN UP DIRECTION (15.89 KM) (WCR) (N22000552)	12/2016	3/2024 (N.A.) {3/2024}	199.63 (N.A.) {199.63}	0.00	
803	SATNA - REWA (50 KM) (WCR) (N22000554)	11/2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80
804	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9/2018	9/2030 (N.A.) {9/2030}	4,340.00 (N.A.) {7,393.75}	1,004.86	12

Table:-7. Project List: Ongoing Projects as of 31st August 2024

ROAD TRANSPORT AND HIGHWAYS	805	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2/2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,125.06	35
	806	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3/2021	4/2024 (May-24) {8/2024}	790.78 (N.A.) {790.78}	1,347.21	46
	807	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1/2021	10/2023 (N.A.) {12/2024}	428.04 (N.A.) {428.04}	345.72	98.89
	808	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9/2019	9/2022 (N.A.) {12/2024}	194.40 (N.A.) {194.40}	170.92	85.07
	809	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756)	10/2020	10/2024 (N.A.) {10/2024}	1,352.56 (N.A.) {1,480.94}	785.11	89.98
	810	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH- 752D (PKG-III) (NHAI) (N24001758)	1/2020	10/2024 (N.A.) {10/2024}	823.05 (N.A.) {823.05}	368.50	98.92
	811	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH-752D (NHAI) (N24001759)	1/2020	6/2024 (Dec-24) {12/2024}	909.84 (N.A.) {909.84}	384.11	70.1
	812	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761)	2/2023	2/2025 (Feb-25) {2/2025}	520.28 (N.A.) {520.28}	348.18	86.91
	813	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10/2021	1/2024 (Dec-24) {12/2024}	1,146.22 (N.A.) {1,146.22}	544.18	78.84

Table:-7. Project List: Ongoing Projects as of 31st August 2024

814	4L OF HARDA - BETUL (PKG-I) FROM KM.0 TO KM.30 [HARDA - TEMAGAON] (NHAI) (N24001763)	9/2021	9/2023 (Sep-24) {9/2024}	774.16 (N.A.) {893.08}	463.85	100
815	4L OF HARDA - BETUL (PKG-III) FROM KM. 81.00 TO KM.121.248 [CHICHOLI - BETUL] (NHAI) (N24001764)	9/2021	9/2023 (Sep-24) {9/2024}	814.04 (N.A.) {947.29}	468.95	100
816	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765)	8/2022	7/2024 (N.A.) {5/2025}	207.77 (N.A.) {207.77}	41.36	32.19
817	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1/2022	10/2024 (N.A.) {10/2024}	1,011.29 (N.A.) {1,011.29}	145.56	30.71
818	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1/2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	463.70	77.1
819	BALANCE WORK OF 4L OF INDORE-GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8/2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	48.20	100
820	DHANGAON - BORGAON SECTION (KM 81.000 TO KM 139.000) [INDORE - EDLABAD PKG IV] (NHAI) (N24001769)	11/2018	8/2023 (Sep-24) {9/2024}	831.00 (N.A.) {831.00}	840.30	99.8
821	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2/2022	3/2024 (Dec-24) {12/2024}	417.51 (N.A.) {417.51}	212.07	71.74
822	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 9OF EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8/2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	116.45	22.05

Table:-7. Project List: Ongoing Projects as of 31st August 2024

823	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3/2022	12/2024 (N.A.) {12/2024}	179.19 (N.A.) {179.19}	75.91	60
824	UPGRADATION OF NASRULLAGANI-REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12/2021	10/2024 (N.A.) {3/2025}	305.12 (N.A.) {305.12}	73.80	17
825	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3/2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	151.39	64
826	REHABILITATION AND UPGRADATION OF KURWAI?MUNGAOLI?CHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3/2022	2/2025 (N.A.) {2/2025}	386.49 (N.A.) {386.49}	103.75	32
827	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI-SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12/2020	4/2023 (May-23) {12/2024}	529.44 (N.A.) {529.44}	165.60	45.69
828	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL-KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11/2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	52.23	11.54
829	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER-MP-RJ B (MoRTH) (N24002018)	1/2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	129.45	68.35
830	UPGRADATION OF DINDORI-SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1/2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	111.42	23.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

831	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3/2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	37.78	2
832	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1/2021	7/2023 (N.A.) {12/2024}	178.18 (N.A.) {178.18}	161.64	84.39
833	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12/2022	3/2025 (N.A.) {3/2025}	652.33 (N.A.) {652.33}	222.81	46.36
834	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7/2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	119.97	87.05
835	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1/2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	422.68	71.8
836	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHAI) (N24002077)	9/2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	134.10	10.42
837	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3/2015	8/2017 (Dec-23) {12/2024}	511.83 (N.A.) {511.83}	485.18	93.06
838	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12/2017	2/2020 (Sep-24) {9/2024}	950.27 (N.A.) {786.43}	627.08	98.44
839	2L+PS OF THIKRI ANJAD SECTION OF NH-347B (MoRTH) (N24000892)	11/2017	7/2018 (N.A.) {9/2023}	249.05 (N.A.) {249.05}	221.19	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		840	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V (NHAI) (N24001212)	12/2017	11/2022 (Dec-24) {12/2024}	656.98 (N.A.) {840.00}	1,103.00	98.51
		841	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM (NHAI) (N24001214)	12/2017	12/2022 (Dec-24) {12/2024}	217.96 (N.A.) {884.00}	2,298.00	99.21
	<u>SOCIAL JUSTICE</u>	842	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2/2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74
	<u>URBAN DEVELOPMENT I</u>	843	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11/2018	2/2023 (Dec-27) {12/2027}	6,941.40 (N.A.) {6,941.40}	2,298.28	29.51
		844	INDORE METRO RAIL (MPMRCL) (N28000125)	11/2018	2/2023 (Dec-27) {12/2027}	7,500.80 (N.A.) {7,500.80}	3,001.23	44.94
<u>MAHARASHTRA</u>	<u>CIVIL AVIATION</u>	845	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3/2017	4/2021 (N.A.) {12/2023}	475.39 (N.A.) {520.00}	505.60	100
		846	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6/2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	266.04	100
	<u>COAL</u>	847	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8/2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	534.87	86
		848	UKNI DEEP OC (WCL) (N06000179)	11/2018	3/2021 (Mar-25) {3/2025}	318.14 (N.A.) {318.14}	253.27	91

Table:-7. Project List: Ongoing Projects as of 31st August 2024

849	BELLORA-NAIGAON DEEP OC (WCL) (N06000180)	11/2018	3/2021 (Mar-25) {3/2025}	252.71 (N.A.) {252.71}	122.94	56
850	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3/2021	3/2028 (N.A.) {3/2028}	241.72 (N.A.) {241.72}	59.30	6
851	SASTI EXPANSION OC (WCL) (N06000206)	8/2020	3/2026 (N.A.) {3/2026}	371.59 (N.A.) {371.59}	105.64	24
852	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	2/2019	3/2028 (N.A.) {3/2028}	720.87 (N.A.) {720.87}	179.54	33
853	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11/2018	3/2024 (Mar-25) {3/2025}	333.43 (N.A.) {333.43}	223.17	78
854	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2/2020	3/2027 (N.A.) {3/2027}	1,184.33 (N.A.) {1,184.33}	849.44	48
855	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9/2018	3/2024 (Mar-25) {3/2025}	313.34 (N.A.) {313.34}	205.45	87
856	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (WCL) (N06000231)	11/2020	3/2026 (N.A.) {3/2026}	826.80 (N.A.) {826.80}	518.85	52
857	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1/2022	3/2028 (N.A.) {3/2028}	253.51 (N.A.) {253.51}	111.68	27
858	SINGHORI DEEP OC (WCL) (N06000252)	5/2022	3/2029 (N.A.) {3/2029}	421.84 (N.A.) {421.84}	115.89	16

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	859	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6/2022	3/2026 (N.A.) {3/2026}	497.06 (N.A.) {497.06}	144.88	12
	860	BHATADI EXPANSION OC (WCL) (N06000254)	2/2020	3/2028 (N.A.) {3/2028}	729.86 (N.A.) {729.86}	159.12	17
	861	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	5/2019	3/2027 (N.A.) {3/2027}	496.38 (N.A.) {496.38}	143.72	27
	862	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9/2022	3/2028 (N.A.) {3/2028}	494.60 (N.A.) {494.60}	99.87	7
	863	GOKUL EXPANSION OC (WCL) (N06000264)	4/2021	3/2026 (N.A.) {3/2026}	456.95 (N.A.) {456.95}	148.57	7
	864	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	1/2023	3/2027 (N.A.) {3/2027}	206.19 (N.A.) {206.19}	7.75	5
	865	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3/2024	3/2030 (N.A.) {3/2030}	1,428.25 (N.A.) {1,428.25}	203.03	17
<u>DEPARTMENT OF HIGHER EDUCATION</u>	866	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1/2018	7/2020 (Nov-23) {2/2024}	223.37 (275.00) {230.00}	141.16	100
<u>HEALTH AND FAMILY WELFARE</u>	867	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7/2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	27.16	0
<u>PETROLEUM</u>	868	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12/2015	4/2018 (Dec-23) {5/2026}	3,190.69 (3,375.90) {3,375.90}	2,961.86	87.6

Table:-7. Project List: Ongoing Projects as of 31st August 2024

869	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4/2019	3/2022 (Jun-24) {2/2025}	3,228.80 (3,976.67) {3,976.67}	3,922.26	98.6
870	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5/2019	4/2025 (Oct-25) {10/2025}	8,797.00 (11,256.00) {11,256.00}	4,538.26	72.3
871	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436)	1/2022	5/2024 (Jan-25) {1/2025}	3,183.58 (N.A.) {3,645.23}	3,417.00	99.1
872	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4/2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	578.27	53.4
873	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9/2021	10/2023 (May-24) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08
874	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5/2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	181.28	63.5
875	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9/2022	8/2025 (N.A.) {8/2025}	165.00 (N.A.) {165.00}	43.39	48.68
876	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6/2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	111.21	10.1
877	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3/2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	42.40	1.3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	878	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6/2017	5/2025 (N.A.) {5/2025}	281.35 (N.A.) {281.35}	82.65	37.2
	879	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4/2022	10/2024 (Aug-26) {8/2026}	341.43 (N.A.) {341.43}	188.94	24.1
	880	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3/2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	55.07	48.7
	881	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11/2022	5/2024 (Dec-24) {12/2024}	1,219.48 (N.A.) {1,145.10}	29.82	34.9
	882	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5/2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	99.89	23.7
	883	MHN TCPG PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2/2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	81.27	13.8
	884	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6/2024	5/2026 (N.A.) {5/2026}	2,379.84 (N.A.) {2,379.84}	0.00	
	885	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6/2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	4.84	3.8
POWER	886	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4/2022	5/2024 (N.A.) {7/2025}	5,491.89 (532.00) {5,491.89}	2,701.37	68

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	887	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAYDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11/2023	7/2025 (N.A.) {7/2025}	224.00 (N.A.) {224.00}	0.00	
RAILWAYS	888	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2/1997	3/2021 (N.A.) {12/2025}	2,271.50 (N.A.) {4,805.17}	4,072.18	85
	889	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTPT) (N22000092)	4/2008	3/2014 (N.A.) {3/2014}	5,300.00 (N.A.) {918.53}	7,135.77	21
	890	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4/2008	3/2023 (N.A.) {12/2026}	3,168.29 (N.A.) {3,445.48}	2,394.71	47
	891	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4/2011	3/2021 (N.A.) {12/2025}	792.89 (N.A.) {792.89}	700.54	50
	892	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4/2012	3/2022 (N.A.) {3/2025}	540.02 (N.A.) {540.02}	547.33	72
	893	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2/2015	3/2022 (N.A.) {3/2025}	1,272.19 (N.A.) {1,384.72}	1,021.24	67
	894	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2/2015	3/2023 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,254.93	42
	895	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2/2015	3/2024 (N.A.) {6/2024}	3,627.47 (3,627.00) {6,463.49}	3,737.52	84
	896	DAUND - MANMAD (236 KM) (CR) (N22000360)	2/2016	3/2023 (N.A.) {12/2024}	1,876.00 (N.A.) {2,081.27}	2,056.27	86

Table:-7. Project List: Ongoing Projects as of 31st August 2024

897	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2/2016	3/2022 (N.A.) {12/2024}	1,035.16 (N.A.) {1,035.16}	1,219.08	75
898	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2/2016	3/2023 (N.A.) {3/2025}	637.95 (N.A.) {637.95}	717.11	70
899	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9/2016	3/2023 (Dec-23) {12/2025}	1,908.51 (2,753.05) {3,544.25}	2,747.21	80
900	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3/2010	(N.A.) {3/2024}	265.88 (N.A.) {311.36}	0.00	0
901	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6/2018	12/2021 (N.A.) {12/2026}	229.00 (N.A.) {1,886.05}	474.93	22
902	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8/2022	8/2027 (N.A.) {3/2027}	955.00 (N.A.) {955.39}	56.34	0
903	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1/2019	3/2028 (N.A.) {3/2027}	904.92 (N.A.) {904.92}	954.11	5
904	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1/2019	3/2026 (N.A.) {12/2026}	492.76 (N.A.) {492.76}	149.60	5
905	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2/2023	3/2027 (N.A.) {3/2026}	836.12 (N.A.) {836.12}	5.28	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	906	BARAMATI - LONAND (CR) (N22000615)	2/1999	3/2027 (N.A.) {3/2026}	736.44 (N.A.) {736.44}	518.52	50
	907	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4/2019	3/2025 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	846.83	0
	908	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10/2019	6/2024 (N.A.) {6/2024}	1,400.00 (N.A.) {1,400.00}	0.00	74
<u>ROAD TRANSPORT AND HIGHWAYS</u>	909	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11/2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	
	910	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3/2022	6/2022 (N.A.) {6/2022}	282.07 (N.A.) {282.07}	34.65	16.17
	911	TUNNEL AT KHAMBATI Ghat SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2/2019	2/2022 (Nov-24) {11/2024}	493.00 (N.A.) {493.00}	374.15	71.42
	912	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL- ALANDI SECTION (NHAI) (N24001488)	9/2021	9/2023 (Oct-24) {10/2024}	618.45 (N.A.) {618.45}	582.77	90
	913	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12/2022	12/2024 (N.A.) {12/2024}	1,749.86 (N.A.) {1,749.86}	1,271.00	55.7
	914	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 () (NHAI) (N24001495)	11/2022	11/2024 (N.A.) {11/2024}	930.00 (N.A.) {930.00}	542.93	58.4

Table:-7. Project List: Ongoing Projects as of 31st August 2024

915	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501)	9/2021	9/2023 (Jul-23) {7/2023}	531.86 (532.41) {532.41}	520.71	0.5
916	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9/2021	9/2023 (Mar-24) {12/2024}	624.45 (580.15) {580.15}	398.06	2
917	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH-965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9/2021	9/2023 (Mar-24) {12/2024}	667.66 (666.21) {666.21}	544.80	13
918	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5/2022	5/2024 (Jan-25) {1/2025}	1,260.00 (N.A.) {1,260.00}	463.45	90.24
919	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3/2022	3/2024 (Oct-24) {10/2024}	1,549.02 (N.A.) {1,549.02}	526.31	51.75
920	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2/2022	2/2024 (Jun-25) {6/2025}	2,747.00 (N.A.) {2,747.00}	929.38	63.1
921	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11/2022	5/2024 (Aug-25) {8/2025}	1,124.00 (N.A.) {1,124.00}	299.43	43.85
922	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11/2022	10/2024 (N.A.) {10/2024}	1,450.00 (N.A.) {1,450.00}	545.51	62.22
923	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11/2022	10/2024 (Apr-25) {4/2025}	990.00 (N.A.) {990.00}	296.63	50.47

Table:-7. Project List: Ongoing Projects as of 31st August 2024

924	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1/2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	728.28	38.05
925	BALANCE WORKS OF 4L PANVEL-INDAPUR SECTION OF NH-66 (OLD NH-17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10/2022	5/2024 (N.A.) {5/2024}	332.00 (N.A.) {332.00}	185.61	42.44
926	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9/2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	357.45	46.72
927	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH-66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1/2023	12/2023 (Dec-24) {12/2024}	151.26 (N.A.) {151.26}	103.46	67.03
928	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ? ALANDI S (NHAI) (N24001610)	1/2022	5/2024 (Oct-24) {10/2024}	1,833.73 (N.A.) {1,833.73}	391.72	77.12
929	FOUR LANING OF AURANGABAD-PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA . (NHAI) (N24001795)	10/2022	7/2024 (N.A.) {9/2024}	490.40 (N.A.) {289.00}	241.93	77
930	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3/2022	10/2024 (Apr-25) {4/2025}	1,013.33 (1,013.33) {1,111.33}	354.52	59.06
931	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10/2021	1/2024 (N.A.) {3/2025}	815.77 (N.A.) {815.77}	609.59	91.24
932	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2/2021	11/2023 (N.A.) {11/2024}	540.21 (N.A.) {540.21}	415.87	94.42

Table:-7. Project List: Ongoing Projects as of 31st August 2024

933	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2/2021	10/2023 (N.A.) {12/2024}	1,166.96 (N.A.) {1,251.00}	1,033.43	80
934	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12/2019	9/2022 (Jun-24) {6/2024}	1,654.07 (N.A.) {980.00}	835.19	91.76
935	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH-166 (PKG ? II) (NHAI) (N24001834)	5/2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	401.14	36.52
936	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH-166 (PKG?III) (NHAI) (N24001835)	5/2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	311.08	36.8
937	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3/2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	27.35
938	REHABILITATION AND UPGADATION OF AMBOLI JUNCTION (DESIGN CH. 71+530) TO AJARA (DESIGN CH.100+835) SE (MoRTH) (N24001881)	6/2021	11/2024 (N.A.) {11/2024}	574.00 (N.A.) {574.00}	574.00	93.94
939	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3/2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8
940	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3/2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65

Table:-7. Project List: Ongoing Projects as of 31st August 2024

941	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3/2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
942	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2/2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	
943	DEVELOPMENT/WIDENING OF TALEGAON ? CHAKAN ? SHIKRAPUR ? NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10/2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78
944	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8/2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	78
945	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8/2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31
946	2 LANE + PS PIMPLNER TO SATANA - [DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9/2019	7/2021 (N.A.) {7/2021}	277.81 (N.A.) {277.81}	148.68	
947	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2/2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46
948	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7/2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66

Table:-7. Project List: Ongoing Projects as of 31st August 2024

949	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2/2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.5
950	SHEWALI (SAKRI) - NANDURBAR (MoRTH) (N24001893)	9/2022	4/2024 (N.A.) {7/2024}	232.59 (N.A.) {232.59}	97.70	77.64
951	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9/2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44
952	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11/2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99
953	UPGRADATION AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11/2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63
954	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12/2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34
955	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8/2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	
956	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9/2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
957	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10/2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.8

Table:-7. Project List: Ongoing Projects as of 31st August 2024

958	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8/2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48
959	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM. 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6/2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
960	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12/2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76
961	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM. 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11/2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
962	REHABILITATION AND UPGRADATION OF JAMKHED TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9/2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
963	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3/2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
964	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3/2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	111.50	15.03
965	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7/2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	12.74	15.86
966	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2/2024	3/2025 (N.A.) {3/2025}	175.00 (N.A.) {175.00}	29.36	11.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

967	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1/2015	(N.A.) { }	225.81 (N.A.) {225.81}	167.96	
968	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12/2015	3/2019 (Nov-23) {12/2024}	649.50 (N.A.) {649.50}	579.82	87.68
969	NAGPUR RING ROAD PACKAGE-1 (NHAI) (N24000558)	3/2016	7/2019 (Jul-23) {9/2024}	546.00 (N.A.) {546.00}	526.26	100
970	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3/2016	7/2019 (Mar-24) {12/2024}	591.66 (N.A.) {591.66}	576.95	90.29
971	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3/2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95
972	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3/2016	(N.A.) { }	1,101.58 (N.A.) {1,101.58}	608.53	65.22
973	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655)	3/2017	3/2020 (Dec-24) {12/2024}	247.02 (N.A.) {157.49}	91.48	98.49
974	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3/2017	3/2020 (Jul-22) {7/2024}	744.64 (N.A.) {1,007.00}	380.66	74.89
975	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3/2017	3/2017 (May-21) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	82.04

Table:-7. Project List: Ongoing Projects as of 31st August 2024

976	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3/2018	7/2021 (N.A.) {9/2024}	1,162.92 (1,182.87) {1,182.87}	371.48	52.32
977	SARSAM TO KOTHARI (MoRTH) (N24001002)	2/2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
978	AKOLA TO AKOT (MoRTH) (N24001003)	1/2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99
979	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1/2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
980	DAHEGAON TO KUHI (MoRTH) (N24001017)	1/2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99
981	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1/2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100
982	AMD I TO SAONER (MoRTH) (N24001021)	1/2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69
983	WADI TO ASOLA (MoRTH) (N24001022)	1/2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
984	WAKAN PALI KHOPOLI (MoRTH) (N24001026)	1/2017	5/2019 (N.A.) {10/2023}	376.19 (N.A.) {376.19}	118.74	99
985	SHAH PUR PATGAON SECTION I (MoRTH) (N24001027)	1/2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	70.66

Table:-7. Project List: Ongoing Projects as of 31st August 2024

986	AHMADPUR TO PIMPLA (MoRTH) (N24001029)	1/2017	8/2019 (N.A.) {12/2023}	422.38 (N.A.) {422.38}	269.59	83
987	PIMPLA TO MANJARSUMBHA (MoRTH) (N24001030)	1/2017	8/2019 (N.A.) {12/2023}	595.77 (N.A.) {595.77}	357.73	89.6
988	MANSAR TO SALAIKHURD (MoRTH) (N24001035)	1/2018	12/2019 (N.A.) {11/2023}	418.36 (N.A.) {418.36}	263.13	99
989	JINTUR TO PARBHANI (MoRTH) (N24001039)	1/2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	80.48
990	JAHIRABAD TO LATUR (MoRTH) (N24001040)	1/2017	11/2019 (N.A.) {11/2023}	461.96 (N.A.) {461.96}	329.59	99
991	SHIROD SHAHPURER TO NANDED (MoRTH) (N24001041)	1/2017	7/2019 (N.A.) {12/2023}	211.34 (N.A.) {211.34}	136.33	99.9
992	SALAIKHURD TO TIRORA (MoRTH) (N24001042)	1/2018	12/2019 (N.A.) {12/2023}	415.25 (415.25) {415.25}	274.02	98
993	NILAJPHATA TO BHANDARA (MoRTH) (N24001043)	1/2018	5/2020 (N.A.) {12/2023}	420.63 (421.00) {420.63}	219.40	71.25
994	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1/2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.5
995	MEHKAR TO AJISPUR (MoRTH) (N24001048)	1/2017	7/2019 (N.A.) {8/2023}	232.77 (N.A.) {232.77}	151.60	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

996	VITA TO NAGAJ (MoRTH) (N24001050)	3/2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
997	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2/2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	89.97
998	KARWANDI TO RAJURI (MoRTH) (N24001058)	3/2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
999	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3/2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95
1000	CHIKALI TO DHAD (MoRTH) (N24001061)	3/2018	12/2019 (N.A.) {3/2024}	189.46 (189.00) {189.46}	133.07	97.76
1001	DHAD BHOKARDAN TO BHOKARDHAN SILLOD (MoRTH) (N24001062)	3/2018	12/2019 (N.A.) {3/2024}	336.21 (336.00) {336.21}	236.11	100
1002	PARBHANI TO GANGKHED (MoRTH) (N24001065)	3/2018	12/2019 (N.A.) {10/2023}	238.19 (238.00) {238.19}	194.54	99
1003	NANDED TO JALKOT (MoRTH) (N24001069)	12/2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	
1004	KOTHARI TO DHANORA (MoRTH) (N24001073)	9/2018	8/2020 (N.A.) {8/2020}	301.38 (301.00) {301.38}	240.32	96.32
1005	OSMANNAGAR TO KUNDRAL (MoRTH) (N24001075)	9/2017	8/2020 (N.A.) {12/2023}	344.25 (344.00) {344.25}	194.72	95.63

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1006	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3/2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	93.83
1007	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12/2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25
1008	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3/2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98
1009	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3/2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	89.99
1010	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3/2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100
1011	KOLDE TO KHETIYA (MoRTH) (N24001090)	1/2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81
1012	SATARA TO MHASWAD (MoRTH) (N24001092)	1/2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	76.76
1013	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1/2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	88.16
1014	SELDOH TO PANVAR (MoRTH) (N24001097)	7/2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	
1015	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1/2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1016	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1/2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27
1017	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7/2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
1018	CHIMUR TO WARORA (MoRTH) (N24001105)	11/2016	3/2019 (N.A.) {3/2019}	467.70 (N.A.) {467.70}	235.04	100
1019	PEN TO KHOPOLI (MoRTH) (N24001106)	3/2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
1020	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7/2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	
1021	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4/2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	
1022	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7/2016	9/2019 (N.A.) {3/2024}	406.54 (407.00) {406.54}	274.30	80.7
1023	BARASGAON TO RAHATEE (MoRTH) (N24001113)	7/2016	9/2018 (N.A.) {12/2023}	289.11 (290.00) {289.11}	232.56	99
1024	INDAPUR TO VADPALE (MoRTH) (N24001114)	1/2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
1025	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3/2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.6

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1026	SHIRUR TO KHARDA (MoRTH) (N24001123)	2/2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
1027	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2/2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
1028	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2/2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
1029	FARDAPUR TO JALGAON (MoRTH) (N24001126)	2/2017	6/2019 (N.A.) {6/2019}	456.45 (N.A.) {456.45}	427.43	89.88
1030	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2/2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	87.84
1031	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9/2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
1032	KANTE TO WAKED (MoRTH) (N24001134)	3/2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	
1033	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2/2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100
1034	WARDHA TO ARVI (MoRTH) (N24001150)	2/2018	4/2020 (N.A.) {12/2023}	313.58 (N.A.) {313.58}	230.41	96
1035	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377)	2/2019	1/2022 (Aug-23) {8/2023}	731.89 (731.99) {731.99}	684.03	0.2

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1036	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378)	2/2019	1/2022 (Jun-23) {6/2023}	362.46 (372.46) {372.46}	346.15	0.7
		1037	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379)	2/2019	1/2022 (Aug-23) {8/2023}	594.75 (594.75) {613.75}	585.20	0.5
	URBAN DEVELOPMENT I	1038	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) (MMRCL) (N28000086)	7/2013	3/2020 (N.A.) {12/2023}	23,136.00 (N.A.) {37,276.00}	23,687.33	87.2
		1039	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12/2016	11/2021 (Sep-24) {9/2024}	11,420.00 (13,656.22) {13,656.22}	12,431.42	99.85
		1040	NAGPUR METRO RAIL PROJECT PHASE II (MMRCL) (N28000155)	12/2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	254.42	11.55
		1041	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10/2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	0.00	3.5
	WATER RESOURCES	1042	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA (BPPB) (N300000001)	3/2017	12/2019 (Aug-24) {12/2023}	233.57 (N.A.) {233.57}	217.42	
MANIPUR	CIVIL AVIATION	1043	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11/2021	7/2024 (Dec-25) {12/2025}	499.00 (N.A.) {499.00}	104.76	32.88
	RAILWAYS	1044	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4/2003	3/2011 (Mar-28) {12/2026}	4,454.17 (12,274.06) {19,517.70}	14,707.39	79.3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

ROAD TRANSPORT AND HIGHWAYS	1045	IMPHAL ? MOREH (PACKAGE 4) (NHIDCL) (N24001399)	3/2021	1/2023 (N.A.) {4/2024}	277.99 (N.A.) {277.99}	146.35	100
	1046	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3/2021	1/2023 (N.A.) {8/2025}	211.70 (N.A.) {211.70}	29.00	31.88
	1047	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7/2021	3/2023 (Feb-24) {3/2025}	467.00 (N.A.) {467.00}	181.65	75.23
	1048	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7/2021	3/2023 (Oct-23) {1/2025}	185.80 (N.A.) {185.80}	112.31	92.65
	1049	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7/2021	3/2023 (May-24) {2/2025}	483.87 (N.A.) {483.87}	278.89	91.03
	1050	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7/2021	3/2023 (Sep-23) {2/2025}	198.77 (N.A.) {198.77}	110.09	85.12
	1051	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7/2021	10/2023 (Feb-24) {6/2025}	673.27 (N.A.) {673.27}	348.20	72.4
	1052	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8/2021	5/2023 (Dec-23) {2/2025}	477.86 (N.A.) {477.86}	235.67	80.3
	1053	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9/2021	5/2023 (Oct-23) {4/2025}	311.18 (N.A.) {311.18}	171.57	72.7
	1054	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8/2021	5/2023 (N.A.) {10/2024}	467.41 (N.A.) {467.41}	243.19	91.69

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1055	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8/2021	12/2023 (N.A.) {12/2025}	579.63 (N.A.) {579.63}	131.58	52.16
1056	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9/2021	2/2024 (N.A.) {4/2025}	310.76 (N.A.) {310.76}	116.81	75.99
1057	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12/2021	5/2024 (N.A.) {10/2025}	410.68 (N.A.) {410.68}	105.71	50.78
1058	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12/2021	2/2025 (N.A.) {11/2025}	504.76 (N.A.) {504.76}	95.59	43.38
1059	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3/2022	2/2025 (N.A.) {2/2025}	152.11 (N.A.) {152.11}	51.41	70.28
1060	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9/2021	1/2025 (N.A.) {1/2025}	315.56 (N.A.) {315.56}	60.63	43.9
1061	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1/2023	12/2025 (N.A.) {3/2026}	760.16 (N.A.) {760.16}	63.80	27.18
1062	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3/2023	2/2026 (N.A.) {3/2026}	578.98 (N.A.) {578.98}	48.64	26.1
1063	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3/2020	6/2022 (Dec-23) {12/2024}	292.24 (N.A.) {292.24}	127.86	85.33
1064	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6/2020	8/2022 (N.A.) {12/2024}	365.53 (N.A.) {365.53}	156.31	77.36

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1065	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3/2020	6/2022 (N.A.) {12/2024}	167.95 (204.12) {167.95}	88.05	69.89
1066	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7/2020	8/2022 (N.A.) {12/2024}	177.76 (N.A.) {177.76}	89.67	80.53
1067	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8/2020	4/2022 (N.A.) {8/2025}	379.39 (N.A.) {379.39}	189.78	45.88
1068	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO (NHIDCL) (N24001275)	8/2020	4/2022 (N.A.) {12/2025}	268.98 (N.A.) {268.98}	22.08	
1069	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8/2020	4/2022 (N.A.) {12/2025}	228.97 (N.A.) {228.97}	0.00	
1070	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2/2021	12/2022 (N.A.) {2/2025}	226.32 (N.A.) {226.32}	85.91	63.1
1071	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2/2021	12/2022 (N.A.) {9/2024}	188.36 (N.A.) {188.36}	124.69	94.92
1072	MARIAM - PEREN PKG-2B (NHIDCL) (N24001351)	2/2021	12/2022 (N.A.) {3/2024}	232.26 (N.A.) {232.26}	156.93	100
1073	IMPHAL ? MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3/2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100
1074	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3/2021	12/2022 (Nov-23) {6/2025}	195.14 (N.A.) {195.14}	59.99	50.01

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1075	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3/2021	12/2022 (N.A.) {1/2025}	234.08 (N.A.) {234.08}	139.45	90.34
MEGHALAY A	DEPARTMENT OF HIGHER EDUCATION	1076	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9/2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	272.05	72
	DONER	1077	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4/2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	98.5
	RAILWAYS	1078	NEW BG LINE FROM BYRNIHAT TO SHILLONG (NFR) (N22000205)	4/2010	3/2021 (N.A.) {3/2021}	906.46 (1,202.33) {8,324.28}	269.80	2
	ROAD TRANSPORT AND HIGHWAYS	1079	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8/2020	2/2022 (Oct-24) {10/2024}	302.88 (N.A.) {302.88}	209.63	93
		1080	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9/2021	5/2024 (N.A.) {1/2025}	359.86 (N.A.) {359.86}	215.22	78
		1081	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11/2021	6/2024 (N.A.) {12/2024}	283.50 (N.A.) {283.50}	196.77	70.19
		1082	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4/2017	9/2021 (Jul-23) {3/2025}	553.51 (610.09) {553.51}	340.07	66.61

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1083	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM (NHIDCL) (N24000903)	3/2019	3/2022 (Dec-23) {12/2023}	306.28 (N.A.) {306.28}	233.49	100
		1084	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11/2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	216.11	20
		1085	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11/2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	375.55	10.4
		1086	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11/2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	191.35	3
		1087	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11/2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	45.46	0.3
		1088	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10/2020	4/2022 (Jun-24) {12/2024}	157.86 (146.92) {157.86}	146.19	97.49
		1089	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3/2021	12/2022 (Jun-24) {11/2024}	260.21 (N.A.) {260.21}	201.39	86.38
MIZORAM	RAILWAYS	1090	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4/2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,466.67	93
	ROAD TRANSPORT AND HIGHWAYS	1091	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9/2021	5/2023 (Jun-24) {1/2025}	492.94 (492.94) {492.94}	355.00	84.44

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1092	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9/2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	216.98	37
1093	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12/2021	2/2025 (N.A.) {5/2026}	500.88 (N.A.) {500.88}	122.78	31
1094	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4/2017	4/2023 (Mar-24) {11/2024}	519.09 (785.65) {785.65}	649.83	90
1095	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4/2017	7/2023 (May-24) {7/2024}	640.07 (990.88) {1,286.35}	1,198.44	99
1096	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4/2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.79	99.5
1097	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4/2017	4/2023 (Nov-23) {12/2024}	473.18 (688.25) {688.25}	514.74	83.66
1098	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4/2017	4/2023 (Oct-23) {12/2024}	537.82 (789.05) {789.05}	746.15	91.3
1099	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4/2017	6/2023 (Feb-24) {12/2024}	518.53 (906.76) {906.76}	784.80	88.32
1100	WIDENING AND UP-GRADATION TO 2- LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4/2017	4/2024 (Jul-24) {12/2024}	404.29 (750.32) {750.32}	584.01	83

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1101	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4/2017	9/2023 (May-24) {12/2024}	428.11 (746.39) {746.39}	579.70	87
1102	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9/2020	10/2022 (Apr-24) {6/2024}	275.02 (247.25) {247.25}	231.19	99.73
1103	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3/2020	7/2022 (Jan-24) {6/2024}	206.88 (219.33) {219.33}	206.55	97.01
1104	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3/2020	7/2022 (Mar-24) {11/2024}	292.24 (331.17) {331.17}	287.95	91.42
1105	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) (NHIDCL) (N24001283)	3/2020	7/2022 (Jan-24) {1/2024}	281.78 (253.41) {253.41}	237.91	100
1106	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3/2021	12/2022 (Mar-24) {3/2024}	374.39 (374.39) {374.39}	292.27	100
1107	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3/2021	12/2022 (Apr-24) {4/2024}	233.25 (233.25) {233.25}	178.37	100
1108	DULTE- KWALKULH - CHAMPAI PKG.3 (NHIDCL) (N24001357)	3/2021	6/2023 (Jan-24) {1/2024}	674.71 (674.71) {674.71}	589.25	100
1109	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3/2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	383.62	42.2

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1110	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3/2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	276.77	41.5
MULTI STATE	COAL	1111	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8/2016	3/2022 (Mar-25) {3/2025}	319.76 (319.76) {319.76}	281.40	98
		1112	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) (WCL) (N06000157)	2/2017	3/2021 (Mar-25) {3/2025}	328.00 (N.A.) {328.00}	321.43	96
		1113	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8/2020	3/2024 (N.A.) {3/2025}	836.42 (N.A.) {836.42}	664.02	54.2
	DPIIT	1114	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9/2011	3/2027 (Mar-27) {3/2027}	20,084.00 (20,084.00) {20,084.00}	9,718.22	50.99
	PETROLEUM	1115	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6/2009	12/2012 (Feb-25) {3/2025}	2,915.00 (5,909.00) {5,909.00}	4,019.40	91.2
		1116	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9/2019	7/2022 (Dec-24) {12/2024}	2,658.34 (N.A.) {2,658.34}	1,949.70	91.6
		1117	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3/2020	11/2022 (Mar-25) {3/2025}	1,030.65 (N.A.) {1,030.65}	763.70	84
		1118	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6/2020	5/2023 (Oct-24) {10/2024}	7,844.25 (N.A.) {7,844.25}	5,658.10	89
		1119	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6/2019	12/2029 (Mar-30) {3/2030}	169.00 (N.A.) {169.00}	70.79	17.9

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1120	NORTH EAST GAS GRID (JGGL) (N16000439)	11/2020	3/2024 (Mar-25) {3/2025}	9,265.00 (9,265.00) {9,265.00}	5,478.65	83.2
	1121	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7/2023	7/2026 (Jul-26) {7/2026}	521.92 (521.92) {521.92}	3.90	12.8
POWER	1122	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO (PGCIL) (N18000184)	3/2015	3/2018 (N.A.) {12/2024}	197.40 (N.A.) {197.40}	161.89	96
	1123	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12/2014	12/2018 (Mar-25) {3/2025}	4,754.42 (9,129.32) {9,129.32}	6,684.40	77.1
	1124	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12/2014	12/2018 (Mar-25) {3/2025}	5,111.33 (6,700.00) {6,700.00}	4,925.53	95
	1125	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264)	8/2017	2/2020 (Apr-23) {9/2025}	1,931.39 (2,635.55) {2,635.55}	1,962.64	99
	1126	NORTH EASTERN REGION STRENGTHENING SCHEME-XII (PGCIL) (N18000316)	5/2021	3/2023 (N.A.) {8/2024}	576.42 (576.42) {576.42}	418.46	100
	1127	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2/2022	4/2025 (N.A.) {4/2025}	318.12 (N.A.) {318.12}	139.55	83
	1128	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3/2022	12/2024 (N.A.) {12/2024}	288.71 (N.A.) {288.71}	100.79	39

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1129	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2/2022	9/2023 (N.A.) {12/2024}	359.47 (N.A.) {359.47}	191.87	63
	1130	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5/2022	11/2023 (N.A.) {12/2024}	1,666.00 (N.A.) {1,666.00}	1,290.22	80
	1131	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7/2022	6/2023 (N.A.) {12/2024}	4,546.26 (N.A.) {4,546.26}	2,102.55	63
	1132	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7/2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	58.93	64
	1133	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10/2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	72.11	51
	1134	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3/2023	11/2024 (N.A.) {11/2024}	3,546.94 (N.A.) {3,546.94}	1,093.24	45
	1135	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3/2023	3/2025 (N.A.) {3/2025}	281.16 (N.A.) {281.16}	27.14	26
RAILWAYS	1136	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3/1981	7/2012 (N.A.) {11/2024}	450.00 (N.A.) {2,017.96}	1,190.75	85
	1137	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9/1998	5/2008 (N.A.) {3/2025}	247.66 (63.57) {8,248.50}	2,520.04	43

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1138	CHHAPRA-BALLIA UP (NER) (N22000134)	3/2013	1/2019 (N.A.) {2/2025}	295.00 (954.00) {954.00}	982.36	95
1139	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4/2007	3/2022 (Dec-26) {12/2026}	1,347.26 (1,793.63) {1,793.63}	1,424.89	58
1140	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4/2007	3/2022 (Feb-27) {2/2027}	1,640.04 (1,873.10) {2,873.11}	2,030.41	58
1141	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4/2011	3/2022 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	
1142	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR (NCR) (N22000158)	4/2010	(Dec-26) {12/2026}	2,030.50 (746.83) {746.83}	81.25	19
1143	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4/2013	3/2019 (N.A.) {9/2024}	1,798.00 (N.A.) {2,832.35}	3,060.11	91
1144	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4/2010	3/2020 (N.A.) {3/2027}	242.22 (N.A.) {1,208.73}	386.72	5
1145	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4/2010	(N.A.) {3/2023}	241.52 (N.A.) {401.65}	343.30	85.42
1146	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4/2011	3/2020 (N.A.) {5/2025}	414.84 (N.A.) {1,265.16}	565.23	30
1147	MADURAI-TUTICORIN VIA ARUPPUKOTTAI (SR) (N22000215)	4/2011	3/2019 (Dec-27) {12/2027}	120.70 (N.A.) {2,053.39}	342.13	14

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1148	PIRPAINTI-JASIDIH (ER) (N22000219)	4/2013	3/2022 (Mar-28) {3/2028}	915.98 (N.A.) {2,137.81}	802.96	45
1149	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4/2012	3/2023 (N.A.) {3/2025}	1,856.95 (N.A.) {1,952.68}	1,296.52	
1150	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4/2007	(N.A.) {2/2024}	336.91 (N.A.) {791.39}	572.99	40
1151	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4/2007	(N.A.) {2/2027}	2,062.30 (2,495.59) {2,495.59}	1,395.25	60
1152	PHULERA - DIGANA DOUBLING (NWR) (N22000326)	5/2015	3/2020 (Apr-24) {4/2024}	600.00 (N.A.) {701.81}	733.13	100
1153	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3/2015	3/2019 (N.A.) {6/2025}	1,614.59 (1,877.81) {2,458.87}	2,396.72	89
1154	KAZIPET-BALHRSHA (SCR) (N22000367)	4/2015	3/2021 (N.A.) {1/2025}	2,063.03 (N.A.) {2,909.00}	2,578.41	
1155	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12/2015	12/2023 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	64,167.00	46.07
1156	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11/2007	3/2020 (N.A.) {3/2020}	16,592.00 (51,101.00) {51,101.00}	47,476.00	83
1157	CHANDIGARH-BADDI (NR) (N22000467)	4/2007	3/2023 (N.A.) {6/2025}	328.14 (N.A.) {1,540.14}	482.67	10

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1158	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3/2019	5/2023 (N.A.) {12/2025}	1,866.31 (N.A.) {1,866.31}	1,597.20	53
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1159	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11/2021	2/2025 (N.A.) {2/2025}	2,155.95 (N.A.) {2,155.95}	1,026.00	42.12
	1160	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4/2022	11/2024 (N.A.) {11/2024}	796.65 (N.A.) {796.65}	249.99	52.85
	1161	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9/2011	3/2014 (N.A.) {9/2024}	2,848.00 (N.A.) {3,241.56}	3,901.66	85.45
<u>SHIPPING AND PORTS</u>	1162	JAL MARG VIKAS PROJECT (JWAI) (N25000072)	1/2018	3/2023 (Dec-25) {12/2025}	5,369.18 (4,633.81) {5,061.15}	3,059.64	60.67
<u>TELECOMMUN ICATIONS</u>	1163	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3/2020	6/2021 (Nov-21) {12/2024}	461.42 (461.42) {461.42}	159.98	81
	1164	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3/2023	3/2024 (Jul-24) {9/2024}	239.60 (N.A.) {239.60}	165.31	100
	1165	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5/2023	8/2024 (Nov-24) {11/2024}	645.13 (N.A.) {645.13}	256.00	57.86
	1166	PLANNING ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGRATION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6/2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	3,122.10	30.87

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1167	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2/2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	0.00	
	URBAN DEVELOPME N I	1168	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3/2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	22,223.13	79.7
NAGALAND	PETROLEUM	1169	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8/2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	0.20	2.1
	RAILWAYS	1170	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4/2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	3,690.86	53
	ROAD TRANSPORT AND HIGHWAYS	1171	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7/2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	62.78	56.14
		1172	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2/2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	0.00	
		1173	MERANGKONG-TAMLU-MON (MTM) PKG- 5 (NHIDCL) (N24001438)	7/2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	43.05	23.33
		1174	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6/2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	
		1175	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3/2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	109.40	55.07

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1176	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3/2021	2/2024 (Feb-25) {2/2025}	226.44 (N.A.) {226.44}	109.16	76.78
1177	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3/2022	12/2024 (N.A.) {12/2024}	605.36 (N.A.) {605.36}	214.50	78.62
1178	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2/2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	55.72	53.23
1179	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2/2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	12.83	20.02
1180	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12/2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	28.75	17.83
1181	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12/2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	10.57
1182	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12/2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	55.97	25.78
1183	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3/2016	9/2019 (Nov-22) {12/2024}	373.07 (534.41) {534.41}	382.50	99.81
1184	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3/2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	283.07	82.64

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1185	(I) CONSTRUCTION OF FOUR/SIX LANEING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2/2017	9/2020 (Feb-23) {12/2024}	387.00 (688.12) {688.12}	387.50	99.32
1186	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3/2018	11/2022 (Aug-24) {12/2024}	500.09 (698.81) {698.81}	373.62	94.43
1187	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3/2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	174.28	99.9
1188	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3/2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	104.37	23.61
1189	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3/2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	81.60	16.03
1190	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3/2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
1191	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3/2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
1192	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9/2020	10/2022 (Apr-24) {9/2024}	277.44 (N.A.) {277.44}	160.86	62.16

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1193	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8/2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	76.69	15.6
1194	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8/2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	71.92	26.96
1195	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9/2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
1196	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) (NHIDCL) (N24001280)	3/2020	6/2022 (Mar-23) {9/2023}	320.97 (N.A.) {320.97}	182.21	100
1197	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3/2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	58.37
1198	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) (NHIDCL) (N24001284)	3/2020	6/2022 (Jun-23) {6/2024}	361.53 (365.42) {365.42}	197.64	97.12
1199	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3/2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
1200	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4/2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	110.22	55.19
1201	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8/2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	39.59	1.34

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1202	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3/2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
ODISHA	COAL	1203	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5/2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	266.56	62
		1204	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2/2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,391.81	42.5
		1205	GARJANBAHAL OCP (MCL) (N06000117)	11/2014	3/2021 (N.A.) {3/2026}	1,375.38 (N.A.) {1,375.38}	826.50	58
		1206	INTEGRATED LAKHANPUR-BELPAHAR- LILARI OCP (MCL) (N06000167)	5/2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,815.42	51
		1207	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11/2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,662.42	44
		1208	TALABIRA II AND III OCP (NLC) (N06000189)	7/2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,348.18	52
		1209	NAINI COAL MINE (SCCL) (N06000203)	3/2020	3/2024 (N.A.) {3/2026}	494.30 (N.A.) {494.30}	491.33	35
		1210	BHUBANESWARI EXPANSION OCP (MCL) (N06000227)	3/2024	3/2031 (N.A.) {3/2031}	6,321.73 (N.A.) {6,321.73}	1,079.82	18
		1211	GOPALJI-KANIHA OCP (MCL) (N06000229)	4/2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,610.66	16.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1212	BALARAM EXPANSION OCP (MCL) (N06000230)	8/2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	900.15	49
	1213	KULDA EXPANSION OCP- 15 MTY (MCL) (N06000248)	6/2014	3/2018 (N.A.) {3/2026}	348.16 (N.A.) {348.16}	197.98	60
	1214	SUBHADRA OCP (MCL) (N06000249)	5/2021	3/2029 (Mar-29) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,133.49	39
	1215	RPR OF HINGULA -II EXPANSION PH-III (MCL) (N06000261)	12/2022	3/2029 (N.A.) {3/2029}	2,264.68 (N.A.) {2,264.68}	999.58	39
	1216	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1/2024	5/2029 (N.A.) {5/2029}	27,213.00 (N.A.) {27,213.00}	965.00	1.51
DEPARTMENT OF HIGHER EDUCATION	1217	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1/2019	3/2022 (N.A.) {11/2024}	790.79 (N.A.) {790.79}	653.77	93
MINES	1218	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12/2014	4/2021 (Sep-25) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,133.39	66.96
	1219	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5/2016	1/2020 (Nov-23) {3/2024}	534.00 (N.A.) {1,021.97}	750.50	73.43
	1220	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12/2015	11/2020 (Sep-25) {9/2025}	355.00 (581.00) {581.00}	109.88	12.6

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1221	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11/2017	4/2021 (May-25) {5/2025}	483.00 (483.00) {483.00}	338.72	84.79
	1222	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5/2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	641.34	46.44
	1223	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9/2019	3/2023 (May-24) {5/2024}	225.79 (44.87) {270.66}	5.00	100
PETROLEUM	1224	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11/2018	9/2021 (Dec-24) {12/2024}	462.30 (552.44) {552.44}	467.87	94.6
	1225	Fuel Quality Upgradation Project at Paradip Refinery (IOCL) (N16000362)	5/2019	8/2021 (Dec-24) {12/2024}	3,361.00 (N.A.) {3,361.00}	2,705.64	97.9
	1226	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY (IOCL) (N16000368)	6/2019	9/2022 (Dec-24) {12/2024}	427.10 (427.10) {427.10}	295.80	93.7
	1227	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7/2020	1/2024 (Apr-25) {4/2025}	13,805.00 (N.A.) {13,805.00}	6,579.95	84.6
POWER	1228	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3/2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	307.27	56
	1229	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8/2022	5/2027 (N.A.) {5/2027}	11,844.00 (N.A.) {11,844.00}	1,405.09	8.4

Table:-7. Project List: Ongoing Projects as of 31st August 2024

RAILWAYS	1230	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4/1994	3/2009 (Dec-26) {12/2026}	2,923.13 (3,791.66) {5,089.37}	4,044.31	77
	1231	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4/2005	6/2021 (N.A.) {3/2026}	810.78 (N.A.) {1,928.07}	1,448.38	
	1232	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3/2013	10/2020 (N.A.) {10/2025}	843.04 (1,284.39) {1,284.39}	1,057.59	70
	1233	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4/2015	3/2022 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,188.77	88
	1234	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4/2015	3/2022 (Mar-26) {3/2026}	2,361.74 (2,361.74) {2,361.74}	1,509.89	67
	1235	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4/2015	11/2018 (N.A.) {3/2025}	701.61 (N.A.) {810.02}	179.43	75
	1236	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4/2015	12/2018 (N.A.) {7/2025}	1,172.92 (2,087.43) {2,087.43}	1,546.52	70
	1237	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1/1991	12/2024 (N.A.) {12/2026}	2,335.67 (N.A.) {4,803.16}	4,620.71	73
	1238	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4/2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	0.00	17.4
	1239	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2/2018	7/2033 (N.A.) {7/2033}	642.69 (N.A.) {642.69}	155.37	0.1

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1240	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7/2017	7/2028 (N.A.) {7/2028}	499.99 (N.A.) {747.91}	0.00	0
	1241	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7/2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	0.00	0
	1242	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8/2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	
	1243	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9/2022	9/2027 (N.A.) {9/2027}	189.93 (N.A.) {189.93}	0.00	0
	1244	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12/2009	12/2026 (N.A.) {12/2026}	48.44 (297.00) {297.00}	0.00	0
	1245	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8/2019	8/2027 (N.A.) {8/2027}	183.00 (N.A.) {183.00}	0.00	0
	1246	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9/2022	9/2026 (N.A.) {3/2026}	209.75 (N.A.) {244.99}	34.31	8
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1247	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHAI) (N24001647)	8/2020	3/2022 (N.A.) {9/2024}	200.00 (154.73) {154.73}	137.04	100
	1248	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE- OD-8 (NHAI) (N24001665)	12/2021	10/2024 (N.A.) {8/2025}	1,592.00 (1,592.00) {1,592.00}	775.94	55.58

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1249	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE- OD (NHAI) (N24001666)	12/2021	9/2024 (N.A.) {10/2025}	714.00 (714.00) {714.00}	395.27	63.95
1250	6L GREENFIELD KALIAGURA ? BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHAI) (N24001667)	9/2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	992.00	70.02
1251	6L OF BADAUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH- 130-CD (PACKAGE ? OD-3) (NHAI) (N24001668)	3/2021	4/2024 (N.A.) {3/2025}	1,249.00 (N.A.) {1,249.00}	403.00	68.7
1252	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH- 130-CD (PACKAGE ? OD-1) (NHAI) (N24001669)	2/2021	3/2024 (N.A.) {3/2025}	586.00 (N.A.) {586.00}	185.26	60.9
1253	6L OF KARKI ? KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH- 130-CD (PACKAGE ? OD-4) (NHAI) (N24001670)	2/2021	3/2024 (N.A.) {12/2024}	593.00 (N.A.) {593.00}	250.22	83.88
1254	6L OF HATIBENA - BADAUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE ? OD-2) (NHAI) (N24001671)	2/2021	3/2024 (N.A.) {10/2024}	925.00 (N.A.) {925.00}	396.59	94.91
1255	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE ? (NHAI) (N24001678)	8/2021	6/2024 (N.A.) {6/2025}	1,460.00 (1,460.00) {1,460.00}	786.00	73.75
1256	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6/2020	12/2023 (Dec-24) {12/2024}	414.24 (N.A.) {414.24}	250.41	80

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1257	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR-BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3/2022	6/2025 (Jun-25) {6/2025}	499.79 (N.A.) {499.79}	218.62	48
1258	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3/2021	3/2024 (Mar-25) {3/2025}	196.94 (N.A.) {196.94}	63.67	34
1259	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1/2022	4/2025 (Apr-25) {4/2025}	300.33 (N.A.) {300.33}	159.82	47
1260	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2/2022	11/2024 (Mar-25) {3/2025}	157.49 (N.A.) {157.49}	59.32	16
1261	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESIGN KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2/2022	10/2025 (Nov-25) {11/2025}	238.78 (N.A.) {238.78}	9.89	20
1262	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3/2021	6/2024 (Jun-26) {6/2026}	154.05 (N.A.) {154.05}	47.47	22
1263	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11/2021	6/2025 (Jun-25) {6/2025}	154.49 (N.A.) {154.49}	45.22	16
1264	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12/2021	5/2025 (May-25) {5/2025}	324.09 (N.A.) {324.09}	70.05	15

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1265	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12/2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	96.90	17.62
1266	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12/2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	122.14	22.62
1267	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12/2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	130.24	22.12
1268	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8/2022	1/2025 (N.A.) {6/2025}	153.61 (N.A.) {153.61}	0.00	15.6
1269	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3/2022	2/2026 (Feb-26) {2/2026}	186.52 (186.52) {186.52}	12.15	12
1270	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3/2022	2/2026 (Feb-26) {2/2026}	636.10 (N.A.) {636.10}	19.26	6
1271	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9/2016	8/2019 (N.A.) {10/2024}	2,510.04 (N.A.) {2,510.04}	1,104.98	97
1272	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12/2017	7/2020 (N.A.) {12/2024}	686.65 (565.00) {686.65}	559.26	86

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1273	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE ((NHAI) (N24000733)	1/2018	8/2022 (N.A.) {2/2025}	633.68 (492.83) {633.68}	560.38	80
	1274	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1/2018	8/2021 (N.A.) {9/2024}	614.48 (503.30) {757.12}	664.48	98
	1275	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1/2018	9/2020 (N.A.) {12/2024}	686.65 (504.09) {1,015.16}	435.85	79
	1276	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (NHAI) (N24000738)	1/2018	9/2021 (N.A.) {3/2025}	999.00 (1,152.70) {1,152.70}	339.23	76.48
	1277	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (NHAI) (N24000739)	1/2018	6/2021 (Dec-24) {12/2024}	503.88 (609.03) {609.03}	536.89	92.12
	1278	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8/2016	2/2017 (Sep-24) {9/2024}	287.70 (5.96) {293.66}	272.95	96
	1279	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12/2016	8/2018 (Sep-24) {9/2024}	223.50 (N.A.) {223.50}	220.50	92
	1280	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3/2018	8/2018 (Oct-24) {10/2024}	199.16 (N.A.) {199.16}	155.44	98
STEEL	1281	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11/2020	5/2023 (N.A.) {9/2024}	377.18 (N.A.) {377.18}	397.89	85.69

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1282	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (<i>SAIL</i>) (<i>N12000125</i>)	1/2022	5/2025 (N.A.) {5/2025}	970.18 (N.A.) {970.18}	430.03	60.4
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1283	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (<i>CPWD EDUCATION</i>) (<i>N28000142</i>)	10/2019	5/2022 (N.A.) {12/2024}	348.24 (N.A.) {348.24}	273.00	86
	PETROLEUM	1284	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (<i>HPCL</i>) (<i>N16000402</i>)	5/2020	2/2023 (Sep-24) {9/2024}	1,421.46 (N.A.) {1,421.46}	1,023.34	94.5
		1285	BHATINDA SANGRUR PIPELINE (<i>HPCL</i>) (<i>N16000440</i>)	11/2021	5/2024 (N.A.) {2/2025}	367.00 (N.A.) {367.00}	280.09	82.2
		1286	CGD PROJECT AT PATHANKOT DISTRICT (<i>IOCL</i>) (<i>N16000488</i>)	3/2022	3/2030 (N.A.) {9/2033}	151.00 (N.A.) {151.00}	8.35	1.5
	RAILWAYS	1287	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (<i>NR</i>) (<i>N22000502</i>)	6/2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	60
		1288	LUDHIANA MULLANPUR DOUBLING (<i>NR</i>) (<i>N22000589</i>)	9/2020	3/2025 (N.A.) {3/2025}	82.99 (N.A.) {235.00}	0.00	0
		1289	RAJPURA-BHATINDA (172.64 KM) (<i>MEGA</i>) (<i>N22000597</i>)	6/2017	3/2024 (N.A.) {3/2024}	1,775.73 (N.A.) {1,775.73}	0.00	0
		1290	FEROZPUR - PATTI (25.72 KM) (<i>NR</i>) (<i>N22000614</i>)	4/2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {299.74}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

ROAD TRANSPORT AND HIGHWAYS	1291	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 (NHAI) (N24001414)	12/2020	1/2024 (May-24) {7/2024}	733.00 (908.28) {908.28}	868.44	95.33
	1292	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA- BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12/2020	4/2024 (Jul-24) {7/2024}	881.00 (N.A.) {881.00}	857.66	88.48
	1293	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA- MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12/2020	1/2024 (Mar-25) {3/2025}	989.66 (N.A.) {989.66}	319.95	31.08
	1294	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA- MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12/2020	4/2024 (Jul-24) {7/2024}	1,234.40 (N.A.) {1,234.40}	744.28	57.04
	1295	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12/2020	4/2024 (Jul-24) {7/2024}	1,094.46 (N.A.) {1,094.46}	757.42	59.56
	1296	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2/2021	4/2024 (Nov-24) {11/2024}	1,269.96 (N.A.) {1,269.96}	584.69	42.88
	1297	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA- SRIHARGOBINDPUR- (NHAI) (N24001420)	2/2021	4/2024 (N.A.) {4/2024}	853.66 (N.A.) {853.66}	105.17	12.45
	1298	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V (NHAI) (N24001514)	1/2021	1/2024 (Oct-24) {10/2024}	1,060.29 (N.A.) {1,060.29}	975.55	98

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1299	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7/2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	270.00	59
1300	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3/2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	270.00	66
1301	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-V) FROM (NHAI) (N24001632)	1/2021	5/2024 (N.A.) {4/2025}	1,741.86 (N.A.) {1,741.86}	1,118.93	75.1
1302	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA ? RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5/2021	12/2024 (Dec-24) {12/2024}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
1303	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3/2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	923.84	24.3
1304	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11/2021	7/2024 (Dec-24) {12/2024}	646.42 (646.42) {646.42}	481.67	90
1305	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5/2020	12/2024 (Aug-25) {8/2025}	864.23 (864.23) {864.23}	434.88	33
1306	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3/2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	635.39	28.61
1307	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3/2021	10/2024 (Sep-25) {9/2025}	1,641.75 (N.A.) {1,641.75}	164.43	22.51

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1308	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2/2021	8/2024 (Mar-25) {3/2025}	1,474.77 (N.A.) {1,474.77}	384.91	61.04
1309	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12/2020	6/2024 (Jun-25) {6/2025}	857.91 (N.A.) {857.91}	127.71	30.52
1310	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12/2020	9/2023 (Sep-24) {9/2024}	524.88 (416.58) {416.58}	157.14	69
1311	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0 (NHAI) (N24001645)	12/2020	6/2023 (Feb-24) {2/2024}	366.85 (366.85) {366.85}	519.77	100
1312	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR-MUKTS (MoRTH) (N24001960)	3/2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	30.00	21
1313	WORK OF WIDENING/UPGRADATION OF 2-LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3/2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	33.45	20
1314	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12/2020	8/2025 (Aug-25) {8/2025}	757.13 (757.00) {757.00}	246.51	87
1315	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3/2021	10/2025 (Oct-25) {10/2025}	2,029.17 (2,029.00) {2,029.00}	84.23	23

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1316	6L ACCESS CONTROLLED LUDHIANA-BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6/2021	9/2025 (Sep-25) {9/2025}	906.51 (906.51) {906.51}	134.05	25.5
1317	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70) (NHAI) (N24002092)	3/2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	795.98	12.5
1318	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3/2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	73.00	27
1319	4L OF EXISTING BEAS ? BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10/2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	219.90	58.02
1320	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8/2021	6/2025 (N.A.) {6/2025}	809.51 (N.A.) {809.51}	125.89	35.23
1321	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1/2020	4/2026 (N.A.) {4/2026}	2,165.23 (N.A.) {2,165.23}	114.71	13.47
1322	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3/2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100
1323	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10/2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	62

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1324	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3/2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	104.98	79
		1325	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941)	3/2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100
RAJASTHAN	ATOMIC ENERGY	1326	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) (NPCIL) (N02000027)	10/2009	12/2016 (N.A.) {12/2026}	12,320.00 (22,924.00) {22,924.00}	18,932.00	92.07
	CIVIL AVIATION	1327	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5/2022	11/2024 (N.A.) {6/2025}	480.00 (N.A.) {480.00}	106.15	47
		1328	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6/2023	3/2026 (N.A.) {3/2026}	887.00 (N.A.) {887.00}	106.59	25.68
	COAL	1329	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3/2023	9/2024 (N.A.) {9/2024}	1,813.00 (N.A.) {1,813.00}	402.12	26.67
	PETROLEUM	1330	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12/2021	10/2024 (Dec-24) {12/2024}	9,028.00 (N.A.) {9,028.00}	5,565.28	63.25
		1331	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAU DISTRICTS (IOCL) (N16000489)	3/2022	3/2030 (N.A.) {3/2031}	575.00 (N.A.) {575.00}	110.06	7.3
		1332	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAU LI (HPCL) (N16000496)	3/2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	177.72	18.7

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1333	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12/2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	15.11	15.2
	1334	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10/2017	10/2022 (Mar-25) {3/2025}	43,129.00 (72,937.00) {72,937.00}	49,210.06	81.5
	1335	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12/2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	165.83	16.2
POWER	1336	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3/2020	9/2021 (N.A.) {9/2024}	1,782.00 (N.A.) {1,782.00}	1,279.42	0
	1337	ANTA SOLAR 90 MW (NTPC) (N18000292)	1/2021	3/2022 (N.A.) {3/2022}	382.22 (N.A.) {382.22}	497.17	0
	1338	BHENSARA 320 MW (NTPC) (N18000293)	1/2021	7/2022 (N.A.) {7/2022}	1,221.73 (N.A.) {1,221.73}	719.49	0
	1339	CHHATTARGARH 150 MW (NTPC) (N18000294)	2/2021	7/2022 (Mar-24) {3/2024}	599.99 (N.A.) {599.99}	243.12	0
	1340	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000300)	5/2021	9/2022 (N.A.) {8/2024}	1,184.88 (N.A.) {1,184.88}	840.52	97
	1341	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000305)	6/2021	12/2022 (N.A.) {8/2024}	713.82 (N.A.) {713.82}	671.59	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1342	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000306)	6/2021	12/2022 (N.A.) {12/2024}	1,562.00 (N.A.) {1,562.00}	1,161.25	92
1343	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000307)	6/2021	12/2022 (N.A.) {12/2024}	1,006.00 (N.A.) {1,006.00}	879.31	95
1344	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3/2022	8/2023 (N.A.) {9/2024}	1,352.71 (N.A.) {1,352.71}	359.51	0
1345	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3/2022	8/2023 (N.A.) {9/2024}	1,409.52 (N.A.) {1,409.52}	632.99	0
1346	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3/2022	8/2023 (N.A.) {9/2024}	1,426.94 (N.A.) {1,426.94}	362.86	0
1347	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6/2022	3/2024 (N.A.) {12/2024}	2,598.92 (N.A.) {2,598.92}	468.43	0
1348	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3/2023	9/2024 (N.A.) {12/2024}	1,433.28 (N.A.) {1,433.28}	485.77	40
1349	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5/2022	11/2023 (N.A.) {3/2025}	1,677.12 (N.A.) {1,677.12}	711.16	60
1350	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372)	6/2023	1/2025 (N.A.) {12/2024}	202.39 (N.A.) {202.39}	20.04	53

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1351	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8/2023	2/2025 (N.A.) {2/2025}	688.74 (N.A.) {688.74}	121.10	18
1352	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10/2023	4/2025 (N.A.) {4/2025}	2,211.00 (N.A.) {2,211.00}	183.03	12
1353	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10/2023	4/2025 (N.A.) {4/2025}	1,796.00 (N.A.) {1,796.00}	344.08	11
1354	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9/2023	4/2025 (N.A.) {4/2025}	2,191.00 (N.A.) {2,191.00}	431.06	12
1355	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12/2022	3/2025 (N.A.) {8/2025}	331.00 (N.A.) {331.00}	7.66	26
1356	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11/2023	6/2025 (N.A.) {6/2025}	428.00 (N.A.) {428.00}	0.00	1
1357	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12/2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	107.08	3
1358	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12/2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	122.70	8

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1359	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSION] (MEGA) (N18000389)	2/2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	0.00	0
<u>RAILWAYS</u>	1360	DAUSA-GANGAPUR CITY(NL),NWR (NWR) (220100184)	2/1997	2/2019 (N.A.) {3/2024}	410.08 (N.A.) {1,020.00}	1,056.05	100
	1361	AGRA FORT-BANDIKUI (NCR) (N22000553)	6/2022	6/2027 (N.A.) {5/2026}	1,389.81 (N.A.) {987.83}	0.24	11
	1362	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4/2019	3/2025 (N.A.) {3/2025}	528.48 (N.A.) {528.48}	320.00	67
	1363	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11/2021	11/2026 (N.A.) {12/2024}	466.42 (N.A.) {466.42}	535.01	70
	1364	DOUBLING BETWEEN CHURU-RATANGARH (42.81 KM) (NWR) (N22000605)	2/2023	2/2028 (N.A.) {1/2026}	422.60 (N.A.) {422.60}	103.92	37
	1365	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NWR) (N22000607)	12/2022	6/2026 (N.A.) {12/2025}	304.00 (239.54) {239.54}	62.98	20
	1366	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1/2023	6/2028 (N.A.) {1/2027}	968.92 (N.A.) {968.92}	182.81	17
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1367	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. (MoRTH) (N24001411)	12/2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	231.12	88
	1368	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12/2021	5/2024 (N.A.) {12/2024}	411.40 (N.A.) {411.40}	157.61	51

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1369	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1/2022	12/2024 (N.A.) {12/2024}	194.88 (N.A.) {194.88}	104.69	60
1370	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12/2021	8/2024 (N.A.) {10/2024}	451.66 (N.A.) {451.66}	401.78	97
1371	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12/2021	9/2024 (N.A.) {3/2025}	150.11 (N.A.) {150.11}	57.33	59
1372	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3/2022	11/2024 (Dec-24) {12/2024}	1,636.15 (N.A.) {1,636.15}	659.29	76.25
1373	4L OF KARWAR (KM. 281.980 OF NH-62 NAGAU ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11/2021	8/2024 (Oct-24) {10/2024}	736.75 (N.A.) {736.75}	216.39	73.1
1374	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE - 0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9/2021	6/2024 (Dec-24) {12/2024}	672.35 (N.A.) {672.35}	358.69	91.01
1375	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561)	10/2019	10/2023 (Aug-24) {8/2024}	839.63 (N.A.) {839.63}	213.85	100
1376	DEOGARH (NEAR DHANDHANIYA)-RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10/2019	8/2023 (Aug-24) {8/2024}	846.59 (N.A.) {846.59}	145.98	97.8

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1377	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE- I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10/2019	7/2023 (Aug-24) {8/2024}	662.08 (N.A.) {662.08}	110.81	96.5
1378	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566)	11/2019	5/2023 (Aug-24) {8/2023}	1,640.10 (N.A.) {1,640.10}	1,159.13	100
1379	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11/2019	10/2022 (Nov-24) {11/2024}	1,272.97 (N.A.) {1,272.97}	595.43	82.72
1380	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11/2019	5/2023 (Aug-24) {8/2024}	1,119.35 (N.A.) {1,119.35}	1,433.58	99.8
1381	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569)	11/2019	3/2023 (Jun-24) {6/2024}	1,425.02 (N.A.) {1,425.02}	1,373.31	100
1382	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571)	11/2019	12/2023 (Aug-24) {8/2024}	1,341.36 (N.A.) {1,341.36}	1,085.34	99.55
1383	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11/2019	12/2022 (Sep-24) {9/2024}	1,658.06 (N.A.) {1,658.06}	180.39	99.9
1384	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7/2020	1/2024 (Sep-25) {9/2025}	1,788.69 (N.A.) {1,788.69}	798.73	65.02

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1385	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3/2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	64
1386	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3/2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	104.08	61
1387	Sagwara Bypass and Garhi- Partapur Bypass of NH-927A in the State of Rajasthan. (MoRTH) (N24001868)	3/2022	8/2025 (N.A.) {2/2025}	187.65 (N.A.) {187.65}	66.57	40
1388	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12/2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	92.29	58
1389	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2/2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	207.87	38
1390	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3/2022	4/2025 (N.A.) {4/2025}	317.74 (N.A.) {317.74}	136.23	3.6
1391	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8/2022	6/2024 (N.A.) {6/2025}	409.64 (N.A.) {409.64}	184.57	41.28
1392	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA (NHAI) (N24000795)	2/2018	4/2021 (Sep-24) {9/2024}	741.86 (649.00) {649.00}	672.53	96

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1393	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241)	3/2020	10/2022 (Dec-24) {12/2024}	255.23 (N.A.) {255.23}	255.00	94
SIKKIM	CIVIL AVIATION	1394	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11/2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	6.01	3
	DEPARTMENT OF HIGHER EDUCATION	1395	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8/2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	135.81	45
	POWER	1396	TEESTA VI HE PROJECT (NHPC) (N18000325)	3/2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,671.26	63.26
		1397	RANGIT IV HE PROJECT (NHPC) (N18000326)	3/2021	5/2024 (N.A.) {5/2025}	938.29 (N.A.) {1,871.23}	1,216.54	78.54
	RAILWAYS	1398	SEVOK RANGPO, NEFR (NFR) (N22000102)	4/2008	12/2015 (N.A.) {12/2023}	1,339.48 (N.A.) {7,876.92}	3,290.96	39.8
	ROAD TRANSPORT AND HIGHWAYS	1399	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10/2021	5/2024 (Jan-25) {1/2025}	385.15 (N.A.) {385.15}	167.49	75
		1400	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3/2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	0.00	71.74
		1401	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3/2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.51	95.26

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1402	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11/2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	96.98
1403	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3/2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	234.88	72.99
1404	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8/2020	4/2023 (Aug-23) {1/2025}	295.97 (N.A.) {295.97}	243.68	93.13
1405	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3/2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
1406	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8/2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	240.56	93.88
1407	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7/2020	4/2023 (Oct-23) {8/2024}	345.38 (395.59) {395.59}	355.08	88.69
1408	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9/2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.16	46.04
1409	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9/2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1410	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8/2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	179.62	49.22
		1411	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8/2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	200.82	77.2
		1412	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10/2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	266.57	39.65
		1413	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10/2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	278.06	35.22
		1414	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1/2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {332.20}	148.62	40.82
		1415	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12/2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	186.64	42.11
TAMIL NADU	ATOMIC ENERGY	1416	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) (BHAVNI) (020100044)	9/2003	9/2010 (N.A.) {3/2025}	3,492.00 (N.A.) {7,670.00}	6,921.72	98
		1417	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 (NPCIL) (N02000028)	3/2013	11/2020 (N.A.) {11/2026}	39,849.00 (68,893.00) {68,893.00}	44,808.00	73.47
		1418	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 (NPCIL) (N02000029)	6/2017	9/2027 (N.A.) {9/2027}	49,621.00 (N.A.) {49,621.00}	17,318.00	29.39

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>CIVIL AVIATION</u>	1419	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6/2018	2/2022 (N.A.) {12/2025}	2,467.00 (N.A.) {2,467.00}	1,497.89	58
	1420	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8/2018	10/2021 (N.A.) {12/2023}	951.28 (N.A.) {1,112.49}	1,112.49	100
	1421	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6/2019	3/2022 (Sep-24) {9/2024}	380.87 (452.93) {452.93}	308.18	90
<u>COAL</u>	1422	JAWAHAR KHANI OPENCASE (JK OC) MINE (SCCL) (N06000259)	12/2021	3/2025 (N.A.) {3/2025}	297.88 (N.A.) {297.88}	45.15	20
<u>FINANCE</u>	1423	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11/2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100
<u>MINES</u>	1424	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9/2017	6/2019 (Mar-24) {12/2024}	166.62 (163.17) {163.17}	135.63	65
<u>PETROLEUM</u>	1425	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11/2012	2/2017 (Oct-25) {10/2025}	678.00 (1,732.00) {1,732.00}	532.04	39.7
	1426	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE (IOCL) (N16000253)	5/2016	12/2018 (Mar-25) {3/2025}	4,497.00 (6,025.00) {6,025.00}	5,513.79	93.06
	1427	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI (IOCL) (N16000403)	10/2020	9/2023 (Dec-24) {12/2024}	921.00 (N.A.) {921.00}	720.11	90.9

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1428	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI (IOCL) (N16000405)	10/2020	12/2023 (Dec-24) {12/2024}	1,398.00 (1,587.00) {1,587.00}	1,178.60	91.5
1429	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1/2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,220.46	10.1
1430	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1/2022	7/2024 (Dec-24) {6/2025}	827.00 (887.71) {887.71}	464.08	72.1
1431	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE (IOCL) (N16000451)	3/2022	11/2024 (N.A.) {11/2024}	564.00 (N.A.) {564.00}	144.55	35.67
1432	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1/2022	7/2024 (May-26) {5/2026}	829.00 (N.A.) {829.00}	209.55	49.61
1433	EXTENSION OF ASANUR-SANKARI SECTION OF CHENNAI-TRICHY-MADURAI PIPELINE UPTO COIMBATORE (IRUGUR) (IOCL) (N16000479)	1/2023	1/2025 (N.A.) {1/2025}	346.70 (N.A.) {346.70}	0.72	17.25
1434	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3/2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	73.44	3.7
1435	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS (IOCL) (N16000490)	3/2022	3/2030 (N.A.) {12/2030}	1,328.00 (N.A.) {1,328.00}	142.13	4
1436	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS (IOCL) (N16000492)	3/2022	3/2030 (N.A.) {12/2030}	1,295.00 (N.A.) {1,295.00}	129.73	4.1

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1437	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12/2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	80.69	4.4
RAILWAYS	1438	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTP) (N22000028)	4/2006	6/2013 (Oct-24) {12/2024}	495.74 (N.A.) {734.01}	628.07	98
	1439	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI (SR) (N22000079)	9/2007	2/2019 (N.A.) {3/2027}	724.69 (N.A.) {3,118.34}	1,926.20	78
	1440	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9/2006	(Dec-26) {3/2027}	582.83 (N.A.) {3,631.34}	773.92	10
	1441	Chinnasalem-Kallakurichi New Line (MM of cuddalore- Salem 191 KM) (SR) (N22000567)	1/2006	3/2025 (Aug-24) {12/2025}	417.50 (N.A.) {419.44}	199.70	75
	1442	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SR) (N22000568)	3/2022	3/2026 (Aug-24) {12/2024}	359.60 (274.20) {274.20}	212.74	70
	1443	MORAPPUR-DHARMAPURI (SR) (N22000618)	2/2019	3/2028 (Mar-27) {3/2027}	358.95 (N.A.) {358.95}	37.12	1
	1444	KARAIKAL - PERALAM NEW LINE (MM OF TIRUCHCHIRAPPALLI-NAGORE-KARAIKAL) (SR) (N22000625)	1/2019	3/2026 (Sep-24) {12/2024}	304.22 (N.A.) {373.42}	302.47	72
	1445	NAGAPATTINAM- THIRUTURAI PUNDI VIA THIRUKUVALAI NEW LINE (MM OF TIRUCHCHIRAPPALLI-NAGORE-KARAIKAL) (SR) (N22000626)	7/2008	3/2026 (Mar-27) {3/2027}	677.12 (N.A.) {788.05}	167.05	17

Table:-7. Project List: Ongoing Projects as of 31st August 2024

ROAD TRANSPORT AND HIGHWAYS	1446	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH- 45A ON (NHAI) (N24001428)	3/2018	11/2021 (Dec-24) {12/2024}	998.70 (1,358.32) {1,358.32}	868.82	96.33
	1447	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3/2018	11/2021 (Dec-24) {12/2024}	1,294.47 (1,588.40) {1,588.40}	852.39	93.7
	1448	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3/2018	1/2022 (Dec-24) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,432.44	99.18
	1449	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3/2018	10/2020 (Aug-25) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,091.58	49.2
	1450	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2/2022	8/2022 (N.A.) {10/2024}	191.33 (N.A.) {191.33}	142.11	80
	1451	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10/2020	5/2023 (Dec-24) {12/2024}	434.12 (N.A.) {434.12}	258.89	99
	1452	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1/2019	1/2023 (Mar-25) {3/2025}	1,051.69 (N.A.) {1,051.69}	540.79	75.11
	1453	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001602)	1/2019	12/2022 (Jan-25) {1/2025}	1,409.38 (N.A.) {1,409.38}	618.30	85.4

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1454	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHAI) (N24001603)	1/2019	10/2022 (Dec-23) {12/2023}	1,518.53 (N.A.) {1,607.54}	915.40	100
1455	REMAINING WORK OF 2L+PS OF TRICHY - KARAUKUDI SECTION OF NH- 210, INCLUDING TRICHY BYPASS (NHAI) (N24001604)	2/2019	3/2021 (N.A.) {10/2023}	166.90 (N.A.) {166.90}	121.94	100
1456	4-LANING OF MELUR - PILLAYARPATTI - KARAUKUDI SECTION OF NH-338, NH-36, NH-383 (NHAI) (N24001605)	6/2018	3/2022 (N.A.) {1/2025}	1,103.86 (N.A.) {1,103.86}	461.32	68.04
1457	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHAI) (N24001606)	12/2018	3/2022 (Mar-25) {3/2025}	854.94 (N.A.) {854.94}	334.05	64.54
1458	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHAI) (N24001692)	1/2022	9/2024 (N.A.) {9/2024}	467.99 (N.A.) {468.00}	18.83	12.2
1459	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHAI) (N24001693)	9/2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	
1460	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHAI) (N24001694)	2/2019	12/2023 (Dec-24) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	
1461	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG-III) FROM KM.60+100 TO KM.94+460 (NHAI) (N24001696)	2/2019	8/2023 (Dec-24) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1462	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7/2022	8/2023 (Dec-24) {12/2024}	186.50 (210.81) {210.81}	12.92	85
1463	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11/2020	8/2024 (N.A.) {3/2025}	1,155.49 (1,458.45) {1,458.45}	444.56	51.61
1464	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12/2020	7/2024 (N.A.) {11/2024}	843.48 (1,051.36) {1,051.36}	389.23	81.92
1465	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2/2021	7/2024 (N.A.) {2/2025}	2,948.31 (3,516.83) {3,516.83}	728.20	62.84
1466	BANGALORE CHENNAI EXPRESSWAY PHASE-III ? PACKAGE I (GUDIPALA TO WALAJHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10/2020	5/2024 (N.A.) {12/2024}	1,023.91 (1,341.51) {1,341.51}	513.56	67.15
1467	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2/2019	5/2024 (N.A.) {8/2025}	1,008.99 (1,360.53) {1,360.53}	163.53	35.15
1468	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11/2021	2/2023 (N.A.) {9/2024}	463.44 (463.44) {463.44}	331.01	98.5
1469	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10/2018	2/2021 (N.A.) {3/2025}	707.90 (766.51) {766.51}	401.98	78.42

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1470	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1/2019	5/2021 (N.A.) {3/2026}	819.89 (N.A.) {922.85}	370.91	57.32
1471	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 ? 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1/2022	11/2024 (N.A.) {11/2024}	221.03 (243.95) {243.95}	119.28	70
1472	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10/2022	11/2024 (N.A.) {11/2024}	172.15 (N.A.) {172.15}	72.66	66.6
1473	CONSTRUCTION OF STRR (WEST SIDE)- NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4/2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	412.90	42.1
1474	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3/2022	2/2025 (N.A.) {3/2025}	1,076.97 (N.A.) {1,076.97}	325.73	57.68
1475	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3/2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	
1476	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3/2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	
1477	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3/2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1478	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3/2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	
1479	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2/2019	12/2025 (Dec-25) {12/2025}	825.94 (1,116.13) {1,116.13}	134.54	19.03
1480	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3/2023	7/2024 (N.A.) {1/2025}	200.30 (N.A.) {200.30}	47.11	64.04
1481	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3/2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	177.05	18.75
1482	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2/2022	4/2025 (N.A.) {4/2025}	1,097.59 (N.A.) {1,317.06}	464.09	66.48
1483	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3/2022	1/2024 (N.A.) {7/2025}	257.14 (295.00) {295.00}	56.29	0
1484	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3/2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	101.44	48
1485	STRENGTHENING OF 2L+PS FROM KM 17/8 ? 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3/2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	43.21	30

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1486	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. (NHAI) (N24000652)	3/2017	3/2020 (May-24) {5/2024}	848.45 (N.A.) {848.45}	303.04	48.26
		1487	FOUR LANNING OF CHOLOPURAM-THANJAVUR (NHAI) (N24000697)	8/2017	9/2020 (Sep-24) {9/2024}	1,176.37 (N.A.) {1,176.37}	1,293.59	94.85
		1488	4-LANNING OF STHIYATHOPU-CHOLOPURAM (NHAI) (N24000708)	9/2017	8/2020 (Nov-24) {11/2024}	1,227.87 (N.A.) {1,227.87}	1,301.26	88.3
		1489	FOUR LANINIG OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3/2018	10/2022 (Jan-24) {1/2024}	505.35 (N.A.) {837.69}	376.61	99.75
		1490	FOUR LANING OF MADURAI-CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) (NHAI) (N24000827)	3/2018	11/2020 (Apr-23) {4/2023}	628.71 (N.A.) {756.13}	583.02	100
	URBAN DEVELOPMEN I	1491	CHENNAI METRO RAIL LTD (PHASE 1) (CMRL) (N28000084)	2/2009	12/2015 (N.A.) {12/2015}	14,600.00 (N.A.) {18,380.00}	17,619.68	100
		1492	CHENNAI METRO RAIL LTD (PHASE 1 EXT) (CMRL) (N28000097)	6/2016	3/2018 (N.A.) {2/2021}	3,770.00 (N.A.) {3,770.00}	2,527.73	100
	TELANGANA	1493	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5/2020	5/2022 (Jun-23) {6/2023}	353.61 (N.A.) {353.61}	303.22	100
		1494	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 (SCCL) (N06000161)	3/2017	3/2022 (N.A.) {3/2025}	413.84 (N.A.) {413.84}	379.13	60

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1495	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7/2019	3/2023 (N.A.) {3/2025}	438.98 (N.A.) {438.98}	152.32	68
	1496	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10/2020	3/2023 (N.A.) {3/2026}	484.51 (N.A.) {484.51}	150.64	30
	1497	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT (SCCL) (N06000210)	11/2015	3/2023 (N.A.) {3/2025}	489.62 (N.A.) {489.62}	405.54	70
	1498	RCE OF INDARAM OPENCAST PROJECT (SCCL) (N06000211)	8/2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	335.24	80
	1499	RCE OF KALYANIKHANI OPENCAST PROJECT (SCCL) (N06000213)	3/2016	3/2020 (N.A.) {3/2025}	384.32 (N.A.) {384.32}	241.21	75
	1500	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8/2017	3/2020 (N.A.) {3/2025}	442.42 (N.A.) {442.42}	174.29	63
	1501	GOLETI OPENCAST MINE (SCCL) (N06000258)	7/2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	50.25	18
<u>HEALTH AND FAMILY WELFARE</u>	1502	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10/2016	3/2020 (Sep-24) {9/2024}	209.84 (281.05) {281.05}	248.43	97.5
	1503	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12/2018	7/2024 (Feb-25) {2/2025}	1,110.55 (1,110.55) {1,110.55}	576.80	73.13
<u>POWER</u>	1504	TELANGANA SUPER THERMAL POWER PROJECT PHASE I (NTPC) (N18000212)	1/2016	11/2020 (Jul-22) {2/2024}	10,598.98 (N.A.) {10,998.00}	10,437.71	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>RAILWAYS</u>	1505	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4/2006	3/2010 (N.A.) {3/2025}	1,160.48 (N.A.) {3,014.00}	1,262.17	
	1506	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K (SCR) (N22000432)	4/2017	3/2022 (N.A.) {3/2022}	119.73 (185.00) {242.28}	54.15	50
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1507	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8/2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	452.54	53.12
	1508	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2/2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	324.52	52.35
	1509	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9/2022	2/2024 (Dec-24) {12/2024}	804.69 (N.A.) {804.69}	410.66	60.78
	1510	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1/2021	1/2024 (Dec-24) {12/2024}	1,307.95 (N.A.) {1,307.95}	531.40	95
	1511	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3/2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	162.55	27.54
	1512	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12/2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	209.49	39.61

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1513	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1/2022	1/2025 (N.A.) {1/2025}	1,227.57 (N.A.) {1,227.57}	4.98	0.95
1514	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2/2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	8.38	2.14
1515	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3/2021	7/2024 (N.A.) {8/2024}	317.19 (N.A.) {317.19}	162.21	67
1516	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1/2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	235.63	54.58
1517	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1/2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	198.05	63.1
1518	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1/2022	12/2024 (N.A.) {3/2025}	549.28 (N.A.) {549.28}	156.95	51.55
1519	REHABILITATION AND UPGRADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6-LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3/2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	264.25	61.92
1520	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3/2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	205.53	58.17

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1521	CONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH-202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10/2017	6/2023 (N.A.) {12/2024}	186.71 (N.A.) {186.71}	165.61	82.23
1522	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3/2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	100.69	39.36
1523	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET-ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1/2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	172.76	68.9
1524	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR ? CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1/2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	248.79	43.93
1525	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3/2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	42.69	13.75
1526	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2/2022	9/2024 (N.A.) {9/2024}	541.58 (N.A.) {541.58}	20.82	
1527	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3/2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,413.00}	740.91	42.8
1528	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1/2014	3/2016 (Sep-19) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1529	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR) (MoRTH) (N24000247)	10/2014	2/2017 (Dec-22) {3/2025}	295.47 (N.A.) {295.47}	224.42	80.07
1530	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3/2015	1/2017 (N.A.) {12/2023}	153.21 (N.A.) {153.21}	100.96	93.11
1531	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10/2016	2/2019 (Jun-22) {8/2024}	298.32 (N.A.) {298.32}	178.47	98
1532	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10/2016	3/2019 (Apr-23) {8/2024}	248.83 (N.A.) {248.83}	173.82	100
1533	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1/2017	5/2019 (Aug-19) {8/2019}	244.54 (N.A.) {244.54}	176.32	99.9
1534	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1/2017	10/2019 (Oct-19) {2/2024}	196.52 (N.A.) {196.52}	125.53	95.7
1535	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1/2017	12/2019 (Dec-19) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.3
1536	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1/2017	5/2019 (Jul-21) {1/2024}	300.00 (N.A.) {300.00}	242.86	96.05

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1537	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1/2018	5/2020 (Dec-22) {8/2024}	283.15 (N.A.) {283.15}	278.69	92.59
1538	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1/2018	12/2019 (Nov-20) {11/2020}	230.03 (N.A.) {230.03}	231.33	99.9
1539	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2/2018	6/2020 (Jan-21) {1/2021}	206.13 (N.A.) {206.13}	190.94	98.36
1540	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2/2018	11/2019 (Mar-22) {1/2024}	294.13 (N.A.) {294.13}	198.75	86.46
1541	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3/2018	9/2020 (Jun-22) {6/2023}	322.81 (N.A.) {322.81}	317.03	98.09
1542	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE- CONGES (MoRTH) (N24000994)	3/2018	7/2020 (Jun-24) {2/2026}	626.76 (N.A.) {626.76}	274.02	44.21
1543	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1/2017	10/2019 (Oct-19) {6/2021}	605.08 (N.A.) {605.08}	416.32	99.84
1544	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL ? MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3/2018	7/2019 (Jun-22) {8/2024}	192.67 (N.A.) {192.67}	176.37	92

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1545	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (<i>MoRTH</i>) (<i>N24000998</i>)	1/2019	(Jan-23) {8/2024}	193.19 (249.72) {249.72}	222.58	95
TRIPURA	PETROLEUM	1546	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (<i>IOCL</i>) (<i>N16000495</i>)	6/2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	298.34	62.5
	RAILWAYS	1547	AGARTALA-AKHAURA NL (<i>NFR</i>) (<i>N22000195</i>)	4/2012	3/2020 (Jun-22) {9/2022}	569.63 (N.A.) {708.73}	380.92	84
	ROAD TRANSPORT AND HIGHWAYS	1548	2 LANING FROM MANU-SIMLUNG PKG-2 (<i>NHIDCL</i>) (<i>N24001542</i>)	2/2022	1/2025 (N.A.) {1/2025}	456.88 (N.A.) {456.88}	95.50	39.12
		1549	IMPROVEMENT AND WIDENING TO 2- LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (<i>NHIDCL</i>) (<i>N24001914</i>)	5/2023	11/2024 (N.A.) {2/2025}	195.95 (N.A.) {195.95}	11.50	15.89
		1550	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (<i>NHIDCL</i>) (<i>N24002132</i>)	3/2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	0.23
		1551	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (<i>NHIDCL</i>) (<i>N24001263</i>)	6/2020	1/2022 (Feb-24) {9/2024}	277.50 (302.02) {302.02}	253.50	98.66
		1552	KAILASHAHAR TO KHOWAI PKG-4 (<i>NHIDCL</i>) (<i>N24001309</i>)	11/2020	6/2022 (Oct-23) {9/2024}	159.13 (171.50) {171.50}	79.43	98.05
		1553	2-LANING FROM JOLAIBARI - BELONIA (<i>NHIDCL</i>) (<i>N24001317</i>)	6/2020	1/2022 (Jul-24) {9/2024}	201.99 (287.47) {287.47}	144.07	92.3

Table:-7. Project List: Ongoing Projects as of 31st August 2024

UTTAR PRADESH		1554	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 (NHIDCL) (N24001318)	9/2020	4/2022 (Oct-22) {10/2023}	173.17 (N.A.) {173.17}	93.35	100
		1555	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3/2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2
	CIVIL AVIATION	1556	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6/2018	9/2021 (Oct-26) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,112.90	75.92
		1557	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3/2021	12/2022 (Sep-24) {9/2024}	242.14 (328.00) {358.00}	338.44	99.9
		1558	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5/2023	11/2024 (N.A.) {12/2024}	185.75 (232.52) {232.52}	62.78	40
		1559	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6/2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	0.00	
		1560	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7/2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	0.00	
	COAL	1561	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7/2016	11/2021 (Mar-25) {3/2025}	17,237.00 (19,406.12) {19,406.12}	18,026.99	84.31
		1562	KHADIA EXPANSION OCP (NCL) (N06000208)	6/2021	3/2025 (N.A.) {3/2026}	491.67 (N.A.) {491.67}	34.73	5.77

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>HOME AFFAIRS</u>	1563	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI (CPWD FOR MHA) (N45000003)	5/2019	1/2022 (Mar-23) {3/2023}	199.31 (N.A.) {199.31}	86.49	85
<u>PETROLEUM</u>	1564	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3/2019	4/2024 (Apr-24) {3/2025}	910.56 (1,299.02) {1,299.02}	769.40	89.5
	1565	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4/2022	4/2025 (Dec-26) {12/2026}	260.12 (N.A.) {260.12}	0.97	1.6
	1566	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9/2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	116.90	31.4
	1567	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12/2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	259.39	4.5
<u>POWER</u>	1568	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3/2019	9/2023 (N.A.) {3/2025}	11,089.42 (N.A.) {13,261.79}	10,965.67	92.5
	1569	KALPI SOLAR POWER PROJECT (NHPC) (N18000323)	7/2020	3/2022 (Mar-24) {3/2024}	314.64 (N.A.) {350.46}	311.97	91
	1570	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (BHEL) (N18000382)	3/2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	531.00	
<u>RAILWAYS</u>	1571	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (RVNL) (N22000401)	4/2015	3/2022 (N.A.) {12/2024}	943.60 (N.A.) {2,018.23}	1,779.61	98
	1572	RAMNA - SINGRAULI DOUBLING (ECR) (N22000417)	8/2015	3/2020 (N.A.) {9/2024}	2,436.21 (2,880.40) {2,880.40}	2,905.39	90

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1573	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419)	8/2015	3/2019 (N.A.) {8/2024}	528.57 (762.97) {762.97}	754.14	90
1574	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4/2016	(N.A.) {7/2025}	602.50 (N.A.) {714.96}	863.49	52
1575	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4/2016	12/2019 (N.A.) {12/2024}	1,177.96 (N.A.) {1,777.39}	1,732.31	76
1576	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3/2018	3/2023 (N.A.) {3/2026}	4,329.53 (N.A.) {4,329.53}	60.37	3
1577	JHANSI BINA DOUBLING (NCR) (N22000496)	9/2016	3/2021 (N.A.) {12/2023}	2,001.00 (2,001.00) {2,001.00}	1,118.80	85
1578	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6/2016	12/2023 (N.A.) {12/2024}	3,677.76 (N.A.) {5,190.26}	4,969.16	80
1579	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10/2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	
1580	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8/2019	12/2026 (N.A.) {12/2026}	2,390.00 (N.A.) {2,390.00}	0.00	0
1581	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4/2020	6/2026 (Jun-26) {6/2026}	1,456.89 (N.A.) {1,456.89}	0.00	5
1582	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3/2017	12/2024 (N.A.) {12/2024}	260.00 (N.A.) {260.00}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1583	ALIGARH-DAUD KHAN - 3RD LINE (6.9 KM) & CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4/2019	12/2025 (N.A.) {12/2025}	451.99 (N.A.) {451.99}	0.00	0
1584	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4/2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	0.00	0
1585	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (NCR) (N22000564)	4/2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.75	8
1586	SAHJANWA - DOHRIGHAT (NER) (N22000565)	8/2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	386.95	1
1587	BAHRAICH - NANPARA - NEPALGANJ (56.15 KM) (NER) (N22000566)	7/2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	20.10	18.28
1588	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (NER) (N22000569)	10/2018	10/2030 (N.A.) {3/2027}	1,600.00 (N.A.) {4,939.78}	734.74	5
1589	BARABANKI AKBARPUR DOUBLING (NR) (N22000578)	9/2017	3/2025 (N.A.) {3/2025}	1,200.00 (N.A.) {1,700.00}	0.00	0
1590	JAUNPUR AKBARPUR (TANDA) DOUBLING (NR) (N22000582)	8/2017	3/2025 (N.A.) {3/2025}	515.50 (N.A.) {676.00}	0.00	0
1591	JANGHAI PRATAPGARH AMETHI DOUBLING (NR) (N22000583)	11/2017	3/2025 (N.A.) {3/2025}	701.98 (N.A.) {1,100.00}	0.00	0
1592	BARABANKI-MALHAUR - 3RD & 4TH LINE (32.84 KM) (NR) (N22000590)	1/2019	3/2025 (N.A.) {3/2025}	323.85 (N.A.) {323.85}	0.00	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1593	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (NR) (N22000591)	3/2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.00	0
	1594	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (RVNL) (N22000596)	11/2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	312.07	48
	1595	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (RVNL) (N22000598)	5/2018	3/2024 (N.A.) {2/2025}	1,177.96 (N.A.) {2,529.46}	1,574.90	76
	1596	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8/2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	0
	1597	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11/2016	6/2024 (N.A.) {2/2025}	186.85 (N.A.) {457.68}	427.67	84
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1598	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7/2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	942.58	68
	1599	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT (MoRTH) (N24001423)	4/2021	9/2023 (N.A.) {3/2026}	309.48 (N.A.) {309.48}	112.84	51
	1600	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3/2021	9/2023 (N.A.) {12/2024}	185.09 (269.81) {269.81}	253.23	95
	1601	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4/2020	2/2024 (N.A.) {10/2024}	199.39 (212.96) {199.39}	142.04	88

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1602	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH-730C F (MoRTH) (N24001457)	4/2020	7/2024 (N.A.) {3/2025}	172.50 (169.56) {172.50}	86.30	59
1603	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4/2020	3/2024 (N.A.) {12/2024}	236.47 (N.A.) {236.47}	118.97	77
1604	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4/2020	7/2024 (N.A.) {12/2024}	211.09 (N.A.) {211.09}	97.06	75
1605	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 (MoRTH) (N24001463)	4/2020	7/2024 (N.A.) {2/2024}	294.84 (309.99) {294.84}	271.61	100
1606	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3/2021	8/2023 (N.A.) {1/2025}	264.86 (N.A.) {264.86}	106.25	67
1607	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11/2021	5/2024 (N.A.) {3/2025}	307.11 (N.A.) {307.11}	158.36	70
1608	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4/2020	11/2024 (N.A.) {11/2024}	325.24 (340.16) {325.24}	203.65	74
1609	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3/2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	210.26	54

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1610	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10/2021	4/2024 (N.A.) {12/2024}	227.06 (N.A.) {227.06}	98.32	83
1611	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR ? DEHRADUN SECTION FROM K (NHAI) (N24001523)	3/2021	10/2023 (Oct-24) {10/2024}	836.24 (N.A.) {836.24}	772.94	97.01
1612	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR ? DEHRADUN SECTION FROM (NHAI) (N24001524)	3/2021	10/2023 (Oct-24) {10/2024}	990.28 (N.A.) {990.28}	997.50	97.86
1613	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3/2020	9/2024 (N.A.) {12/2024}	262.37 (343.77) {343.77}	235.03	62
1614	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT-SHAMLI-MUZAFFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1/2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	77.15
1615	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3/2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	410.75	65.14
1616	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12/2021	7/2025 (N.A.) {7/2025}	1,138.81 (N.A.) {1,138.81}	226.92	82.83
1617	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT ? SHAMLI ? MUZAFFARNAGAR) AND NH-709A (KARN (NHAI) (N24001729)	8/2022	4/2024 (N.A.) {12/2024}	326.79 (N.A.) {329.79}	93.31	79

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1618	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12/2021	1/2025 (N.A.) {1/2025}	1,384.79 (N.A.) {1,384.79}	619.87	88.12
1619	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12/2021	5/2025 (May-25) {5/2025}	2,470.64 (N.A.) {2,335.00}	456.99	62.95
1620	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12/2021	10/2024 (N.A.) {10/2024}	540.97 (N.A.) {540.97}	126.98	60.85
1621	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.-MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3/2022	8/2024 (N.A.) {12/2024}	1,602.48 (N.A.) {1,602.48}	341.16	71.85
1622	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-LOHADDA TO VILL.-KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3/2022	8/2024 (N.A.) {12/2024}	1,335.45 (N.A.) {1,335.45}	335.55	61.65
1623	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KHYAWARI TO VILL.-LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3/2022	8/2024 (N.A.) {12/2024}	1,428.19 (N.A.) {1,428.19}	414.64	68.35
1624	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL.-KARAUNDA MAHAJAN TO VILL.-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1/2022	8/2024 (N.A.) {12/2024}	1,159.96 (N.A.) {1,159.96}	503.59	98
1625	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG-III (NHAI) (N24001737)	11/2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	97.1

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1626	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9/2021	10/2023 (Dec-24) {12/2024}	300.79 (N.A.) {300.79}	122.56	66.5
1627	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10/2019	11/2023 (Dec-24) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,028.00	96.89
1628	4L OF SHAMLI BYAPSS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5/2019	11/2022 (N.A.) {12/2024}	779.17 (N.A.) {779.17}	13.27	93
1629	KANPUR LUCKNOW EXPRESSWAY PKG- 1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12/2021	7/2025 (Jul-25) {7/2025}	1,972.10 (N.A.) {1,936.00}	431.50	53.74
1630	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3/2021	4/2024 (Jan-25) {1/2025}	364.47 (N.A.) {364.47}	123.68	63
1631	4 LANING OF NAJIBABAD BYPASS OF NH-119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2/2022	6/2024 (Nov-24) {11/2024}	570.98 (578.02) {578.02}	335.34	79
1632	SPUR OF MEERUT-GARH- MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1/2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	37.54
1633	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10/2019	3/2023 (Dec-24) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	98.1
1634	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8/2021	3/2024 (Dec-24) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	30

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1635	4L BYPASSES FOR JAGATPUR, B4BUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12/2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	51.2
1636	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2/2019	2/2022 (Dec-24) {12/2024}	927.77 (N.A.) {1,603.00}	1,202.77	79.45
1637	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6/2020	11/2023 (Dec-24) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	97
1638	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1/2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	741.63	59.23
1639	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHAI) (N24001852)	10/2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	614.24	82.07
1640	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHAI) (N24001853)	10/2021	9/2024 (N.A.) {9/2024}	772.05 (N.A.) {772.05}	541.27	65
1641	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1/2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	254.18	61
1642	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH- 87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHAI) (N24001992)	8/2022	2/2024 (Dec-24) {12/2024}	199.31 (199.38) {199.38}	123.86	63.5

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1643	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH-731B ON (MoRTH) (N24001996)	3/2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	324.61	28
1644	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10/2022	5/2025 (N.A.) {5/2025}	189.31 (N.A.) {189.31}	50.66	15
1645	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11/2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	54.79	14
1646	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH-31 TO NH-330 (MoRTH) (N24002016)	10/2022	6/2025 (N.A.) {6/2025}	225.17 (N.A.) {225.17}	80.68	32
1647	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3/2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	465.37	18
1648	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12/2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	337.81	5
1649	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1/2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	200.18	21
1650	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4/2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	774.19	33

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1651	GARHMUKTESHWAR (KM. 83.200 OF NH-24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10/2019	10/2023 (N.A.) {6/2024}	2,068.99 (2,171.00) {2,171.00}	209.60	47
1652	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11/2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	16.37
1653	CONSTRUCTION OF FOUR LANE HIGHWAY FORM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10/2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	688.34	33.28
1654	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10/2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	45.30	18
1655	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10/2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	474.79	23.5
1656	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10/2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	95.37	38.37
1657	CONSTRUCTION OF FOUR-LANE ?WESTERN SIDE SPUR OF RAMPUR- RUDRAPUR SECTION CONNECTING NH-24 TO NH-87 BY (NHAI) (N24002090)	3/2021	11/2024 (N.A.) {11/2024}	646.27 (N.A.) {646.27}	44.01	20.22
1658	IMPROVEMENT , UP-GRADATION OF NH-734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: ?PACKAGE-I: MORA (NHAI) (N24002093)	10/2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	169.15	23.6

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1659	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9/2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	295.00	15.13
1660	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12/2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	748.74	32.72
1661	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2/2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	506.17	21.17
1662	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 (NHAI) (N24002097)	2/2023	9/2025 (N.A.) {3/2025}	526.45 (N.A.) {526.45}	115.32	52.6
1663	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1/2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	196.44	11
1664	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8/2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	62.14	11.16
1665	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8/2023	3/2025 (N.A.) {3/2025}	993.77 (N.A.) {349.48}	117.99	32
1666	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3/2023	8/2025 (N.A.) {8/2025}	438.24 (362.39) {438.24}	169.21	12

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1667	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1/2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	44.98	19
1668	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 () (MoRTH) (N24002120)	2/2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	66.72	35
1669	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1/2022	9/2025 (N.A.) {9/2025}	509.65 (N.A.) {509.65}	130.57	12
1670	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ ? NICHLOUL ? TH) (MoRTH) (N24002134)	3/2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	151.41	
1671	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y) (MoRTH) (N24002138)	3/2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	205.24	4
1672	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12/2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	104.25	
1673	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12/2019	4/2022 (N.A.) {12/2024}	282.41 (N.A.) {319.96}	270.96	83
1674	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] (NHAI) (N24000551)	3/2016	4/2019 (Dec-24) {12/2024}	1,587.49 (3,473.59) {3,500.00}	3,341.70	95.56

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1675	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 (NHAI) (N24000556)	3/2016	4/2019 (Dec-24) {12/2024}	899.00 (1,623.88) {1,623.88}	1,105.28	92.1
	1676	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3/2016	7/2020 (Mar-25) {3/2025}	1,408.00 (1,659.12) {1,659.12}	1,199.58	79.87
	1677	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3/2018	12/2021 (Dec-23) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,198.22	99.26
	1678	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3/2018	11/2021 (N.A.) {12/2024}	2,140.93 (N.A.) {2,140.93}	2,062.18	97.94
	1679	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH ? 14 (NHAI) (N24001185)	11/2017	7/2021 (Dec-24) {12/2024}	2,159.00 (2,262.00) {2,262.00}	2,249.93	97.5
	1680	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHAI) (N24001306)	10/2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	84.92
<u>URBAN DEVELOPMENTS</u>	1681	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5/2019	3/2024 (N.A.) {6/2026}	11,076.48 (N.A.) {11,076.48}	7,434.03	66
	1682	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5/2019	3/2024 (N.A.) {12/2025}	8,379.62 (N.A.) {8,379.62}	3,873.50	43.9
<u>WATER RESOURCES</u>	1683	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UP JalNigam) (N30000006)	5/2017	9/2021 (N.A.) {6/2023}	767.59 (N.A.) {767.59}	276.97	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1684	FARRUKHABAD I AND D AND STP WORKS HAM (UPJalNigam) (N30000008)	10/2017	3/2022 (Feb-21) {8/2024}	213.62 (261.12) {261.12}	177.62	93
		1685	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UPJalNigam) (N30000010)	3/2018	9/2021 (N.A.) {7/2023}	967.23 (708.70) {967.23}	254.98	100
		1686	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UPJalNigam) (N30000013)	3/2019	8/2021 (N.A.) {7/2024}	271.39 (N.A.) {271.39}	182.26	100
		1687	MATHURA SEWERAGE SCHEME (UPJalNigam) (N30000019)	12/2017	12/2020 (Jun-18) {6/2022}	460.45 (N.A.) {460.45}	315.30	100
		1688	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1/2019	12/2021 (Jan-20) {9/2024}	231.79 (234.03) {234.03}	141.79	95
		1689	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UPJalNigam) (N30000022)	1/2019	10/2021 (N.A.) {7/2023}	206.05 (N.A.) {206.05}	139.23	100
		1690	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2/2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	
		1691	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UPJalNigam) (N30000025)	3/2019	7/2021 (May-20) {9/2024}	298.12 (N.A.) {240.93}	94.86	94
UTTARAKHAND	CIVIL AVIATION	1692	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7/2018	9/2020 (N.A.) {9/2024}	456.86 (N.A.) {500.00}	482.64	99.99

Table:-7. Project List: Ongoing Projects as of 31st August 2024

<u>POWER</u>	1693	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7/2006	2/2016 (Jun-22) {12/2024}	1,657.00 (4,825.60) {6,856.05}	6,847.67	97.4
	1694	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11/2006	3/2013 (N.A.) {4/2029}	2,978.48 (N.A.) {7,103.00}	6,298.38	75
	1695	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8/2008	6/2013 (N.A.) {6/2026}	2,491.58 (3,860.35) {6,303.00}	3,951.78	68.2
	1696	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7/2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	
<u>RAILWAYS</u>	1697	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4/2011	12/2024 (N.A.) {3/2025}	16,216.00 (N.A.) {24,659.00}	18,267.00	82.1
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1698	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR ? DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3/2021	3/2024 (Oct-24) {10/2024}	169.08 (N.A.) {169.08}	93.67	98.87
	1699	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8/2021	10/2024 (Oct-24) {10/2024}	1,377.79 (1,384.11) {1,377.79}	679.10	46.81
	1700	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3/2022	2/2025 (Feb-25) {2/2025}	1,092.90 (1,092.90) {1,092.90}	461.82	52.89
	1701	4L POANTA SAHEB?MEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6/2022	5/2025 (May-25) {5/2025}	524.54 (683.26) {683.26}	74.84	43.28

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1702	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5/2022	9/2024 (Mar-25) {3/2025}	314.31 (N.A.) {314.31}	134.15	51.75
1703	4L OF DUDHADHARI ELEVATED FLYOVER (MUZAFFARNAGAR ?HARIDWAR SECTION) FROM KM 356.450 TO KM 353.800 OF (NHAI) (N24001995)	5/2021	11/2023 (Dec-24) {12/2024}	154.52 (N.A.) {154.52}	150.26	98.43
1704	4-LANING OF KASHIPUR-SITARGANJ SECTION (MEGA) (N24000465)	11/2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	0
1705	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHAI) (N24000559)	3/2016	10/2019 (Oct-24) {10/2024}	720.00 (1,150.00) {1,150.00}	639.87	94
1706	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3/2018	11/2020 (Dec-22) {8/2024}	274.31 (N.A.) {274.31}	251.61	99
1707	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3/2018	11/2020 (Dec-22) {9/2024}	403.36 (N.A.) {403.36}	337.72	95.91
1708	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3/2018	11/2020 (Dec-22) {9/2024}	417.24 (N.A.) {417.24}	344.20	98.72
1709	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12/2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1710	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12/2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100
1711	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12/2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100
1712	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6/2017	6/2019 (Mar-23) {3/2023}	282.08 (N.A.) {282.08}	234.97	100
1713	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11/2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100
1714	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11/2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100
1715	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11/2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100
1716	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2/2018	2/2020 (Mar-23) {3/2023}	418.88 (N.A.) {418.88}	339.71	94
1717	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2/2018	(Apr-23) {4/2023}	293.68 (N.A.) {293.68}	244.25	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1718	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5/2018	5/2020 (Dec-23) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56
		1719	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3/2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	
		1720	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3/2018	7/2022 (Jul-22) {1/2026}	1,383.78 (N.A.) {1,383.78}	591.11	61.1
		1721	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8/2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100
	<u>WATER RESOURCES</u>	1722	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UKJalNigam) (N30000004)	3/2017	11/2019 (N.A.) {2/2022}	158.00 (N.A.) {158.00}	104.53	100
<u>WEST BENGAL</u>	<u>CIVIL AVIATION</u>	1723	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB I AIRPORT KOLKATA (AAI) (N04000080)	1/2016	3/2020 (Jun-22) {12/2023}	458.00 (N.A.) {458.00}	246.64	100
		1724	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1/2019	11/2021 (N.A.) {5/2023}	389.71 (N.A.) {392.00}	393.60	100
		1725	NSCB I AIRPORT KOLKATA: RE-CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4/2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	41.06	20
	<u>COAL</u>	1726	RANIGANJ MASTER PLAN (ECL) (N06000163)	8/2009	8/2019 (N.A.) {8/2019}	2,661.73 (N.A.) {5,146.48}	752.42	40

Table:-7. Project List: Ongoing Projects as of 31st August 2024

1727	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5/2018	3/2026 (N.A.) {3/2026}	535.18 (N.A.) {535.17}	3.91	13.2
1728	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8/2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	57.88	25.3
1729	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4/2020	3/2025 (Mar-26) {3/2026}	483.65 (N.A.) {483.65}	28.95	12
1730	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12/2015	3/2017 (N.A.) {9/2024}	341.22 (341.22) {341.22}	308.53	94
1731	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7/2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	500.14	17
1732	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4/2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	390.67	35
1733	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11/2020	3/2025 (Mar-26) {3/2026}	888.99 (N.A.) {888.99}	89.80	30
1734	BONJEMEhari EXPANSION OCP (ECL) (N06000244)	8/2021	3/2025 (Mar-26) {3/2026}	570.12 (N.A.) {570.11}	47.30	16
1735	ITAPARA OC (ECL) (N06000272)	12/2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	42.39	5
1736	UCE OF TILABONI UG (ECL) (N06000276)	1/2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	39.53	0

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1737	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1/2023	3/2029 (N.A.) {3/2029}	389.10 (N.A.) {389.10}	106.52	0
<u>DEPARTMENT OF HIGHER EDUCATION</u>	1738	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3/2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	185.75	99
<u>HOME AFFAIRS</u>	1739	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10/2014	4/2018 (N.A.) {12/2024}	162.88 (210.83) {210.83}	185.40	87
<u>MINES</u>	1740	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA (CPWD) (N10000015)	4/2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	50.51	23
<u>PETROLEUM</u>	1741	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3/2017	12/2020 (Mar-25) {3/2025}	1,740.00 (2,433.15) {2,433.15}	1,944.40	86.6
	1742	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3/2019	3/2031 (Mar-29) {3/2029}	5,830.20 (N.A.) {5,830.20}	714.57	22.2
	1743	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11/2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	246.37	54.18
	1744	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3/2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	65.35	1.1
	1745	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6/2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	147.39	16.6

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1746	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12/2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	68.44	16.9
POWER	1747	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9/2014	9/2019 (N.A.) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,042.24	45.1
	1748	DURGAPUR PP-III (2X20 MW) - NSPCL (NTPC) (N18000277)	12/2016	11/2018 (Mar-24) {3/2024}	529.68 (633.80) {679.00}	558.39	89
RAILWAYS	1749	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4/2000	3/2019 (Mar-25) {3/2025}	1,188.91 (N.A.) {1,619.51}	1,079.40	75
	1750	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4/2010	3/2016 (N.A.) {3/2016}	2,397.72 (N.A.) {2,397.72}	197.20	17
	1751	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4/2010	3/2014 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.84	33
	1752	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4/2010	3/2016 (N.A.) {3/2026}	3,951.98 (N.A.) {8,964.35}	6,817.20	73
	1753	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4/2010	3/2016 (N.A.) {12/2026}	2,913.51 (N.A.) {4,834.54}	3,869.56	95.41
	1754	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE (MRTP) (N22000135)	3/2013	3/2016 (Dec-23) {12/2023}	4,874.58 (8,574.98) {10,442.41}	8,008.94	96.2

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1755	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4/2018	6/2022 (N.A.) {12/2024}	338.00 (N.A.) {393.83}	176.50	60
	1756	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7/2015	3/2025 (Mar-26) {3/2026}	283.54 (N.A.) {283.54}	158.56	44
	1757	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2/2009	9/2016 (N.A.) {6/2024}	4,874.58 (8,575.00) {10,442.41}	0.00	0
<u>ROAD TRANSPORT AND HIGHWAYS</u>	1758	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3/2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	1,905.34	73.64
	1759	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3/2021	9/2024 (N.A.) {6/2025}	2,200.93 (N.A.) {2,430.39}	2,430.39	87.77
	1760	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHAI) (N24001749)	8/2021	8/2023 (N.A.) {11/2024}	557.55 (N.A.) {557.55}	465.08	90.22
	1761	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHAI) (N24001750)	8/2018	12/2021 (N.A.) {2/2025}	622.04 (N.A.) {622.04}	471.13	79.37
	1762	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 (NHAI) (N24001752)	12/2018	2/2023 (Aug-23) {9/2024}	2,375.87 (2,843.79) {2,843.79}	2,371.78	100
	1763	DEVELOPMENT TO 4/6-LANNING OF NH- 31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3/2022	9/2025 (Sep-25) {9/2025}	995.04 (995.04) {995.04}	220.45	31.23

Table:-7. Project List: Ongoing Projects as of 31st August 2024

	1764	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12/2015	6/2018 (May-24) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100
	1765	SIX-LANING OF BARWA ADDA-PANAGARH (NHAI) (N24000515)	4/2014	9/2016 (N.A.) {11/2024}	1,665.00 (N.A.) {4,905.99}	4,905.99	92.9
	1766	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3/2018	9/2022 (Dec-22) {3/2025}	841.57 (708.30) {708.30}	5,802.45	92.09
	1767	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3/2016	11/2018 (Dec-23) {10/2024}	271.17 (291.20) {291.20}	178.40	76.39
	1768	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2/2018	9/2020 (Jan-24) {9/2024}	426.18 (426.18) {426.18}	364.92	89.89
	1769	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND (MoRTH) (N24000885)	3/2016	9/2023 (Mar-24) {7/2024}	160.27 (213.97) {213.97}	144.31	100
	1770	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N (MoRTH) (N24000887)	6/2016	9/2021 (Feb-24) {9/2024}	236.78 (263.26) {263.26}	222.11	99.57
STEEL	1771	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11/2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	42.14	22

Table:-7. Project List: Ongoing Projects as of 31st August 2024

WATER RESOURCES	1772	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS (KMDA) (N30000029)	1/2019	4/2022 (Feb-19) {12/2024}	384.96 (N.A.) {384.96}	0.00	
	1773	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL (KMDA) (N30000030)	3/2019	4/2022 (N.A.) {12/2024}	287.53 (N.A.) {287.53}	0.00	
	1774	I AND D AND STP WORKS AT BURDWAN WEST BENGAL (KMDA) (N30000031)	12/2018	4/2022 (N.A.) {12/2024}	234.31 (N.A.) {234.31}	0.00	
	1775	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5/2018	2/2022 (N.A.) {3/2025}	198.43 (224.69) {224.69}	75.76	77
	1776	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS (KMDA) (N30000033)	3/2018	6/2022 (N.A.) {3/2024}	165.16 (N.A.) {165.16}	0.00	
	1777	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8/2017	9/2022 (Jan-23) {12/2026}	307.12 (N.A.) {653.67}	0.00	
	1778	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH (KMDA) (N30000042)	5/2018	2/2022 (Sep-20) {10/2024}	160.00 (154.73) {154.73}	84.27	88
	1779	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045)	8/2017	12/2021 (Feb-21) {2/2024}	185.22 (N.A.) {185.22}	49.99	100
	1780	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046)	2/2014	12/2019 (N.A.) {6/2022}	274.76 (N.A.) {332.56}	276.80	100

Table:-7. Project List: Ongoing Projects as of 31st August 2024

		1781	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047)	12/2014	4/2020 (N.A.) {6/2022}	272.32 (341.68) {272.32}	306.80	100
		1782	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048)	1/2018	12/2021 (Feb-21) {2/2024}	172.10 (N.A.) {172.10}	47.20	100
		1783	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049)	10/2017	12/2021 (Feb-21) {2/2024}	164.93 (N.A.) {164.93}	45.45	100
			Total			2,738,539.25 (-) {3,304,696.35}	1,733,448.44	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	MITES
MITES OF HIGHER EDUCATION	MITES OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
